


CONSTRUCTION ENVIRONMENTAL MANAGEMENT PLAN

Thornwood Gardens – Thurnscoe Bridge Lane-Thurnscoe

Ref: AVH/4211thurnscoe/CEMP – 14/8/26

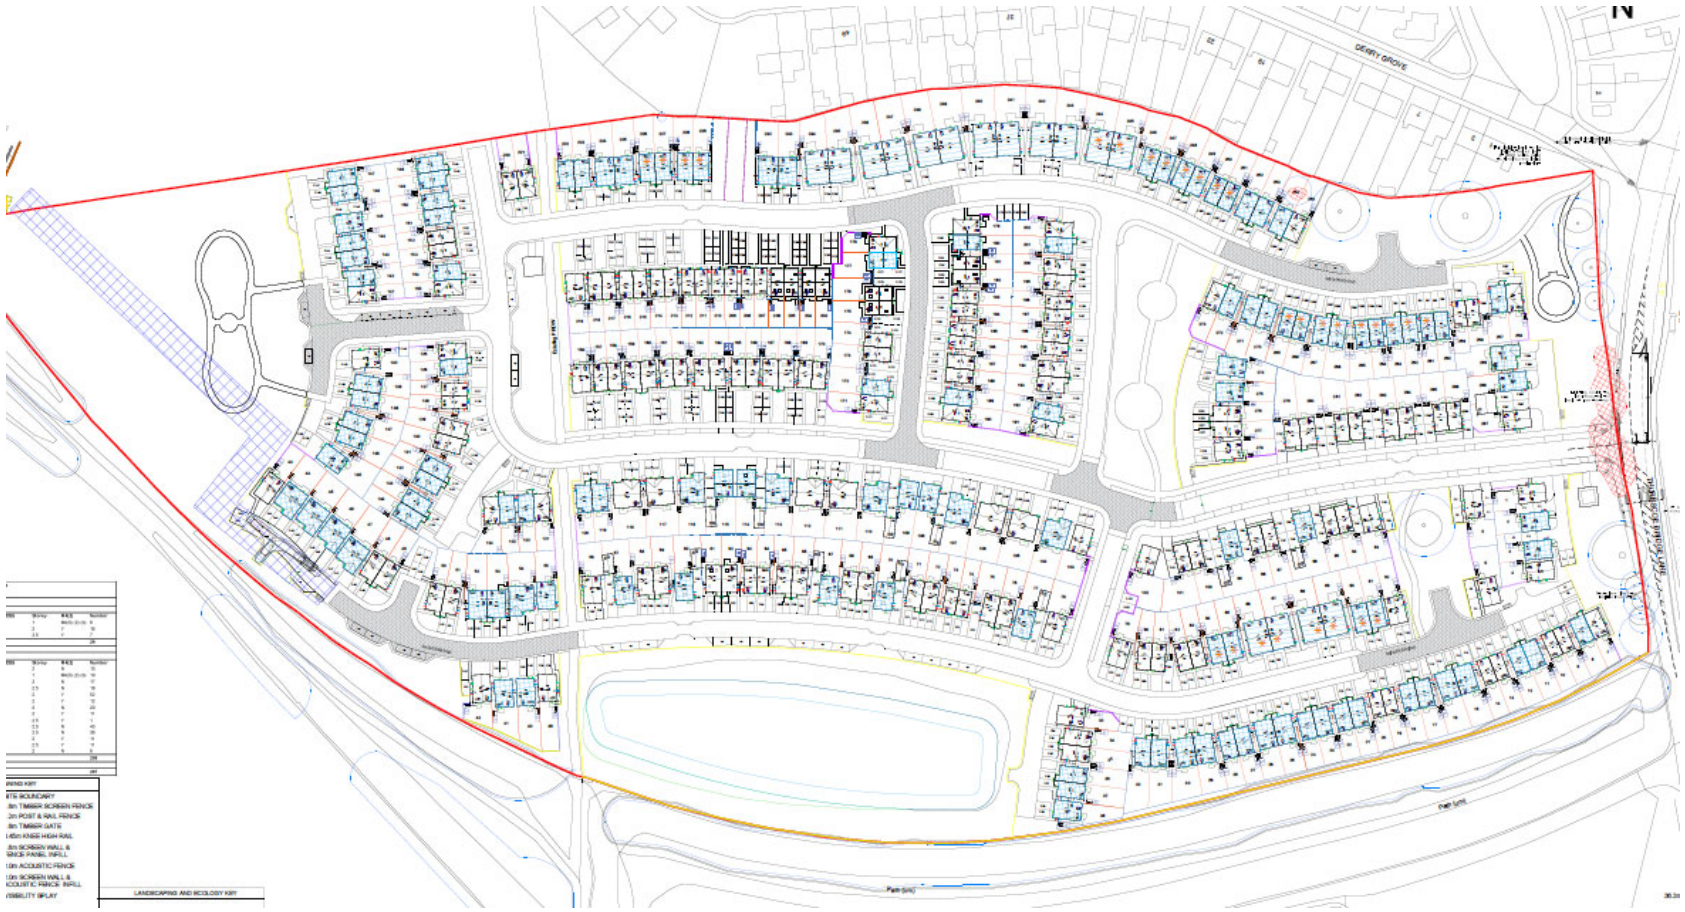

INTRODUCTION


This document has been prepared to enable construction activities in accordance with the planning permission **2024/1004/FUL** associated with the development Thurnscoe Bridge Lane, Thurnscoe, S630TX

The purpose of the CEMP as described in the British Standard 5228: 2009 "refers to the need for the protection against noise and vibration of persons living and working in the vicinity of, and those working on, construction and open sites. It recommends procedures for noise and vibration control in respect of construction operations and aims to assist architects, contractors and site operatives, designers, developers, engineers, local authority environmental health officers and planners."

CONSTRUCTION MANAGEMENT PLAN

1. Site Location

The site is located off Thurnscoe Bridge Lane adjacent Derry Grove and Thurnscoe Rifle Club.
The site is currently used as an agricultural field with no known historic uses other than agriculture.
The site is approximately 5 miles from the A1(M) and half a mile from the A635.

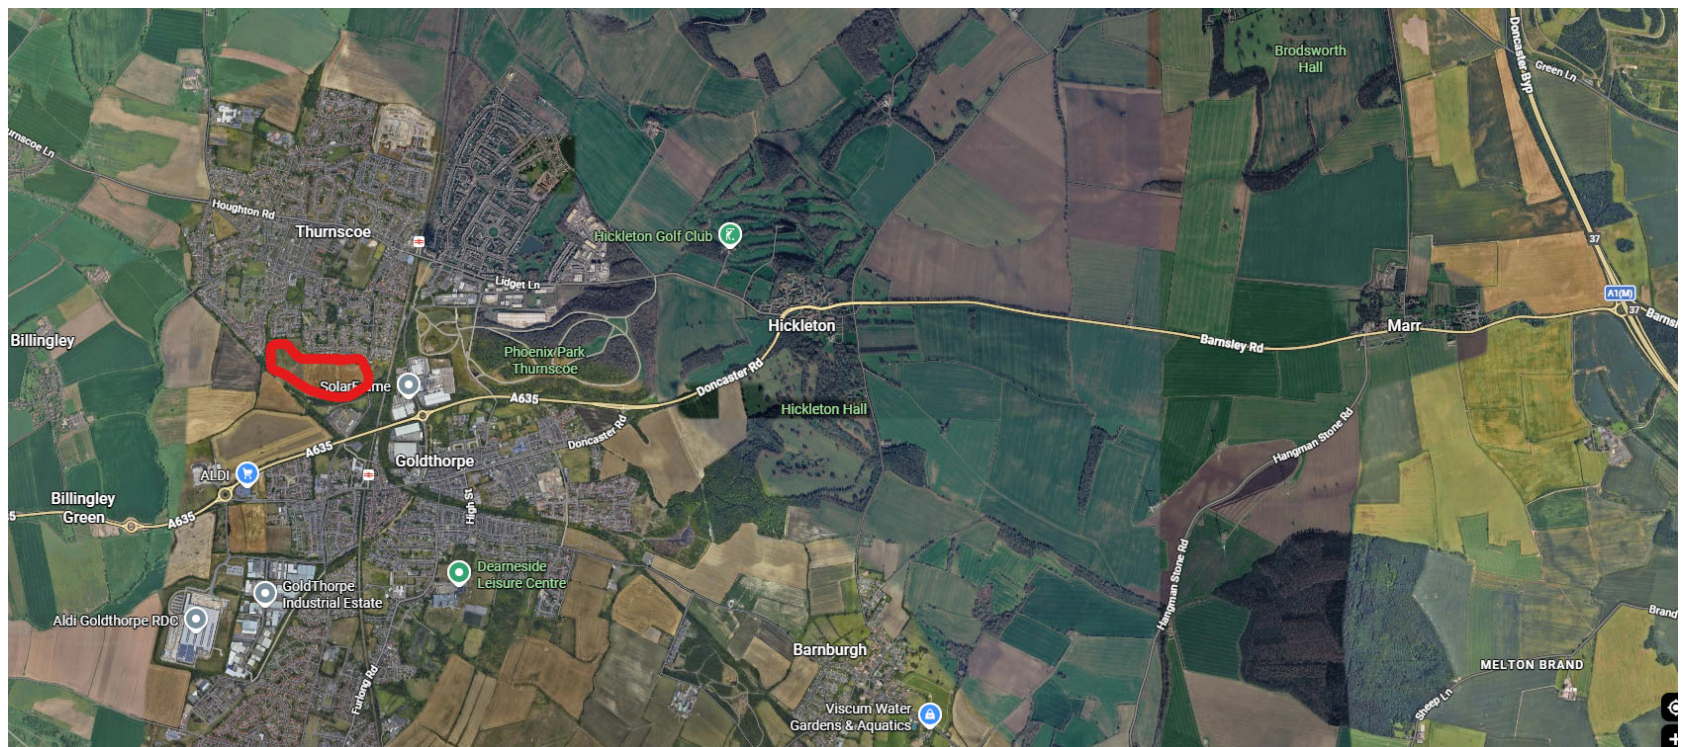

2. Site Management

Contact details for the site management team will be posted on the gate of the site office and entrance to the site compound. An F10 will be submitted prior to commencement on site, which will contain the contact details below which will be updated as available for the project.

During work hours the site team will be contactable directly by telephone and email. Out of hours, a voicemail message will provide emergency contact details.

Site Contact Details:

Site Manager	TBC		
Contracts Manager	TBC		
Construction Director	Joe Ramsbottom	01924 939912	joe.ramsbottom@avanthomes.co.uk@avanthomes.co.uk
Health & Safety Manager	Ian Hunter	07779 869305	ian.hunter@avanthomes.co.uk
Planner	Jenny Nicholson	01924 248442	jenny.nicholson@avanthomes.co.uk
Technical Director	Gareth Uttley	07967 841972	gareth.uttley@avanthomes.co.uk

3. Restriction of Vehicular Traffic

The site is within easy access from the A1(M) and the A635, The route to the A1(M) which would go through Thurnscoe and Hickleton village is already an established and very frequently used HGV and bus route being used by traffic from Goldthorpe and Thurnscoe Business park. Access to the site can also be taken using the A635. All routes to and from the site are currently used by both public transport and HGV lorry of varying sizes.

All other Oversized loads will be infrequent. However, if an oversized load is required, a site survey to assess the best means of delivery will be undertaken. This will consider:

- Width of access road
- Condition of road way
- Possible pinch points
- Flow of traffic
- Volume of traffic
- Duration of passage

Oversized loads that fall into the abnormal load category must be pre-approved via the Electronic Service Delivery for Abnormal Loads (ESDAL) system.

Tracking has been reviewed to ensure that all vehicles we will have operating on site will be able to manoeuvre comfortably in the space provided.

A comprehensive review of access to ensure that site material can be delivered and be dropped off without damaging the existing infrastructure will be undertaken prior to commencement of construction works on site. If in the unlikely event that damage occurs to the roadway, reinstatement work will take place in accordance with the requirements of the Highway Authority and Barnsley Council

All loads delivered to site will be within the loading capacity of the roads.

All site traffic will be directed to the construction site access using directional signage. All signage will be reviewed throughout the construction phase and adjustments made as necessary and further agreed as appropriate. Directional signage to site will not be permitted from the strategic road network (SRN).

Suppliers and sub-contractors will be notified in advance of the desired location for delivery. Direction and access point maps with site delivery rules and times will be sent out to suppliers and sub-contractors.

All gates on site open inwards and will not impede the public highway or footpaths at any time.

During Mobilisation stage there will be HGV articulated wagons infrequently to deliver machinery and larger drainage material.

During the Construction phase the average vehicle movements will be estimated at the below in addition to operatives vehicles:

- 10 rigid 32 ton wagons (concrete or stone or tarmac)
- 5 rigid Hiab wagon delivering materials
- 5 articulated flat back truck with material
- Diesel delivery 1-2 visit per week
- 1-2 delivery of small tools on Pick ups

4. Protection of Buried Services

Any existing buried services will be located and marked then

5. Waste, Recycling and Contaminated Materials

The developer will establish a dedicated Waste Management Contractor team who will be tasked with the removal of all waste from site.

The developer will implement a re-cycling regime for materials and packaging. The Waste Management Contractor will compile a report quantifying the materials recovered.

It is planned that site waste will be reduced through segregation and recycling. As per Avant Homes Environmental Policy Statement and Environmental Management Policy and Guidelines.

The developer will segregate the following materials in the material recovery programme:

- Timber
- Plastics
- Metal
- Plasterboard
- Pallets and cable drums

All contractors working on site will be supplied with refuse bins by the waste management team. Once the bins are filled, the waste management team will consolidate the waste and remove from site.

The consolidated waste will be collected from the site by a licensed waste carrier.

Waste certificates will be collated for all waste deposited at Environmentally Controlled Waste Reception Centres.

Any hazardous waste that is removed from site will be monitored to record compliance with the Site Waste Management Plan. Records will be gathered about the waste generated on site including:

- Volume - Quantity to landfill/recycled.
- Type
- Cost

6. Public Footpaths/Highways

Where works are to be undertaken outside the boundary of the site, measures will be put in place to ensure public footpaths remain open or are subject to clear and safe diversions in accordance with the requirements of the local authority.

No property on site will be occupied until a clear and safe access has been provided from the home to the site boundary.

7. Welfare

The developer will construct a welfare which shall provide sanitary convenience for both male and female workers. There will be a canteen to cater for workers and changing/drying rooms.

The maintenance of the workers canteen, toilets and changing rooms will be maintained to high standard to ensure the hygiene of the facilities.

8. Logistics

All vehicle movements will be controlled by the site construction team who shall co-ordinate all construction traffic to and from site and in accordance with the Avant Homes Traffic Management Policy Guidelines.

All vehicles will be parked on site in holding areas set aside from the construction works. The compound location are included on the site enabling plan.

9. Controlling Sediment Runoff

From the onset of works, all contractors will be required to use all possible means to ensure that the least amount of debris are carried out onto the external carriageway.

When the construction of dwellings commences the site roads will be brought up to binder course. Delivery vehicles will not leave hard standing areas. The site roads will be regularly cleaned using a mechanical road sweep attachment. In addition, a mechanical road sweeper will be hired and used if the requirement is there.

Road sweeping activity will be kept to a minimum and only used in exceptional circumstances. Road sweeping to be continually monitored through active and ongoing dialogue with North Lincolnshire Highways Department.

The site management team and contractors are to undertake routine inspections throughout each working day to confirm no mud or sediment on the site roads. Should internal roads become contaminated Avant Homes will immediately instruct road sweepers to cleanse the internal roads.

Should there be a risk to the public highway, Avant Homes will inform Barnsley Council with a view to instructing them to undertake a cleanse of the adjacent public highway network. No road sweeper employed by Avant Homes will be allowed to work on the public highway at any time unless an emergency situation arises and after contacting [Barnsley Council](#).

All vehicle movements will cease if mud on the roads cannot be controlled with measures/mitigation put in place as above.

A Surface Water Management Plan has been prepared. Contractors must ensure they adhere with the full requirements and recommendations in this document.

In Accordance with Part H of the building regulations all road and yard gullies will contain a Gully guard or similar silt trap to prevent solids and grits entering the surface water drainage system.

10. Site access during works period

The proposed development is to be accessed initially via an existing farm entrance into the field which will act as a temporary construction access until the permanent site access is constructed.

Site access is controlled by Avant Homes and is both deliverable and achievable.

Operatives will only be permitted to access the site working areas after receiving an induction.

Site notice boards will be displayed at the site entrance and will display the project particulars, contact details, access and egress procedure, site rules and all necessary health and safety information.

11. Noise and Vibration

The developer will adhere to the key legislation on noise and vibration as detailed in the:

1. Control of Pollution Act 1974
2. Environmental Protection Act 1990 (ss79-82)
3. BS 5228: 2009, Code of Practice on Construction and Open Site.

Site operations will be controlled so that all plant and machinery noise emissions (including the provision of ventilation, heating and cooling) shall be designed, installed and operated at noise levels that do not cause noise nuisance to the nearest adjoining residential properties.

The developer shall ensure that disruptive sound levels will be kept to a minimum.

A variety of measures will be used to effect the reduction of noise transmitted from site, this will include:

- Co-ordinated delivery times and efficient traffic management to prevent queues of traffic accessing the site.
 - Ensuring all plant has sound reduction measures (mufflers, baffles or silencers).
 - Utilising construction techniques that minimise the production of noise.
 - Strict adherence to the site working hours.
 - Using acoustic hoarding where necessary.
 - Positioning plant away from properties
 - Machines in use will be throttled down to a minimum
 - Cutting operations will be kept off site as much as possible by pre-fabrication.
 - Localised shrouding of plant in accordance with BS5228-2:2009
 - Use of mains electrical power wherever possible with the use of generators kept to a minimum
 - Where practicable, works will be carried out to ensure that the ground vibrations are contained within the target limits set out below. Any works expected to exceed these limits will be discussed and agreed with the Environmental Control office of North Lincolnshire Council.
 - Any reversing warnings that are necessary should be of the white noise type, subject to H&S considerations.
- A peak particle velocity of 1mm/s at any occupied residential property
 - Peak particle velocity of 3mm/s at any other property in any orthogonal direction

12. Air Quality and Dust Management Plan

The developer will adhere to the key legislation on noise and vibration as detailed in the:

1. BRE (2003a): Guidance on the Control of Dust from Construction and Demolition Activities
2. BRE (2003b): Controlling Particulates, Vapours and Noise Pollution from Construction Sites
3. Greater London Councils (2014): The control of dust and emissions from construction and demolition: Supplementary Planning Guidance

All care will be taken not to cause the primary environmental nuisances of noise and dust pollution. Below are some actions that will be carried out to abate these problems:

- Ensure that all materials transported to and from site are in enclosed containers or fully sheeted.
- An MMP will be prepared for the site prior to import of any material and all donor sites are identified.
- Ensure stockpiles of topsoil etc are kept below hoarding heights and kept damp in dry windy conditions.
- During dry periods the works are to be damped down to control the generation of dust.
- Ensuring materials have a minimum of packaging.
- Ensuring all polystyrene and similar lightweight materials are weighted down.
- Making sure all dust generating materials are adequately packaged.
- Ensuring all vehicles leaving the site have loads covered where spoil or demolition material is being removed.
- Provide regular road cleaning using road sweepers or brushes to control dust and must.
- Keeping the loading drop heights of spoil into trucks as low as possible.
- Implementing an effective procedure to deal with complaints from third parties to ensure issues are dealt with efficiently and quickly.
- Ensuring all contaminants kept on site are safely stored with the necessary procedures put in place for leaks and spillages etc.
- Use of mains electrical power wherever possible with the use of generators kept to a minimum.
- A waste management system will be implemented on site.
- Use of suitable hard bonded surface to temporary haul roads such as tarmacadam to keep dust levels to a minimum during dry periods.
- The burning of rubbish or surplus materials on site will be strictly prohibited.
- The developer should provide hard surfacing and effectively dust suppressed haul routes to prevent machines/vehicles tracking over loose ground and appropriate speed limit around site to prevent re-suspension of dust on roads from vehicle movements. Effective cleaning of hardstanding and bowing of haul roads shall take place when necessary.

13. Emergency Services Routes and Access by Third Parties

Access for emergency services on site will be via the site access routes and emergency escape routes. Local emergency services will be notified of the access points before work starts on site and in due time before access arrangements are relocated.

14. Police Requirements

Appropriate signage is to be installed and made a requirement of all order/deliveries to the site.

15. Site Security

Fire escape routes, fire fighting stations, alarm points, muster points and practice drills within the works will be in accordance with standard Health and Safety Procedures and agreed with local fire officer.

Site management will be responsible for seeing that all plant and materials are stored safely and securely after the workday ends.

16. Protection of Third Parties

Wherever possible, all site activities will be contained within the site boundary and a comprehensive traffic management plan will be implemented to ensure no disruption is caused to traffic or pedestrians on the adjoining roads or walkways. Specific loading and unloading areas will be designated inside the site boundary.

17. Notifications

During the mobilisation period communications will be set up with the following authorities:

- Notice will be served to the Health and Safety Executive
- Meeting with Building Control and Planning Authorities
- Meeting with local Environmental Health Officer
- Meeting with local Police and Fire Brigade
- Liaison with local residents
- Notification to the emergency services giving full details of the construction works.
- Highways Authority

18. On Site Storage

"Just in time" deliveries will reduce the volume of on-site storage requirements.

Secure storage of materials, plant, chemicals and gasses will be controlled in accordance with the developers Health and Safety Procedures and Environmental Policy.

Any liquid storage tanks should be located within a bund with a capacity of not less than 110% of the largest tank or largest combined volume of connected tanks.

19. Craneage and Hoists

The majority of unloading and distribution will be by tele-handler.

Craneage will be provided with mobile cranes suitably sized for the required works. All lifting works will be subject to the production of a Lifting Plan. Cranes will at no time be permitted to over sail the public highway, footpaths or neighbouring properties.

20. Induction/Site Rules/Consultation

Every worker who enters the site will receive a specific site induction before they are allowed to leave the compound and commence work on site.

Inductions will provide an introduction to the project, a description of the project risks and a review of the individual's competency. Site access will be only permitted following site induction from the site management personnel.

Induction talks for operatives new to the site will include site rules which cover among other things:

- Behaviour toward others on site and nearby
- Drugs and alcohol
- Smoking areas
- PPE and safety issues
- Welfare facilities and use of
- Security issues
- Emergency procedures
- Good and bad practice

Regular 'toolbox talks' will be undertaken by the Principal Contractor outlining a variety of relevant Health and Safety issues.

21. Health and Safety

The developer will treat safety as a highest priority and will develop a successful programme of initiatives in order to improve Health and Safety awareness and performance on the project. These will work by actively encouraging operatives to think in a manner that assesses personal safety and the safety of others. The layout of the site accommodation will ensure that all staff, visitors and operatives will have the ability to store and retrieve the correct PPE before entering the construction area.

22. First Aid

The site management will be qualified First Aiders and the site will have first aid attendance at all times.

23. Construction Activities

The construction of the development will be managed and carried out in accordance with detailed method statements, risk assessments and Construction Phase Plan approved by the site management team.

Good Practice Guide:

The construction phase groundworker and road and sewer contractor should follow good environmental practice to minimize the risks of spillage, leakage etc. with reference, but not limited, to the following documents:

- CIRIA C502 'Environmental Good Practice on Site'
- EA Pollution Prevention Guidelines:
 - PPG6 - Working at construction and demolition sites.
 - PPG2 - Above ground oil storage tank
 - PPG7 – The safe operation of refueling facilities.
 - PPG21 – Incident Response Planning
- Yorkshire Water Services. 'Guideline for developers to Yorkshire Water requirements. New sewerage infrastructure in Ground Water Source Protection Zones'

24. Measures to protect nesting birds habitats (including any vegetation removal)

The developer proposes that any vegetation or site clearance will be undertaken outside of the nesting bird season (March to August inclusive) where possible and if otherwise will be carried out such works should be supervised by a suitably qualified ecologist who will advise and supervise all site personnel of the potential presence of nesting birds and their legal protection.

Procedure

Each area will be observed for at least 30 minutes and note taken of whether any birds are nesting or preparing to nest (e.g. carrying nest building materials and/or food for the young). The observations will take place from a reasonable distance from the proposed working area, to avoid disturbance to any possible nesting birds, and it may be necessary to observe the area from more than one vantage point.

Birds incubating eggs are extremely illusive and therefore a more detailed search of the area may be necessary and care must be taken not to disturb nesting birds present. Searches for possible nest sites may be conducted using angled mirrors or similar to avoid flushing birds off hidden nests. If no signs of nesting birds are observed then works may commence. The site will be constantly monitored during the working period and if at any time nesting birds are observed, works, which may disturb them, must cease immediately and any active nests identified will be protected until the young have fledged. The ecologist will provide guidance on the required 'no-works' zone around the nest depending on the species of bird.

25. Working Hours

Construction or remediation work comprising the use of plant, machinery or equipment, or deliveries of materials shall only take place between the hours of

Monday to Friday - 0730 hours to 1800 hours
Saturday - 0830 hours to 1400 hours

Sunday and Public Holidays - No works (without formal agreement with the LPA).

All deliveries should avoid peak times where possible.

Working hours to be fully reviewed against planning conditions.

26. Surface Water and Foul Water discharge

The Surface water and foul sewer network are designed in accordance with national standards and will be offered for adoption under a section 104 agreement. The surface water system includes a large attenuation basin which will be constructed as part of the first phase of works so it can be utilised for the site as part of the Surface water management plan.

The surface water discharges to a local watercourse from the attenuation basin via a length of underground pipe, enabling the surface water management for treatment to be placed within the attenuation basin for easier visibility, operation and maintenance.

27. Complaints Procedure

In addition to the above the site will operate a complaints procedure in the event of any complaint from a member of the public about dust or mud

1. All sensitive properties located within 100m of the site boundary will be contacted before commencement of the site development.
2. A single point of contact and telephone number will be provided to each property.
3. Details on the hours of operation and timescale for development works will be provided.
4. Any complaint received will be dealt with by the site manager on the day on which it is received.
5. The complainant will be contacted to find out the nature of the complaint and a visit carried out, if needed.
6. Additional monitoring (noise, dust or vibration) will be carried out.
7. If remedial steps are required they will be carried out as soon as practicable and the complainant advised of what will be done.
8. Once any works have been completed the complainant will be contacted to see if the problem has been resolved.
9. A log book of complaints and remedial actions taken will be kept on site.

NOISE AND DUST ON CONSTRUCTION SITES

CODE OF PRACTICE FOR CONTRACTORS

1. The contractor must ensure compliance with current legislation on noise and dust control and in particular the Environmental Protection Act 1990 and the Control of Pollution Act 1974. The relevant Codes of Practice which set out procedures for dealing with the control of noise on construction and demolition sites are contained in BS5228: 2009 "Noise And Vibration Control On Construction And Open Sites" together with the specific requirements described below.
2. The contractor shall employ "best practicable means" to minimize noise vibration and dust from within the site, compound area and roadways. In particular the contractor shall: -
 - a. Consider at an early stage the most appropriate siting of the plant and compound areas relative to noise sensitive properties such as occupied residential dwellings, hospitals, hotels, shops, schools or offices.
 - b. Select the quietest available plant to ensure that "site noise" (as defined in BS5228 Part 1) is kept to a minimum.
 - c. Ensure that all plant and equipment is maintained to eliminate unnecessary noise.
 - d. Make full use of suppressers, silencers and other mechanical means of reducing noise where these are commercially available.
 - e. Ensure that plant, which is used intermittently, is shut down, or throttled back, during periods of non-use.
3. Where operations require the use of compressors, breakers, pumps, generators, mobile crushers and other similar plant, the following conditions shall apply: -
 - a. Compressors shall be silenced by all effective means and covers shall remain closed except when access is required.
 - b. Breakers shall be fitted with mufflers and, where commercially available, damped tools and accessories shall be used.
 - c. Any operations involving the use of compressors or breakers shall be acoustically screened.
 - d. Pumps and generators shall be acoustically screened and sited so as not to cause a nuisance to a noise sensitive building.
 - e. Any proposed blasting or piling shall be discussed with the Environmental Health Officer prior to commencement.
 - f. Mobile crushers must be permitted under the Pollution, Prevention and Control Regime and due notification must be given of their movement into the area.
 - g. Adequate water supply for dust suppression shall be provided when crushers are in use.
4. The hours for construction involving noisy activities shall be 0800 to 1800 hours Monday to Friday and 0900 to 1400 on Saturdays and at no time on Sunday or Bank Holidays unless otherwise agreed with the Environmental Health Officer.
5. Where operations require the use of temporary traffic signals the electric power shall be directly from the Distribution Network Operator's mains source wherever possible.
6. Where possible stone cutting shall be carried out away from any noise sensitive premises. If bench saws/abrasive wheels or other stone cutting equipment is on site it should be adequately screened & provided with dust suppression.
7. "Best practicable means" shall be employed to prevent dust nuisance arising as a result of the works and shall include watering or any other necessary measures, which may be required from time to time.
8. Ensure roads and footpaths adjacent to the site are kept clean of construction materials, mud and spillage.
9. Ensure skips are emptied before they become overfilled and cover skips where dust and wind borne litter could be a nuisance
10. Burning of any material on site is not permitted unless exemption is granted by the Environment Agency
