

**TRAFFIC VOLUMES**  
**Barnsley West - North (Barugh Green)**

**Wagon Deliveries:**

Daily Average 3 - 4  
 Peak 20 - 30

[Peak times will be at early stages for placing stone during road construction and end of phases for surfacing works]

**Cars & Vans:**  
 Daily average 8 to 10

**NOTES**

- DRAWING TO BE READ IN CONJUNCTION WITH CMP
- SUPPLIERS AND COURIERS TO BE NOTIFIED OF ROUTE TO SITE IN ADVANCE
- INCOMING AND OUTGOING ROUTES TO WORK AREAS TO BE MADE UP OF STONE / HARDCORE
- ROAD SWEEPER TO BE VISITED REGULARLY, INCREASING PRESENCE DURING PEAK DELIVERY PERIODS
- ALL DELIVERIES WILL BE MET BY A TRAFFIC MARSHALL
- COMPOUND AREA TO BE TARMAC CONSTRUCTION AND SEGREGATED WITH HOARDING
- SITE STORAGE AREA TO BE SEGREGATED WITH HERAS FENCING
- WARNING SIGNAGE TO BE INSTALLED AT SITE ENTRANCES
- NOTICE SIGNAGE TO BE INSTALLED PRIOR TO TRAFFIC MANAGEMENT SETUP
- PROPOSED CONSTRUCTION AREAS TO BE UTILIZED FOR MATERIAL STORAGE & VEHICLE MANEUVERING WHERE FEASIBLE
- ACCESS TO SITE VIA M1 JNC 38 VIA A637 SUPPLIERS TO BE NOTIFIED OF ROUTE TO SITE
- ROAD CLOSURES TO BE PUT IN PLACE DURING FINAL SURFACING WORKS AT TIE-IN AREAS

**KEY**

 PHASE 4 CONSTRUCTION AREA

Revision	By	Date
0	For Information	CY 03/08/2023
A		
B		
C		

**CORE** Special Projects Earthworks Remediation Infrastructure

Core Special Projects Limited  
 2175 Century Way  
 Thorpe Park  
 Leeds LS15 8ZB

Tel: +44 (0)113 232 8000  
 Fax: +44 (0)113 232 8001  
 E-mail: mail@coresp.co.uk  
[www.coresp.co.uk](http://www.coresp.co.uk)


**Project:**  
 Barnsley West S278 - North

**Title:**  
 Construction Phase Traffic Management Plan  
 North Roundabout Phase 4

**Drawing No:** 001(1) **Revision:** 0

**Drawn By:** CY **Approved By:** LF

**Scale:** 1:250 **Date:** 03 Aug 2023 **Sheet Size:** A1

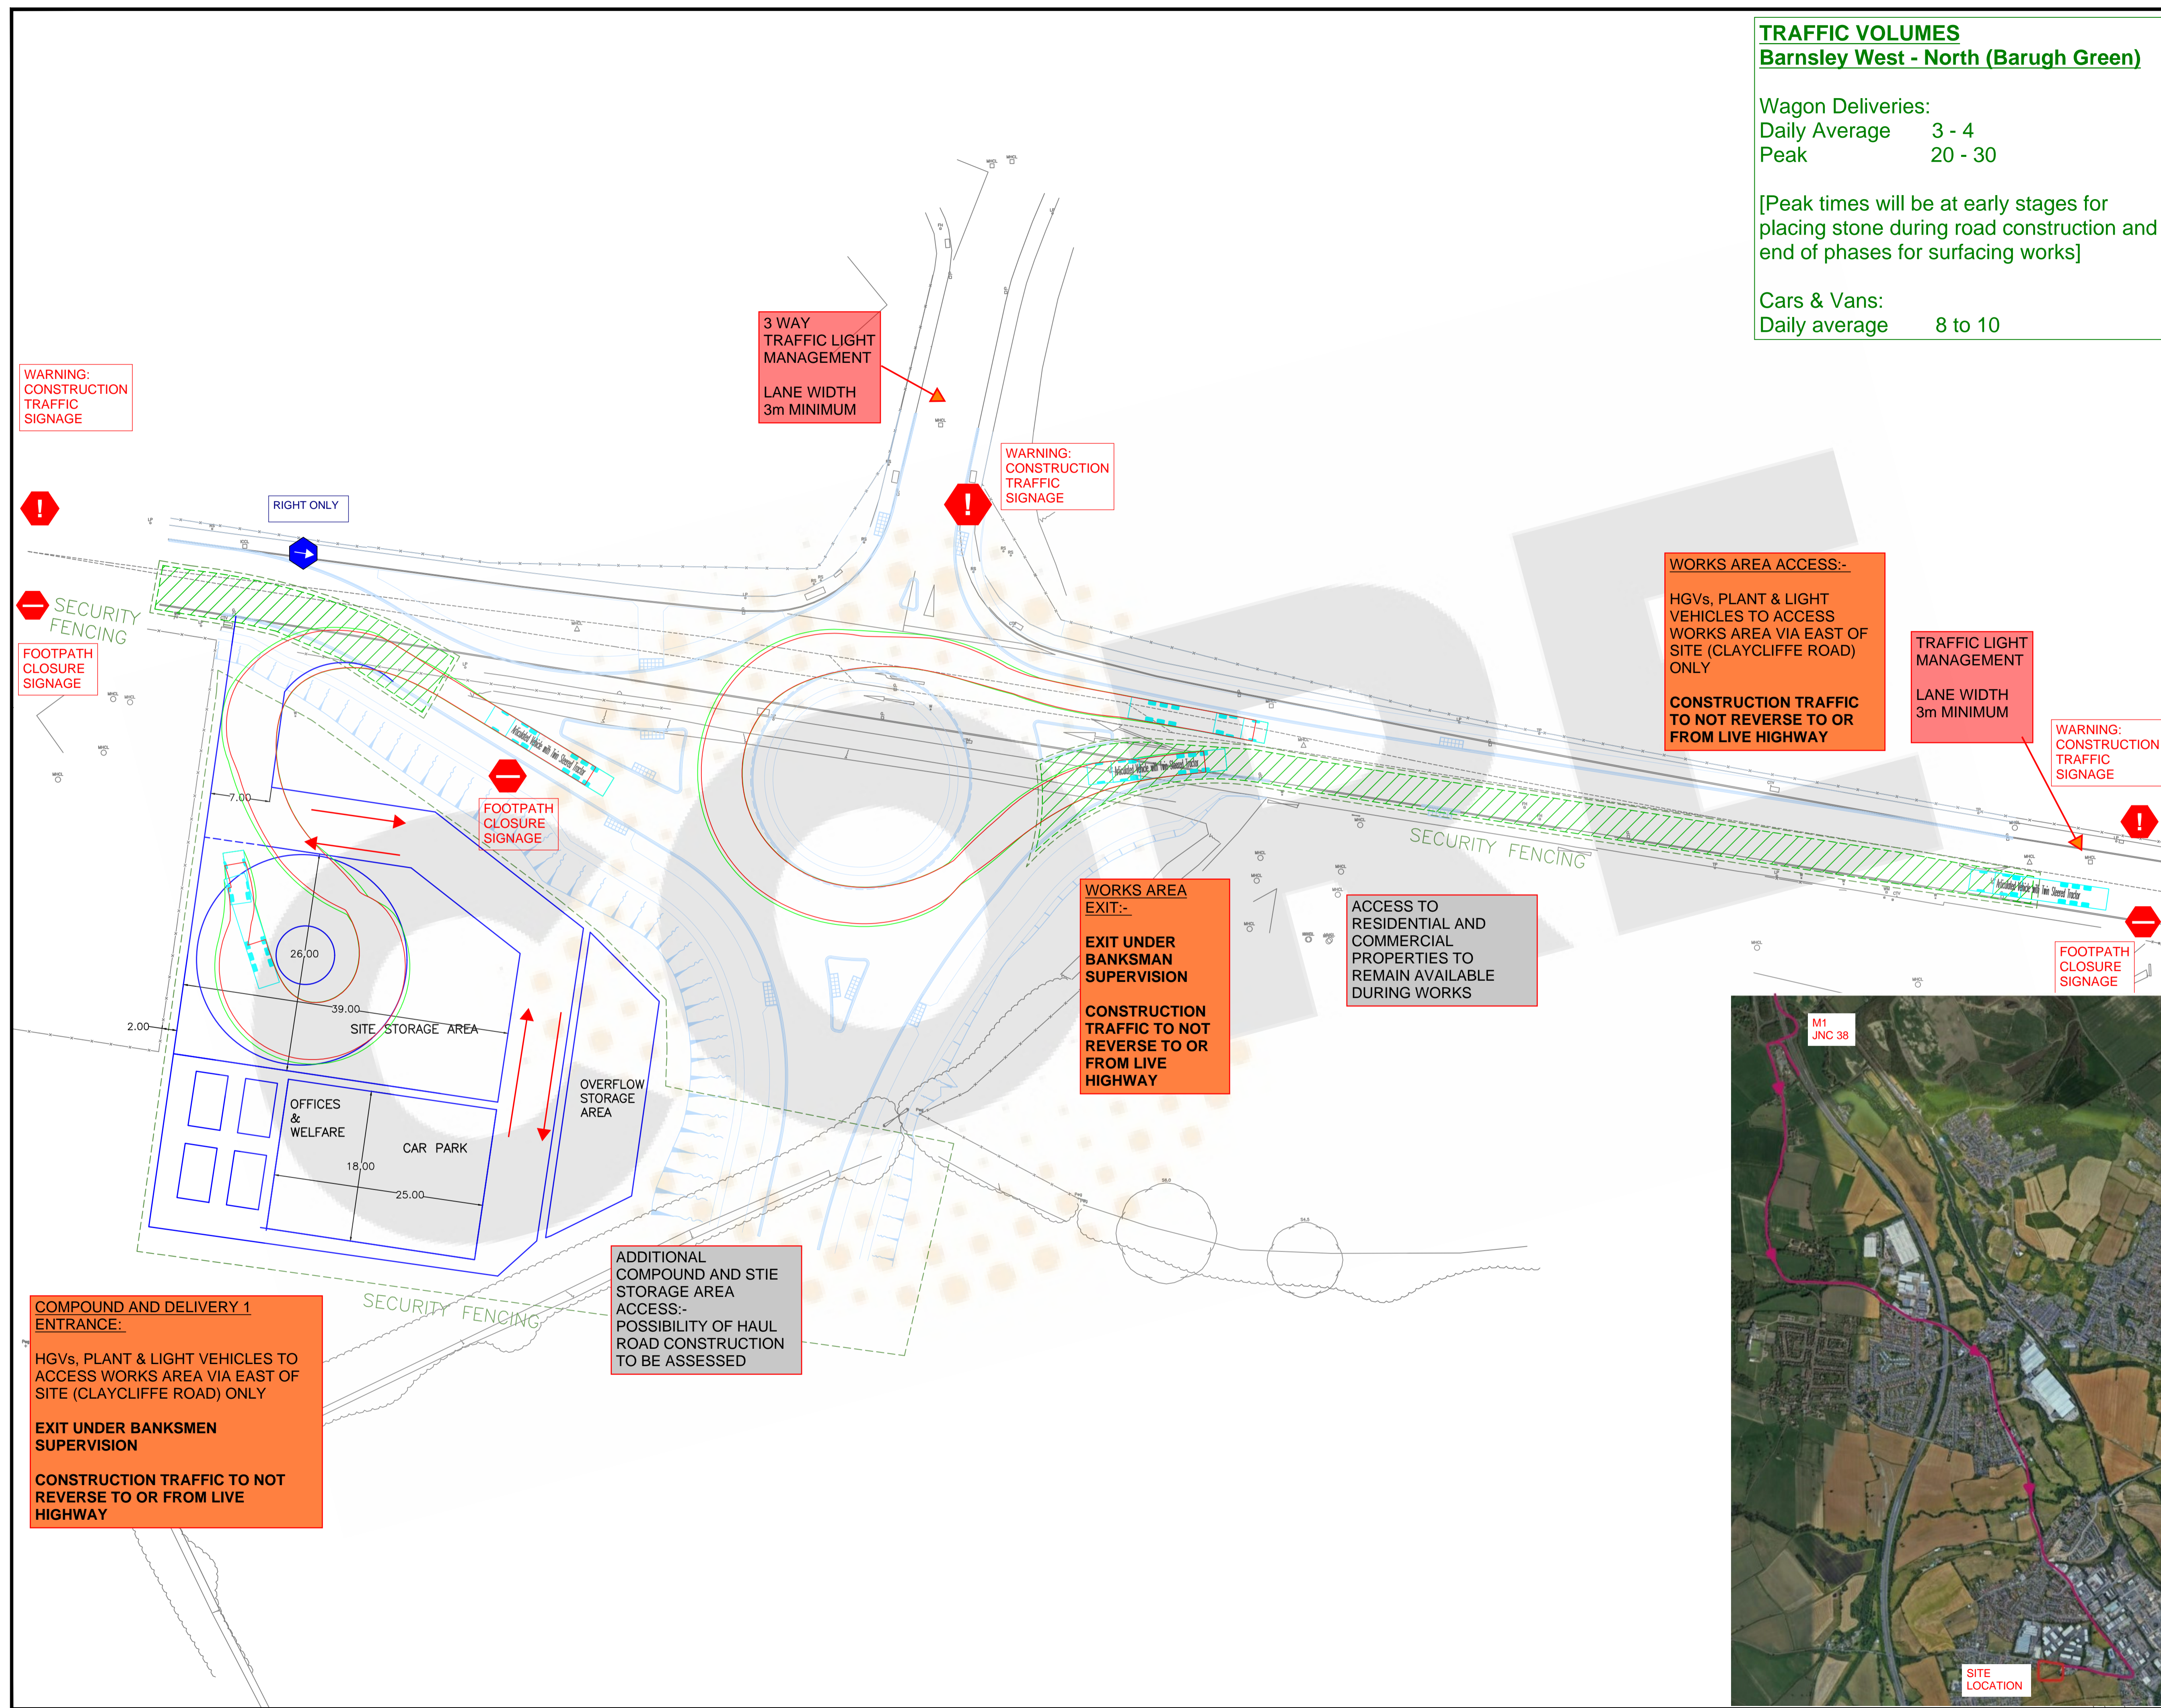

WARNING: CONSTRUCTION TRAFFIC SIGNAGE

3 WAY TRAFFIC LIGHT MANAGEMENT  
 LANE WIDTH 3m MINIMUM

WARNING: CONSTRUCTION TRAFFIC SIGNAGE

WORKS AREA ACCESS:-  
 HGVs, PLANT & LIGHT VEHICLES TO ACCESS WORKS AREA VIA EAST OF SITE (CLAYCLIFFE ROAD) ONLY  
 CONSTRUCTION TRAFFIC TO NOT REVERSE TO OR FROM LIVE HIGHWAY

TRAFFIC LIGHT MANAGEMENT  
 LANE WIDTH 3m MINIMUM

WARNING: CONSTRUCTION TRAFFIC SIGNAGE

WORKS AREA EXIT:-  
 EXIT UNDER BANKSMAN SUPERVISION  
 CONSTRUCTION TRAFFIC TO NOT REVERSE TO OR FROM LIVE HIGHWAY

ACCESS TO RESIDENTIAL AND COMMERCIAL PROPERTIES TO REMAIN AVAILABLE DURING WORKS

COMPOUND AND DELIVERY 1 ENTRANCE:-  
 HGVs, PLANT & LIGHT VEHICLES TO ACCESS WORKS AREA VIA EAST OF SITE (CLAYCLIFFE ROAD) ONLY  
 EXIT UNDER BANKSMEN SUPERVISION  
 CONSTRUCTION TRAFFIC TO NOT REVERSE TO OR FROM LIVE HIGHWAY

ADDITIONAL COMPOUND AND STIE STORAGE AREA ACCESS:-  
 POSSIBILITY OF HAUL ROAD CONSTRUCTION TO BE ASSESSED



RIGHT ONLY

SECURITY FENCING

FOOTPATH CLOSURE SIGNAGE

FOOTPATH CLOSURE SIGNAGE

FOOTPATH CLOSURE SIGNAGE

SECURITY FENCING

SITE LOCATION
