




Phase	Requirements	Method
<b>5</b> Completion of main construction and undertaking of landscaping	Landscaping and Dismantling of tree barrier protective fencing.	<p>It is essential that ground levels within the root protection areas are not altered, either by raising or lowering soil levels; even at the landscaping stage.</p> <p>Landscaping operations must be undertaken in a manner that will not impact trees.</p> <p>Landscaping within the root protection area of trees must be undertaken in the following manner:</p> <ol style="list-style-type: none"> <li>Any existing ground flora (grass/weeds/scrub) is to be sprayed with a systemic herbicide and left to die-off.</li> <li>Dead flora is to be strimmed as hard as possible with a brush cutter or similar. The bulk of the strimmed material is to be removed by raking.</li> <li>A good quality organic topsoil layer may be placed down. Small depressions may be filled (and <b>lightly</b> compacted underfoot). Placed topsoil soil layers <b>must not exceed</b> 100mm depth.</li> <li>No plant machinery operating within the root protection areas to exceed 1 tonne gross weight and must only operate from propriety ground protection boards such as DuraMatt Access Mats (see <b>Appendix C</b>).</li> <li>Turf and other planting to proceed thereafter.</li> </ol>

HIS DRAWING MUST BE VIEWED  
IN COLOUR AND READ IN  
CONJUNCTION WITH  
ARBORICULTURAL IMPACT  
ASSESSMENT AND METHOD  
STATEMENT

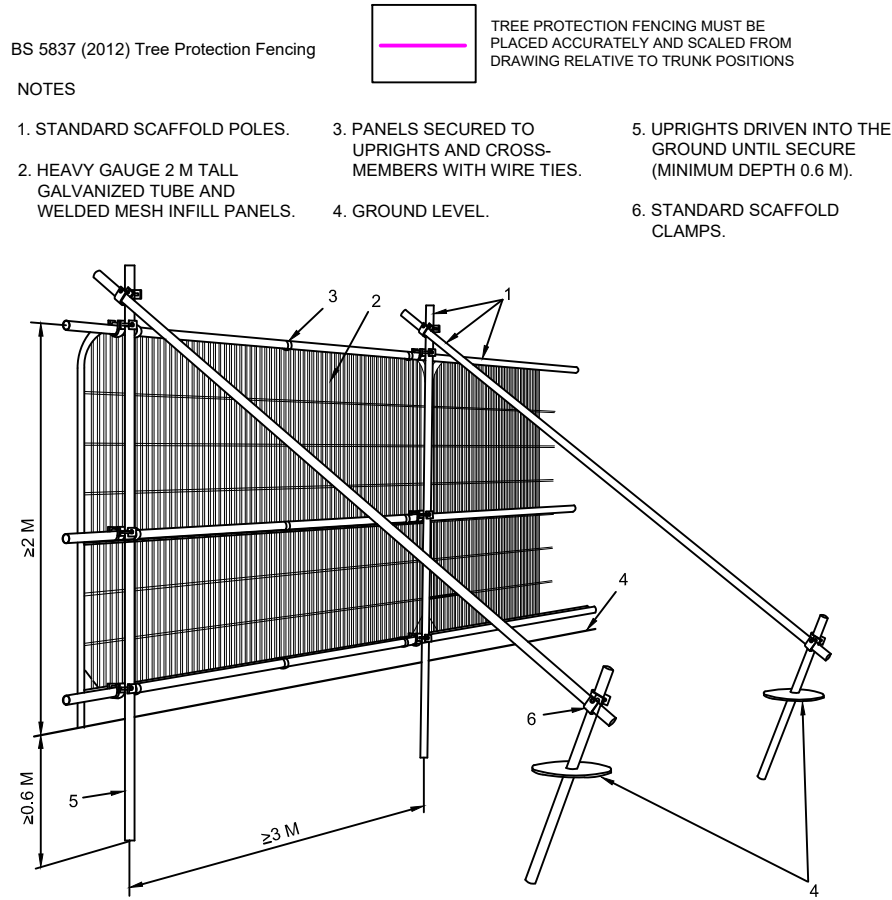

No dimension to be scaled from this drawing © Copyright reserved		Date	Dwn	Rev
				
<p>Landscape Architecture Arboriculture</p> <p>Trevor Bridge Associates Ltd Ashton Old Baths Stamford Street West Ashton-under-Lyne Lancs OL6 7FW</p> <p>Tel: 0161-804 2099 E-mail: info@trevorbridge.co.uk</p>				
Project				
St Helens Street, Elsecar, Barnsley				
Leon Grayson				
Title				
TREE PROTECTION PLAN				
Date	Scale(s)	Dwg no	Rev	
FEB23	1:250	7107.03		
Dwn	Chkd	@ A1		
KR	MG			
