




# Arboricultural Method Statement (AMS) for Granville Oil & Chemicals

|                      |                                                                    |                     |                                               |
|----------------------|--------------------------------------------------------------------|---------------------|-----------------------------------------------|
| <b>Site Address:</b> | Unit 28,<br>Goldthorpe Industrial Estate,<br>Rotherham,<br>S63 9BL | <b>Client:</b>      | Granville Oil & Chemicals<br>F.A.O James Todd |
| <b>Report Ref:</b>   | (AMS)GR02-19                                                       | <b>Report Date:</b> | 19th June 2019                                |
| <b>Author:</b>       | Laurence Smith BSc (Hons)<br>Arb, M Arbor A                        | <b>Signed:</b>      | <i>Laurence Smith</i>                         |

|                                                         |           |
|---------------------------------------------------------|-----------|
| <b>1 Executive Summary</b>                              | <b>3</b>  |
| <b>2 Introduction</b>                                   | <b>3</b>  |
| 2.1 Client Instruction                                  | 3         |
| 2.2 Purpose of the Method Statement                     | 3         |
| 2.3 Project Background                                  | 3         |
| 2.4 Assumption and Limitations                          | 4         |
| <b>3. Tree Preservation Orders</b>                      | <b>4</b>  |
| <b>4. Method Statement</b>                              | <b>4</b>  |
| 4.1 Status of the Method Statement                      | 4         |
| 4.2 Introduction                                        | 5         |
| 4.3 Arboricultural Monitoring and Timescales            | 5         |
| 4.5 Relevant Contact Details                            | 6         |
| 4.6 Methodology                                         | 6         |
| 4.7 Tree Protection Barriers                            | 6         |
| 4.8 Tree Works Prior, During and Post Construction      | 7         |
| 4.8.1 Tree Works Prior to Construction                  | 7         |
| 4.8.2 Tree Works During Construction                    | 7         |
| 4.8.3 Tree Works Post Construction                      | 7         |
| 4.8.4 Recommendations For Tree Works                    | 8         |
| 4.9 Location of the Site Compound                       | 8         |
| <b>5. Landscaping Plan</b>                              | <b>8</b>  |
| 5.1 Planting Locations and Species                      | 8         |
| 5.2 Site Preparation                                    | 8         |
| 5.3 Planting                                            | 9         |
| 5.4 Planting Schedule                                   | 9         |
| <b>6. Landscaping Management Plan</b>                   | <b>9</b>  |
| 6.1 Period of Maintenance                               | 9         |
| 6.2 Weed Control                                        | 9         |
| 6.3 Replacement of losses                               | 10        |
| <b>References</b>                                       | <b>10</b> |
| <b>Appendix 1: Site Plans</b>                           | <b>10</b> |
| <b>Appendix 2: Example of Protective Barrier</b>        | <b>15</b> |
| <b>Appendix 3: Example of Protective Barrier Notice</b> | <b>16</b> |

# **1 Executive Summary**

James Todd of GGP Consult has requested an arboricultural report in order to provide an arboricultural method statement for tree protection methodology. This also includes a landscape management plan post development, in order to comply with planning conditions.

The development proposal consists of an extension to Unit 28 with 2 additional units to the south; Unit28a and Unit28b. Along with the unit extension there are 3 areas which are to be modified into regions of hard standing. The details of these plans can be seen in Appendix 1.

Retained trees are to be protected during the development by the use of protective fencing which complies with the recommendations sent out in the British standards document BS 5837:2012.

It is the opinion of Key Tree Solutions that although the volume of tree stock will decrease as a result of this development, by employing better management practices the quality, longevity, and value of the remaining tree stock can be significantly increased as part of the mitigation.

## **2 Introduction**

### **2.1 Client Instruction**

Key Tree Solutions was instructed by James Todd to produce an Arboricultural Method Statement (AMS) relating to the proposal for an extension at Unit 28, Goldthorpe Industrial Estate.

### **2.2 Purpose of the Method Statement**

The purpose of this document is to provide reference to and clarification on tree protection and any necessary tree management works relating to the impact on any trees, in order to ensure good practice in the protection of retained trees throughout the proposed development.

### **2.3 Project Background**

Planning permission on APPLICATION NO. 2019/0105 has been granted for the proposed development provided a number of conditions are met. This includes an AMS, Landscaping Plan and Landscaping Management Plan.

Key Tree Solutions have previously been commissioned to undertake an arboricultural survey and impact assessment report (GR01-19) which conforms to the most recent specifications outlined in BS 5837: 2012 *Trees in relation to design, demolition and construction - Recommendations*.

This report was used to guide the AMS along with the landscaping and landscape management plan.

## **2.4 Assumption and Limitations**

A topographical map plotting the exact tree locations has not been undertaken due to the high volume of trees which fall outside of the threshold for inclusion, ie those with a diameter of 150mm or below. Thus tree locations for those included within the report, ie trees with a diameter of over 150mm, have been approximated. The accuracy of this method is considered to be adequate for this project. All trees within the Tree Protection Plan contained in Appendix 1 have been plotted according to this information.

## **3. Tree Preservation Orders**

Local Planning Authorities (LPAs) have the power to preserve selected trees and woodlands through the making of Tree Preservation Orders (TPOs). Similarly, special provision is provided to trees located within Conservation Areas (CAs) which are not the subject of a TPO. The LPAs powers to do this are provided by the following Act of Parliament and its associated regulations:

- Town and Country Planning Act 1990
- Town and Country Planning (Determination of Appeals by Appointed Persons) (Prescribed Classes) (Amendment) (England) Regulations 2008
- Town and Country Planning (Trees) (Amendment) (England) Regulations 2012. The principle effect of a TPO is to prohibit the cutting down, uprooting, topping, lopping, wilful damage or wilful destruction of trees without first obtaining the consent of the relevant Local Authority.

Unauthorised works to trees either protected by a TPO or those that are located within a CA, could result in a fine of up to £20,000 per tree.

The LPA have confirmed that the trees on site are neither protected by a TPO nor fall within a Conservation Area.

## **4. Method Statement**

### **4.1 Status of the Method Statement**

This Arboricultural Method Statement should be included as part of the specification and schedule of works issued to the building contractor and can form part of the contract.

This Arboricultural Method Statement should be available on site for inspection by the local authority, contractors and other relevant persons.

## 4.2 Introduction

Movement of heavy mechanical plant (excavators etc), with the exception of tracked wood chippers pre fence erection, shall not be undertaken within the Exclusion Zone (EZ). This region will be contained by barrier fencing or large differences in ground level after the initial tree works have been undertaken.

There are no foreseeable Root Protection Areas (RPA's) which extend beyond the fencing. As such, there is no recommendation for the use of temporary ground protection.

The approach to tree protection for this scenario is outlined in the following methodology, approval of which must be confirmed in writing by the LPA prior to the commencement of works.

## 4.3 Arboricultural Monitoring and Timescales

The LPA will be given notice of the planned dates of the construction works to facilitate the on-site presence of a Tree Officer should they be wish to attend.

The following Arboricultural Sequence of Events can also be referenced during the works process:

| Timescale | Action                                                                                                                                                                          | ✓ |
|-----------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---|
| Stage 1   | All requirements listed in the planning consent are approved by the Local Authority planning office.                                                                            |   |
| Stage 2   | Complete tree works to facilitate the development.                                                                                                                              |   |
| Stage 3   | Install the temporary protective fencing around the trees (as detailed in Section 4.7 and as shown on the Tree Protection Plan in Appendix 1).                                  |   |
| Stage 4   | Invite the Local Planning Authority to inspect the fencing measures prior to any on-site construction. Once inspected, the protective fencing must not to be moved or breached. |   |
| Stage 5   | Undertake the construction phase.                                                                                                                                               |   |
| Stage 6   | Following the completion of the construction phase and when all site traffic and machinery has left, the protective fencing can be removed.                                     |   |
| Stage 7   | Post construction remedial tree works to be undertaken (if required)                                                                                                            |   |
| Stage 8   | Commence the landscaping scheme.                                                                                                                                                |   |

#### 4.5 Relevant Contact Details

| Contact Name   | Organisation/ Detail | Contact       |
|----------------|----------------------|---------------|
| Laurence Smith | Key Tree Solutions   | 07716 638 613 |
|                | Tree Officer         |               |
| Site Manager   |                      |               |

#### 4.6 Methodology

Tree removals necessary to facilitate the development will be undertaken, which includes all trees and woody vegetation which falls outside off the EZ as shown on the Tree Protection Plan (Appendix 1). The boundary of the EZ will be set back by 3 metres from the proposed retaining wall (where applicable) to ensure that RPA's of the remaining trees are not damaged during pre development landscaping.

The remaining tree stock will be thinned by 20%. The thinning process will focus on the Birch, Willow, and Laurel trees or trees in poor condition i.e. defects which can not be improved with formative pruning. Wood chip created as a result of these removals can be spread evenly inside the EZ provided it is not heaped in piles deeper than 10cm.

Once all tree works have been undertaken, the temporary protective fencing around the Exclusion Zone 3 (EZ3) to the east as detailed in Section 4.7 and as shown on the Tree Protection Plan in Appendix 1, can be erected.

The two remaining Exclusion Zones (EZ1, EZ2) to the south will not be fenced off due to the changes in height making these regions hazardous to access by machine.

Post construction phase and after all development traffic has left site, the fence can be removed and the landscaping plan undertaken provided the season is suitable.

#### 4.7 Tree Protection Barriers

Tree protection barriers must be fit for the purpose of excluding construction activity and provide adequate protection to retained trees. It is proposed that they will consist of 2m tall welded mesh panels supported on concrete feet. Each panel will be secured to its neighbour with a minimum of 2 anti-tamper couplers secured so that they can only be undone from inside the EZ. The panels will be further supported by stabiliser struts which will be pinned to the ground. An example of this type of barrier is contained in Appendix 2. The location of the tree protection barriers is provided on the Tree Protection Plan contained in Appendix 1.

Inside the tree protection barriers the following prohibitions will be complied with:

- No excavations, including by hand; unless agreed with the retained arboricultural consultant;

- No storage of machinery;
- No storage or handling of building materials, fuel, chemicals or spoil;
- No fires;
- No vehicular access;
- No pedestrian access; unless agreed with the retained arboricultural consultant;
- No alteration, increase or decrease, to existing ground levels;
- No excavation or installation of services.

The tree protection barriers will not be moved. To enable site operatives to appreciate the purpose of the protective fencing, and reduce the risk of operatives attempting to move them, all-weather notices will be erected on the barriers similar to the example in Appendix 3. The barriers will only be adjusted or removed if prior written approval is obtained from the retained arboricultural consultant.

## **4.8 Tree Works Prior, During and Post Construction**

### **4.8.1 Tree Works Prior to Construction**

Trees which need to be removed to facilitate the development have not been individually listed for this AMS due to the volume of trees which fall under the 150mm diameter and were not included on the Arboricultural Survey. Additionally the potential for inaccuracy in tree location plotting may result in inaccuracies for marking trees for retention or removal.

As such, the EZ's will be marked out by a competent person or arboricultural consultant/contractor with Eco Marker spray. This also includes marking up of any trees scheduled for removal as part of the thinning program of works.

Trees outside of the EZ's or those marked within them can then be safely removed by the arboricultural contractor.

### **4.8.2 Tree Works During Construction**

In this case, no above ground tree works are envisaged to be required during the construction phase.

Damage to trees during the construction phase should be entirely prevented by the installation of the temporary protective fencing to create a EZ. All persons on site must be aware of limitations that apply within the EZ (please refer to Section 4.7).

If any trees on site are damaged, this must be immediately reported to Key Tree Solutions to agree on appropriate remedial action. Contact numbers for all parties can be found at Section 4.5.

### **4.8.3 Tree Works Post Construction**

No destructive tree works post construction have been envisaged.

#### **4.8.4 Recommendations For Tree Works**

All work must be undertaken to BS 3998: 2010 - *Recommendations for tree work* and carried out by qualified, experienced and, ideally, Arboricultural Association approved contractors who must be adequately insured.

Any defects seen by a contractor or the client that were not apparent to the consultant must be brought to the attention of Key Tree Solutions immediately.

No liability can be accepted by Key Tree Solutions in respect of the trees unless the recommendations of this Method Statement are carried out under our supervision.

#### **4.9 Location of the Site Compound**

The site compound, typically including the site office, mess facilities, toilets, storage of materials and parking, must be located away from and outside the RPA of retained trees. Areas designated for the storage and/or mixing of chemicals, including petrol, diesel and oils must also be located away from and outside the RPA of retained trees. Such areas should be constructed with consideration to, and contingencies for, the occurrence of spillages, preventing the leaching of chemicals into unprotected, open ground.

### **5. Landscaping Plan**

#### **5.1 Planting Locations and Species**

Tree planting will be undertaken in the regions above the retaining wall as show in Appendix 1 - New Planting Plan. Planting in this region will be undertaken with species with a small maximum height such as; Birch, Hawthorn, Crab Apple and Rowan. Additionally new planting will also be undertaken where there are gaps in the overall canopy, i.e after the removal of a tree with significant defects or other naturally occurring regions where there are currently less trees, such as close to the southern boundary. Planting in this location will be undertaken with trees that have a larger potential growth such as Oak. This species have been selected due to their ability to accommodate a high biodiversity

#### **5.2 Site Preparation**

All weeds shall be cut down and where necessary removed from site to a facility found by the contractor. An approved, contact herbicide spray shall be applied to all new planting areas on site to reduce competition by weeds on new plant growth. The weed free area should surround each new plant by at least 0.5m.

All stone, brick, concrete, wood, wire, pipes debris, rubbish, weed roots and foreign matter of any kind above a maximum dimension of 150mm shall be removed from the planting areas.

### 5.3 Planting

All trees shall conform to BS 3936 for Nursery stock and BS 5236 for Advanced Nursery Stock. Trees should have a sturdy and well-defined straight leader. All plants must have a good root system, vigorous with a good fibrous growth. Plants must meet the sizes stated in the planting schedule (Section 5.4).

Protection of plants until final planting shall comply with the industry best code of practice for plant handling, during lifting, packaging and transportation to site.

Holes will be dug out large enough to receive the roots of the plant fully extended and well spread out. Top-soil should be carefully worked among roots and backfilled. Plants should be well firmed by heeling and the surface left neat and even. Planting must be to the same depth as in the nursery. Care must be taken not to disturb the root balls of pot grown plants and not to let any roots dry out at any time. For small seedlings and whips, notch planting may be undertaken where the notch will provide a slit of sufficient size to accommodate the roots of the plants without any trimming or being forced into the slits. Tree will be staked and protected with appropriate means.

Unless otherwise specified, all transplanting shall be carried out between the end of October and the end of March. The transplanting shall be carried out when the weather is dull and the ground is moist and workable. On no account must the planting take place when there is freezing wind.

### 5.4 Planting Schedule

| Tree Species                                     | Size        | Type | Density    |
|--------------------------------------------------|-------------|------|------------|
| Oak, Birch,<br>Hawthorn, Crab<br>Apple and Rowan | 0.5m - 1.0m | Whip | 5m Spacing |

## 6. Landscaping Management Plan

### 6.1 Period of Maintenance

The contractor will be responsible for the programme of maintenance for all new planting. The maintenance work is to ensure that all plantings that fail to make active growth are replaced during the first available planting season for the first 12 months.

### 6.2 Weed Control

During March, an application of Glyphosate will control competitive weeds and grass around trees for the first 5 years after planting. A weed free zone of 0.5m radius around each plant is to be provided. Glyphosate is a non-selective herbicide that is absorbed through leaves. The chemical should be applied by someone who has a relevant pesticide application certificate.

### **6.3 Replacement of losses**

During the first 12 months from the date of planting, the contractor will be responsible for all deaths of newly planted trees and shrubs. Replacement will be at the contractor's expense.

### **Signed**



Laurence Smith BSc (Hons) Arboriculture, M Arbor A

### **References**

British standards document BS 5837:2012 *'Trees in relation to design, demolition and construction – Recommendations'*

British standards document BS 3998:2010 *'Tree work - recommendations'*

Management of the risk from falling trees or branches - Health & Safety Executive (HSC) Document

2018 National House Building Council (NHBC) standards

### **Appendix 1: Site Plans**


- Site Plan as Existing
- Site Plan as Proposed
- Tree Protection Plan
- New Planting Plan

Extent of Land Ownership

Extent of Proposed Site

Boundary Legend


1 : 1000



0m 5m 10m 20m

Scale Bar

1 : 200

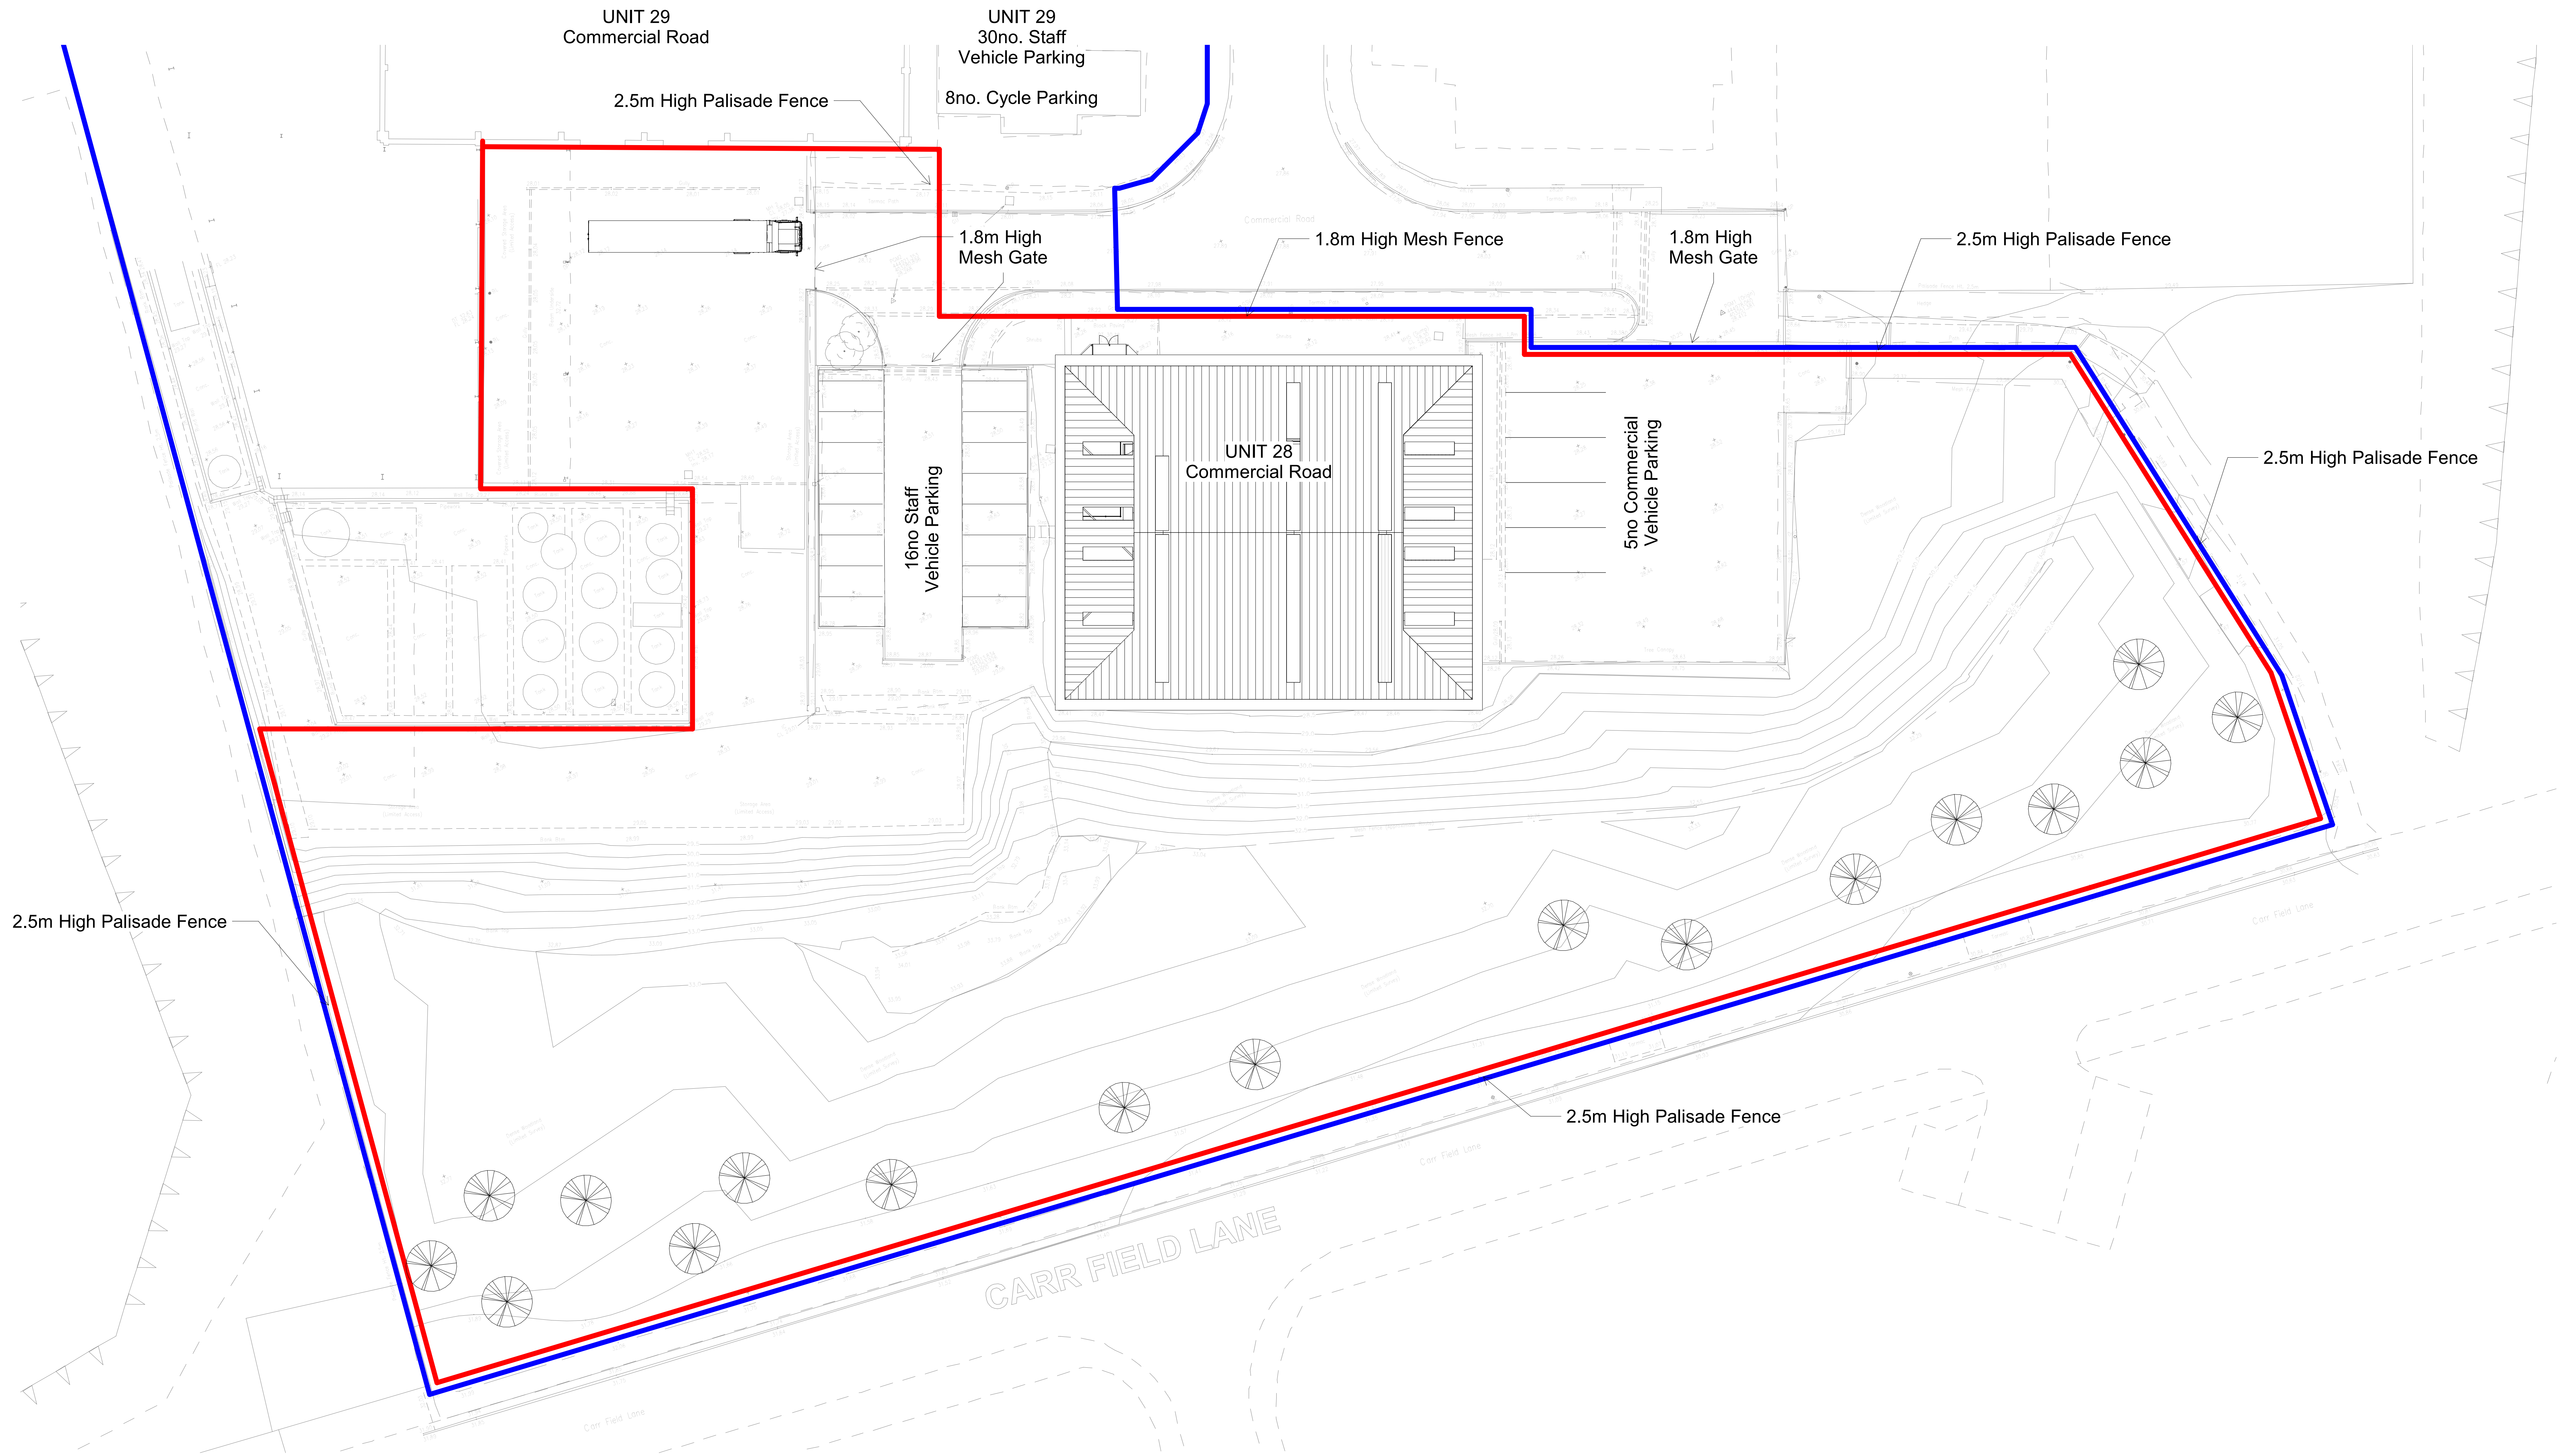

2.5m High Palisade Fence

UNIT 29  
Commercial Road

UNIT 29  
30no. Staff  
Vehicle Parking  
8no. Cycle Parking

2.5m High Palisade Fence

1.8m High  
Mesh Gate

1.8m High Mesh Fence

1.8m High  
Mesh Gate

2.5m High Palisade Fence

16no Staff  
Vehicle Parking

UNIT 28  
Commercial Road

5no Commercial  
Vehicle Parking

2.5m High Palisade Fence

2.5m High Palisade Fence

CARR FIELD LANE

1 Site Plan As Existing

1 : 200

NOTES

|     |          |                        |     |    |
|-----|----------|------------------------|-----|----|
| B   | 18.02.19 | Boundary Lines amended | JHT | JH |
| A   | 21.01.19 | Parking identified     | JHT | JH |
| Rev | Date     | Description            | DR  | CH |



**GGP**  
CONSULT



CONSULTING ENGINEERS  
ARCHITECTS  
PROJECT MANAGEMENT  
2 Hallam Road  
Priory Park East  
HULL HU4 7DY  
United Kingdom

Telephone (+44) 01482 627963  
Fax (+44) 01482 641736  
Email info@ggpconsult.co.uk

Client: Granville Oil & Chemicals Ltd.

Job Title: Proposed Extension Unit 28  
Goldthorpe Industrial Estate  
Rotherham

Site Plan As Existing

|          |                   |          |            |
|----------|-------------------|----------|------------|
| Status   | PLANNING          |          |            |
| Scale    | As indicated      | Date     | 02/01/2019 |
| Drawn By | JHT               | Checked  | JC         |
|          |                   | Approved | AT         |
| Dwg No.  | 27988 AA_(100)_02 | Rev      | B          |


A0 - ORIGINAL SHEET SIZE

Extent of Land Ownership

Extent of Proposed Site

Boundary Legend


1 : 1000



0m 5m 10m 20m

Scale Bar

1 : 200

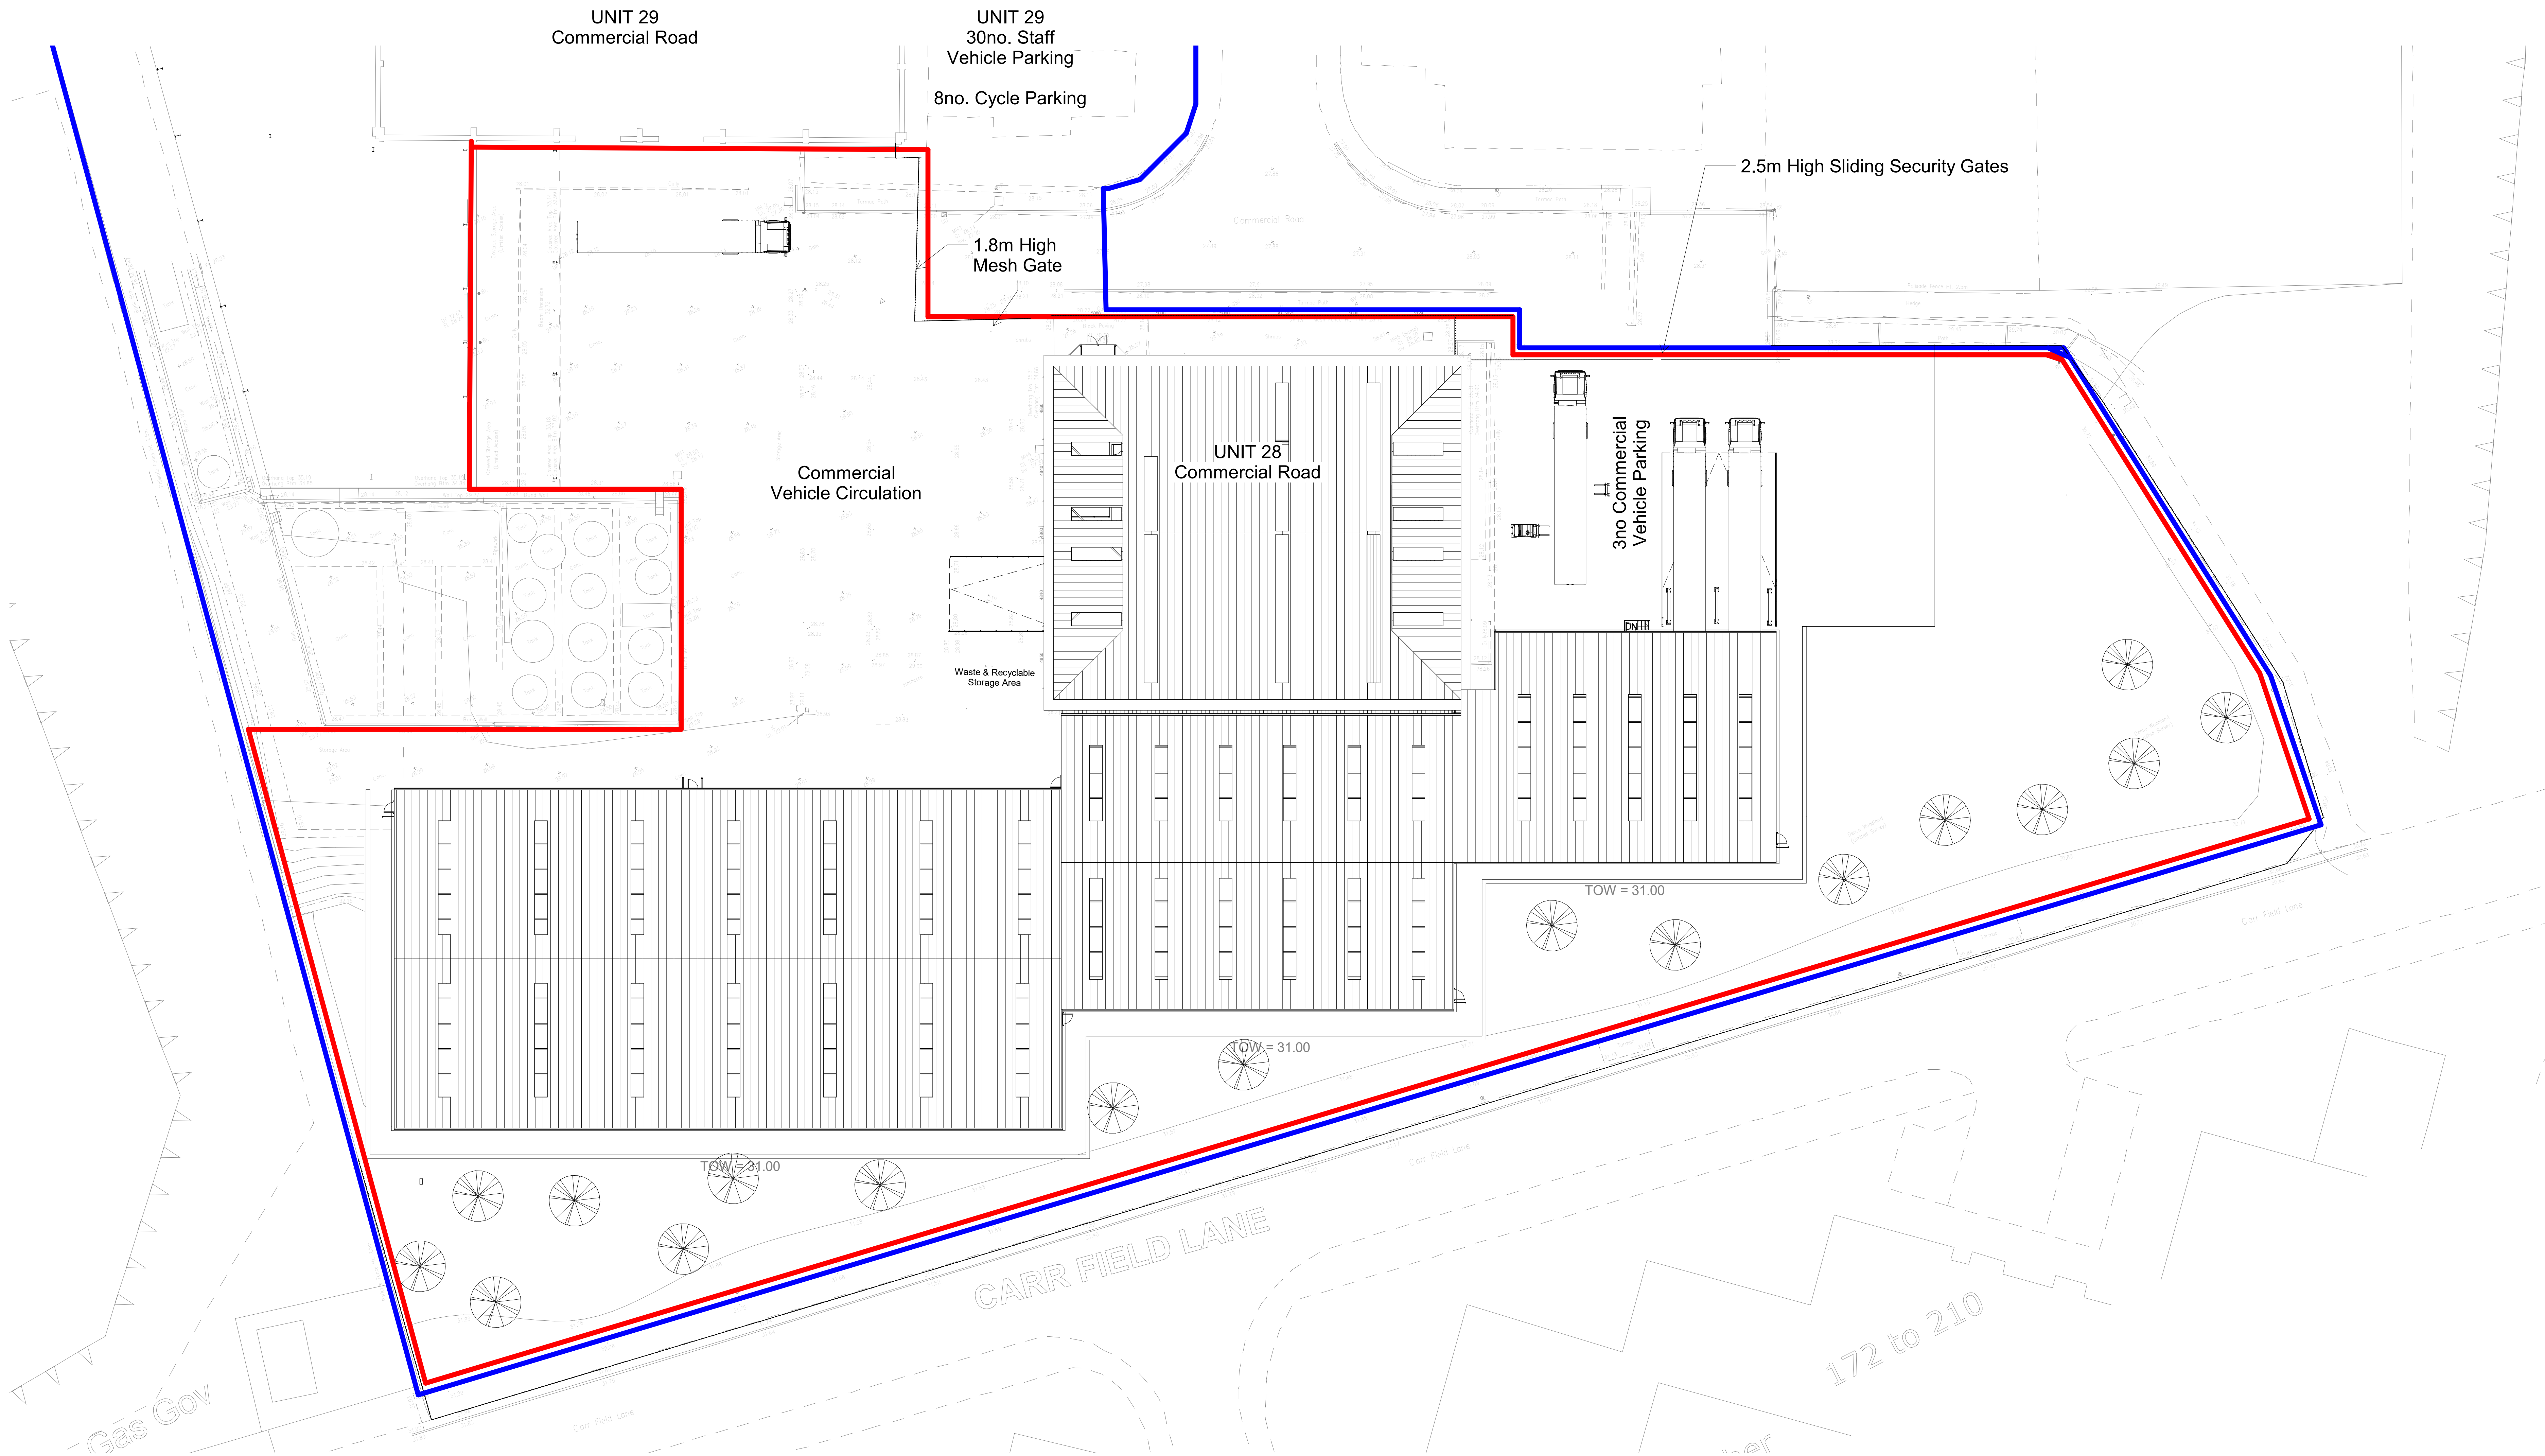

1 Site Plan As Proposed

1 : 200

NOTES

|     |          |                        |     |    |
|-----|----------|------------------------|-----|----|
| B   | 18.02.19 | Boundary Lines amended | JHT | JH |
| A   | 21.01.19 | Parking identified     | JHT | JH |
| Rev | Date     | Description            | DR  | CH |

©copyright



**GGP CONSULT**

CONSULTING ENGINEERS  
ARCHITECTS  
PROJECT MANAGEMENT  
2 Hallam Road  
Priory Park East  
HULL HU4 7DY  
United Kingdom

Telephone (+44) 01482 627963  
Fax (+44) 01482 641736  
Email info@ggpcconsult.co.uk

Client: Granville Oil & Chemicals Ltd.

Job Title: Proposed Extension Unit 28  
Goldthorpe Industrial Estate  
Rotherham

Drawing Title: Site Plan As Proposed



Status: PLANNING

Scale: As indicated Date: 02/01/2019

Drawn By: JHT Checked: JC Approved: AT

Dwg No: 27988 AA\_(100)\_10 Rev: B


A0 - ORIGINAL SHEET SIZE


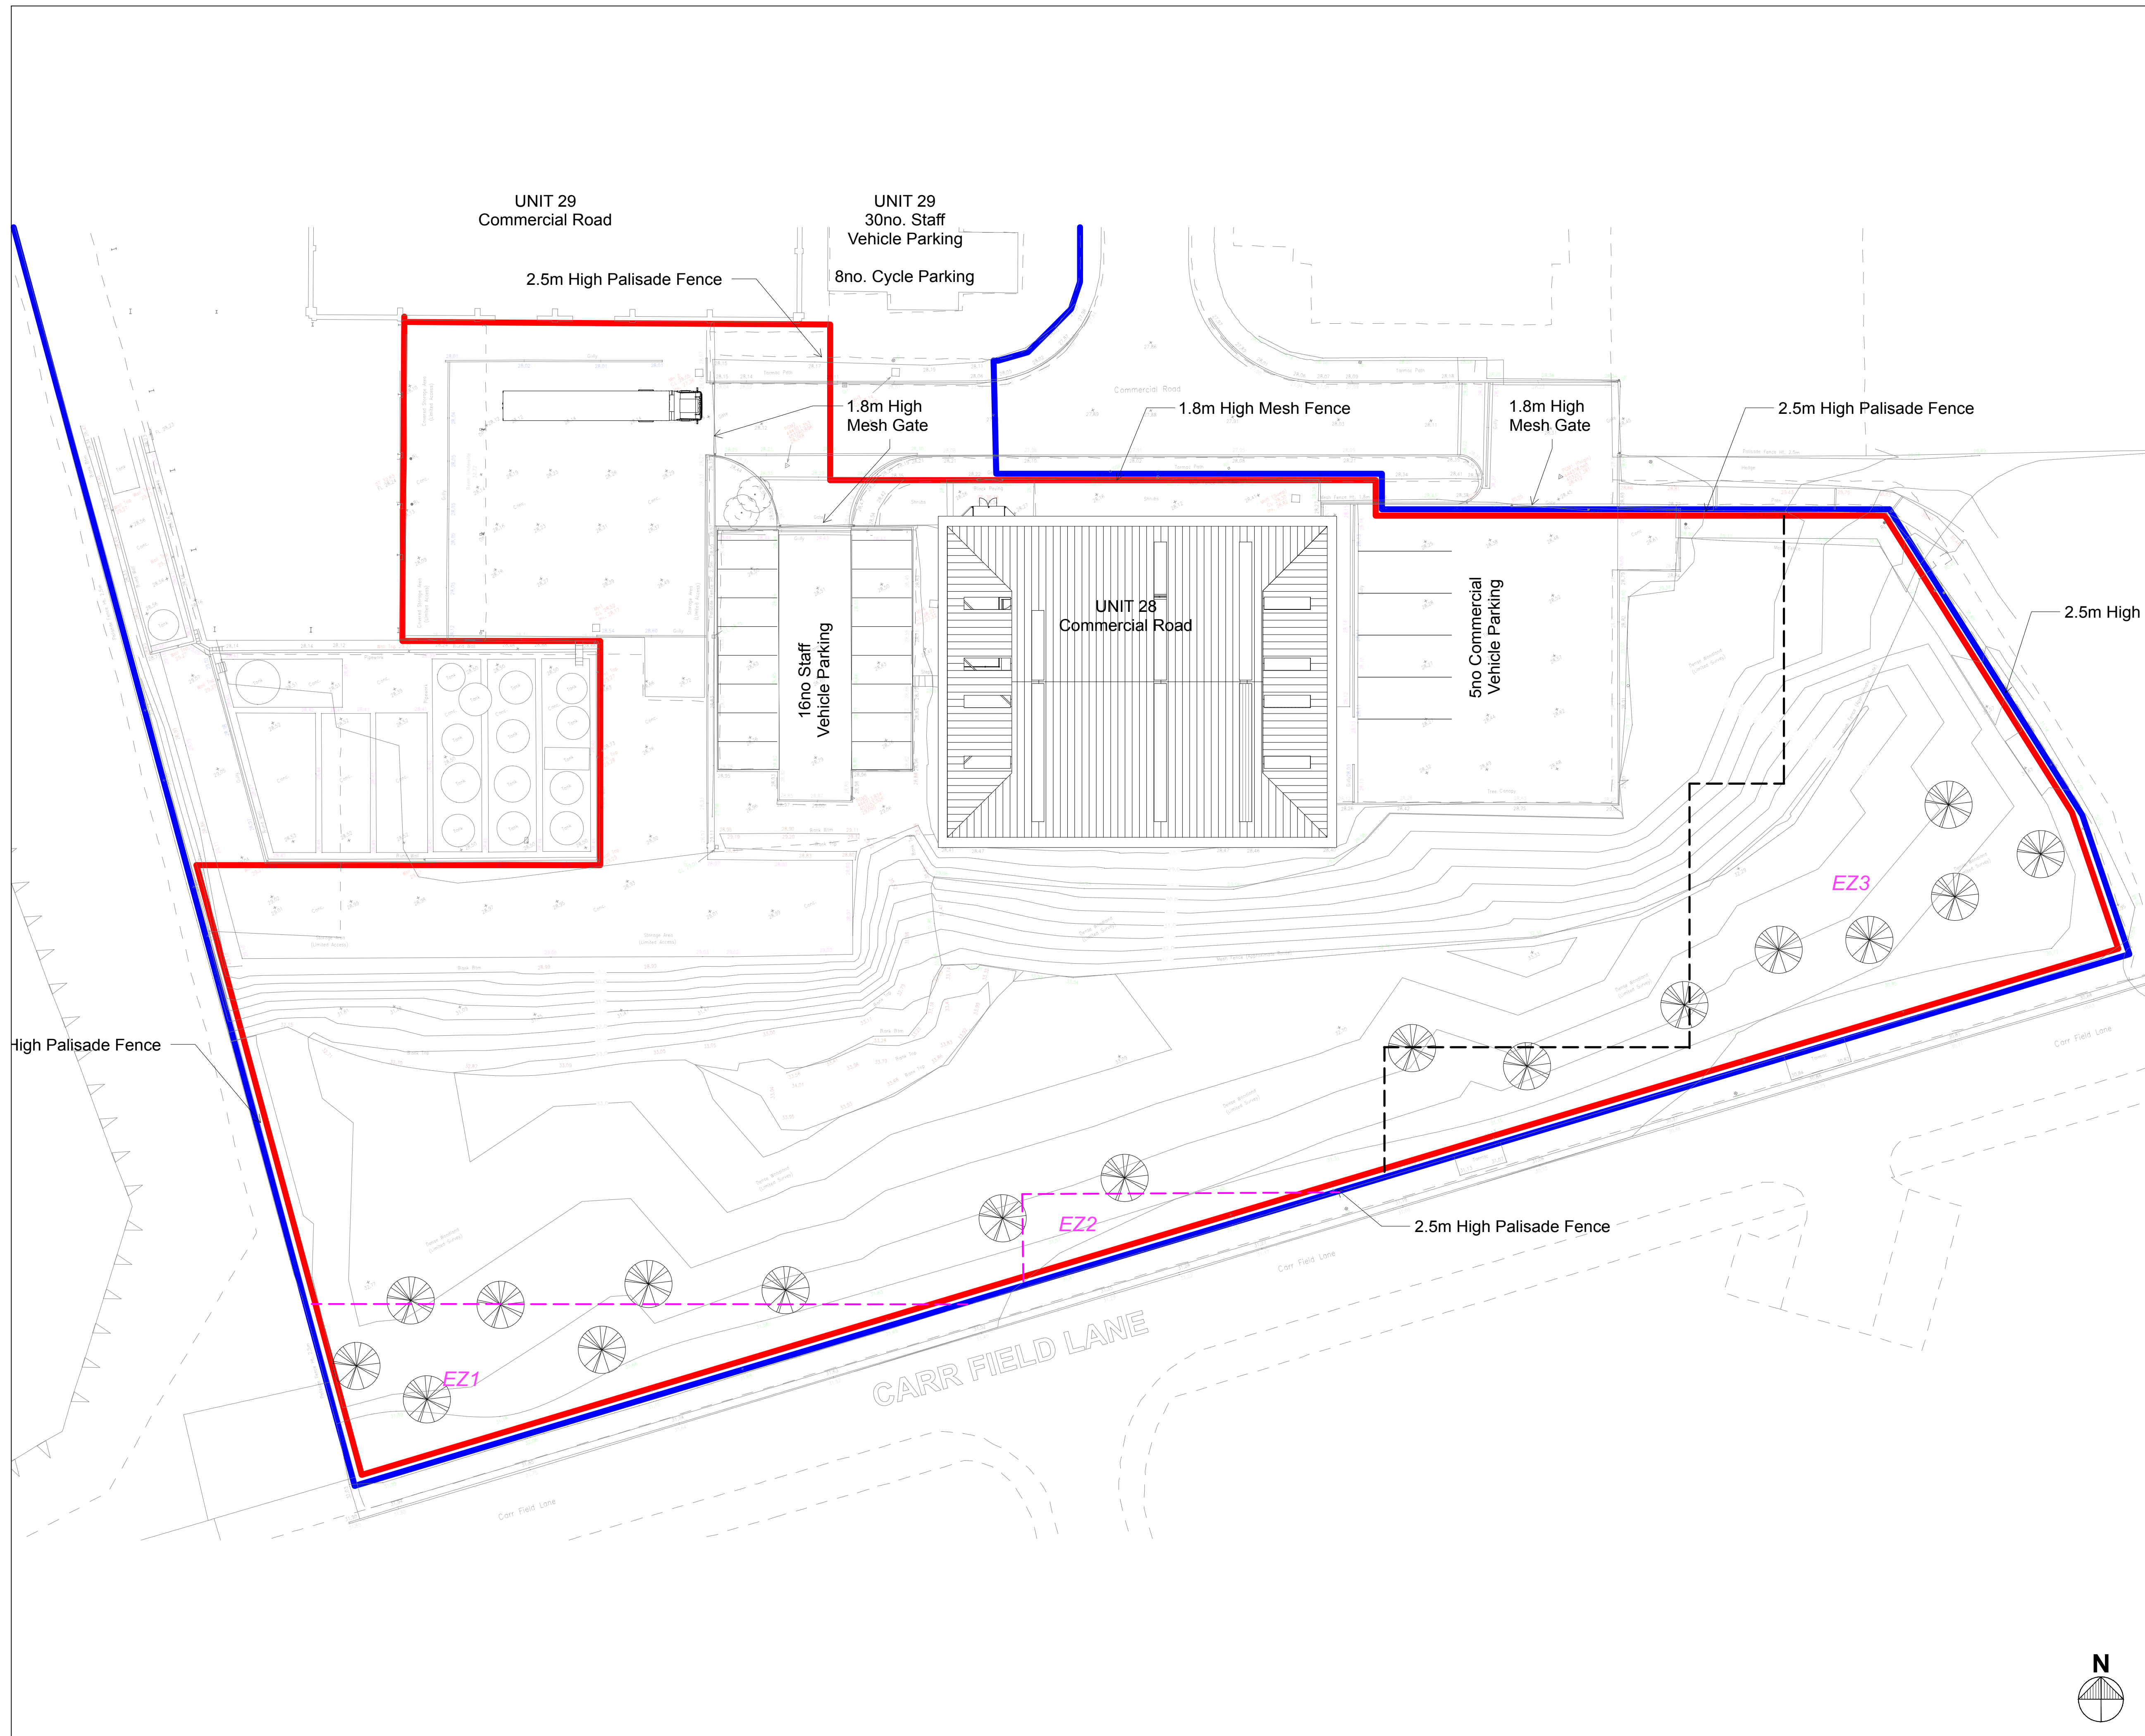


KEY- Site plan to be read in conjunction with Key Tree Solutions AMS ref: GR02-19

- Protective Barrier - BS5837 (2012), clause 6.2.2
- Construction Exclusion Zone (EZ)

|                                                                                        |                  |                     |                 |
|----------------------------------------------------------------------------------------|------------------|---------------------|-----------------|
| Site Location<br>Unit 28,<br>Goldthorpe<br>Industrial Estate,<br>Rotherham,<br>S63 9BL |                  |                     |                 |
| Job<br>Arboricultural Method Statement GR02-19                                         |                  |                     |                 |
| Title<br>Tree Protection Plan                                                          |                  |                     |                 |
| Drawn by<br>L.Smith                                                                    | Date<br>Jun 2019 | Scale @ A1<br>1:250 | Drg. no.<br>1/2 |



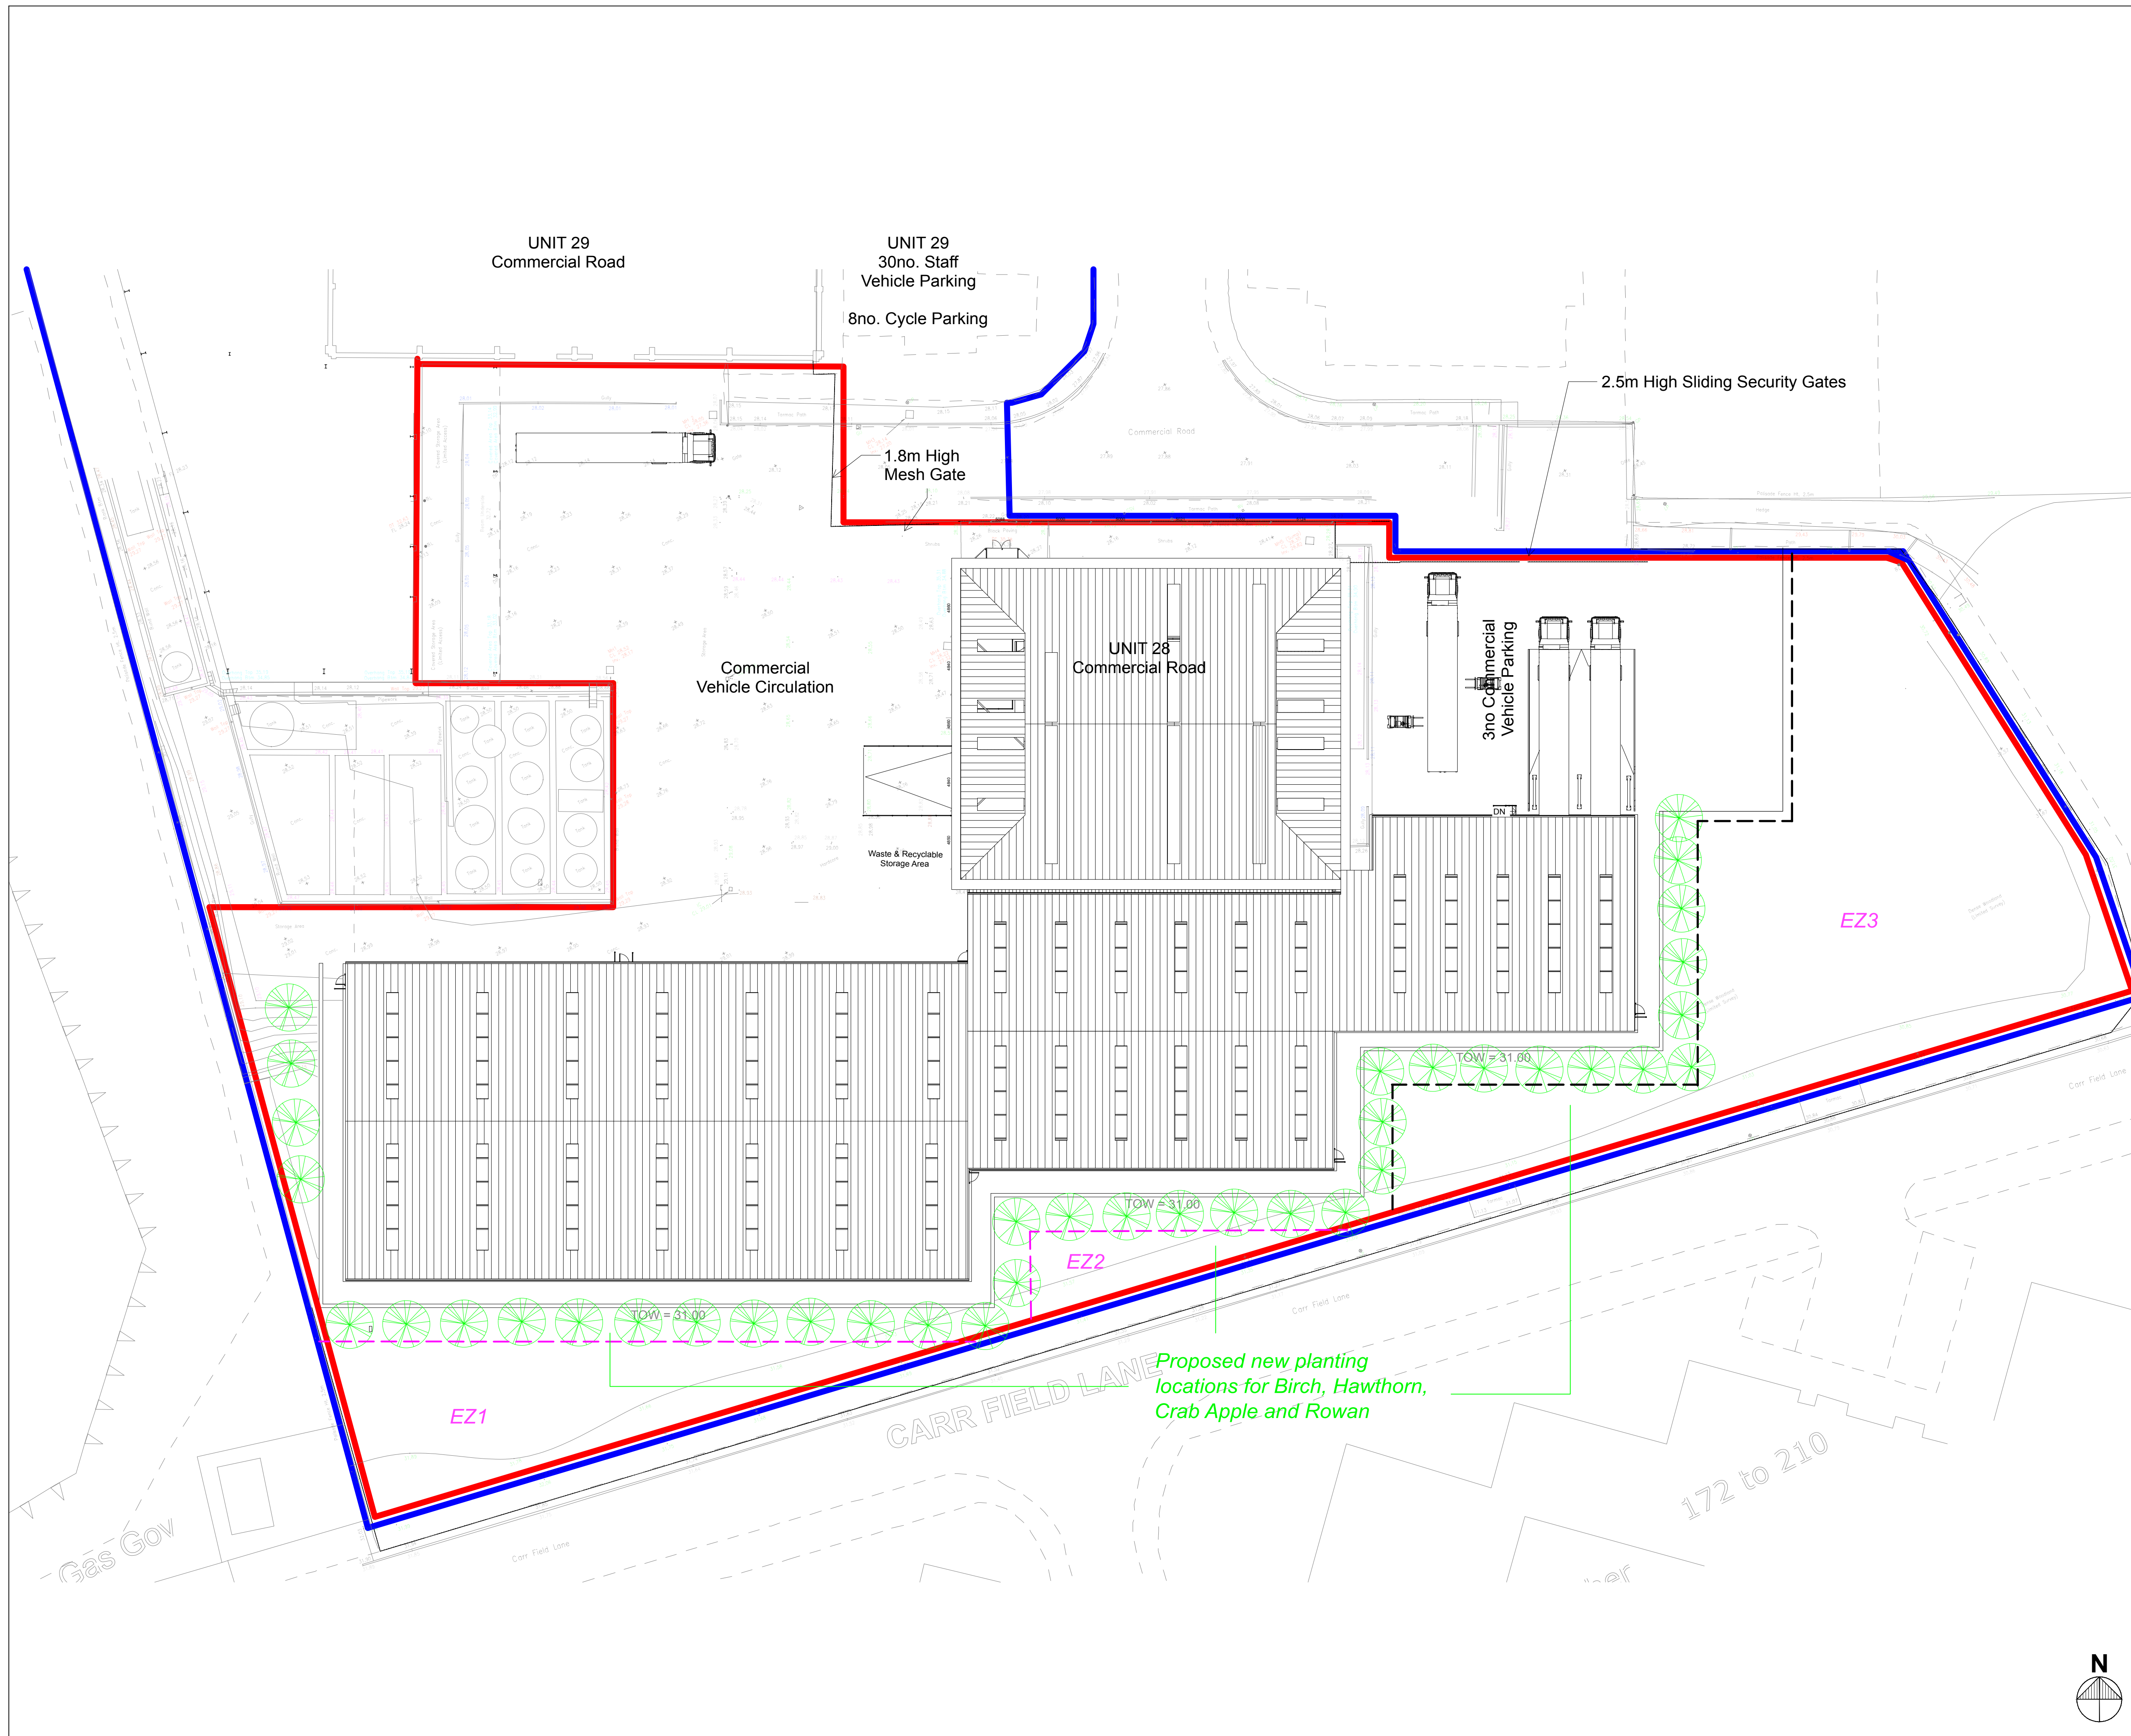

KEY- Site plan to be read in conjunction with Key Tree Solutions AMS ref: GR02-19


- Protective Barrier - BS5837 (2012), clause 6.2.2
- Construction Exclusion Zone (EZ)

|                                                                                        |                  |                     |                 |
|----------------------------------------------------------------------------------------|------------------|---------------------|-----------------|
| Site Location<br>Unit 28,<br>Goldthorpe<br>Industrial Estate,<br>Rotherham,<br>S63 9BL |                  |                     |                 |
| Job<br>Arboricultural Method Statement GR02-19                                         |                  |                     |                 |
| Title<br>New Planting Plan                                                             |                  |                     |                 |
| Drawn by<br>L.Smith                                                                    | Date<br>Jun 2019 | Scale @ A1<br>1:250 | Drg. no.<br>2/2 |



## Appendix 2: Example of Protective Barrier

The protective barrier will be installed in accordance with BS5837: 2012. The default specification of BS 5837: 2012 (pictured below for reference) recommends a vertical and horizontal, scaffold framework, well braced to resist impacts, with vertical tubes at no more than 3m intervals. These should be driven into the ground. Weld mesh panels should be affixed to this framework with scaffold clamps.

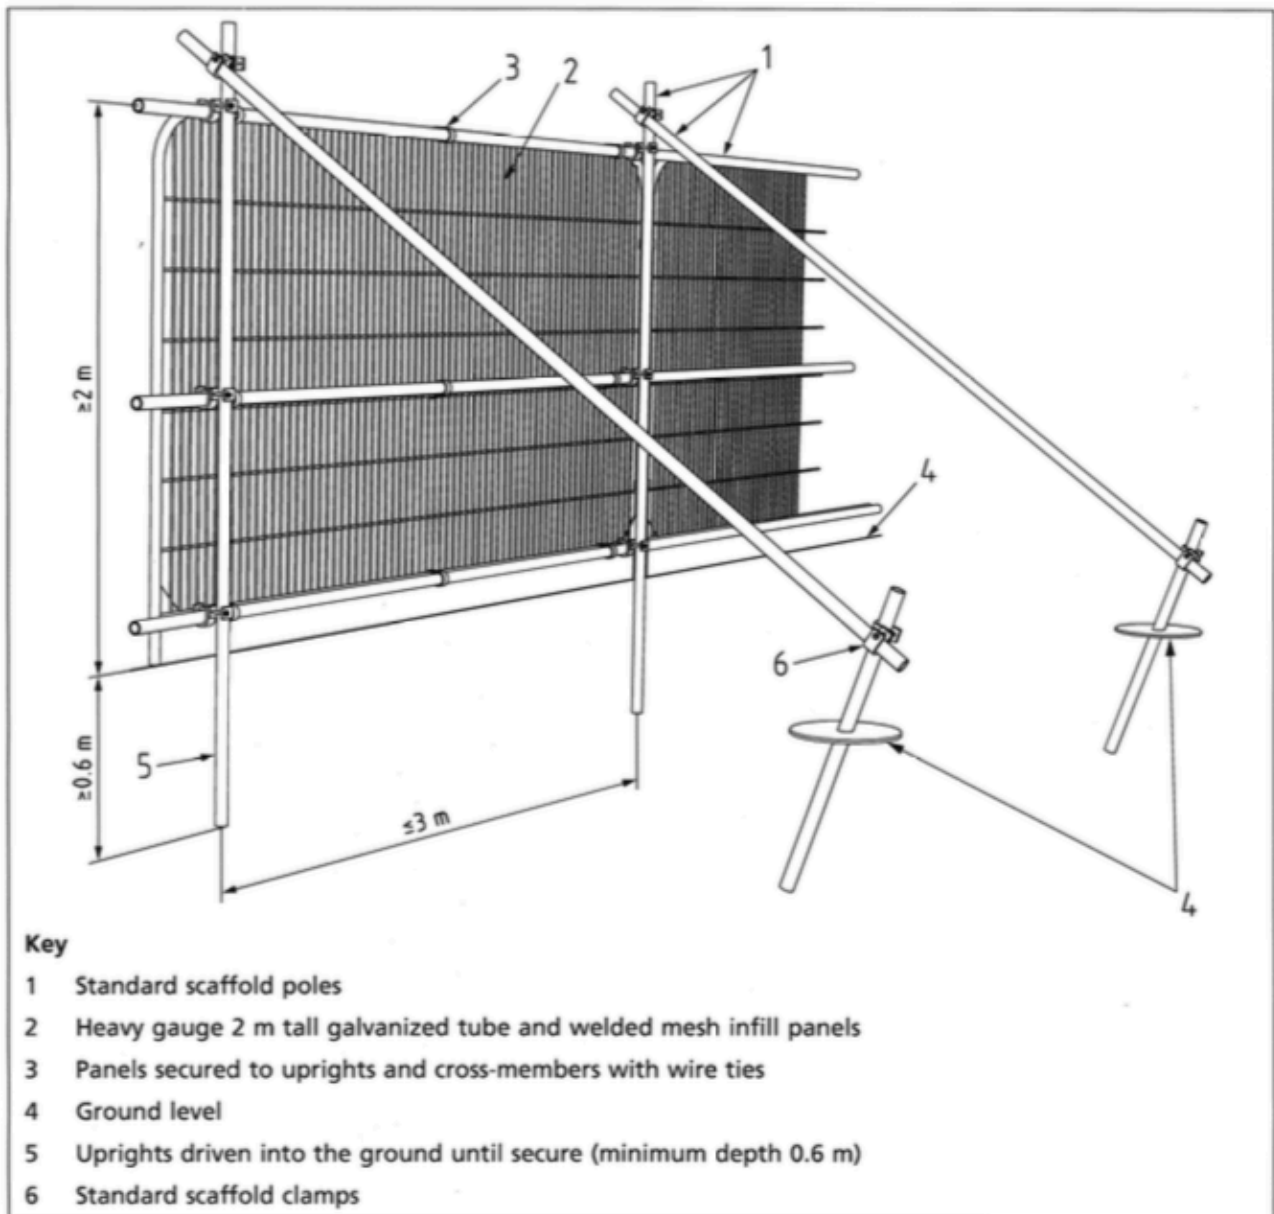

**Appendix 3: Example of Protective Barrier Notice**

**Tree Protection Zone**

**KEEP OUT**

**TREES ENCLOSED BY THIS FENCE ARE PROTECTED BY  
STRICT PLANNING CONDITIONS**

**ANY DAMAGES CAUSES TO THESE TREES MAY RESULT IN  
CRIMINAL PROSECUTION**

**RESTRICTED AREA**

**THE PROTECTIVE FENCE MUST NOT BE MOVED OR BREACHED**

**NO PERSON, MACHINERY, VEHICLE OR PLANT IS PERMITTED  
WITHIN THE TREE PROTECTION ZONE**

**NO MATERIALS SHALL BE STORED WITHIN THE TREE  
PROTECTION ZONE**

**NO EXCAVATIONS ARE PERMITTED WITHIN THE TREE  
PROTECTION ZONE**

**NO SPOIL IS TO BE DEPOSITED WITHIN THE TREE PROTECTION  
ZONE**

**NO FIRES ARE TO BE LIT WITHIN THE TREE PROTECTION ZONE**

**ANY DAMAGES MUST BE REPORTED TO THE SITE MANAGER**
