

TRAFFIC VOLUMES
Barnsley West - North (Barugh Green)

Wagon Deliveries:

Daily Average 3 - 4
 Peak 20 - 30

[Peak times will be at early stages for placing stone during road construction and end of phases for surfacing works]


Cars & Vans:

Daily average 8 to 10

NOTES

- DRAWING TO BE READ IN CONJUNCTION WITH CMP
- SUPPLIERS AND COURIERS TO BE NOTIFIED OF ROUTE TO SITE IN ADVANCE
- INCOMING AND OUTGOING ROUTES TO WORK AREAS TO BE MADE UP OF STONE / HARDCORE
- ROAD SWEEPER TO BE VISITED REGULARLY, INCREASING PRESENCE DURING PEAK DELIVERY PERIODS
- ALL DELIVERIES WILL BE MET BY A TRAFFIC MARSHALL
- COMPOUND AREA TO BE TARMAC CONSTRUCTION AND SEGREGATED WITH HOARDING
- SITE STORAGE AREA TO BE SEGREGATED WITH HERAS FENCING
- WARNING SIGNAGE TO INSTALLED AT SITE ENTRANCES
- NOTICE SIGNAGE TO BE INSTALLED PRIOR TO TRAFFIC MANAGEMENT SETUP
- PROPOSED CONSTRUCTION AREAS TO BE UTILIZED FOR MATERIAL STORAGE & VEHICLE MANEUVERING WHERE FEASIBLE
- ACCESS TO SITE VIA M1 JNC 38 VIA A637 SUPPLIERS TO BE NOTIFIED OF ROUTE TO SITE
- ROAD CLOSURES TO BE PUT IN PLACE DURING FINAL SURFACING WORKS AT TIE-IN AREAS

KEY

 PHASE 3 CONSTRUCTION AREA

Revision	By	Date
0	For Information	CY 03/08/2023
A		
B		
C		

CORE Special Projects Earthworks Remediation Infrastructure

Core Special Projects Limited
 2175 Century Way
 Thorpe Park
 Leeds LS15 8ZB

Tel: +44 (0)113 232 8000
 Fax: +44 (0)113 232 8001
 E-mail: mail@coresp.co.uk
www.coresp.co.uk


Project:
 Barnsley West S278 - North

Title:
 Construction Phase Traffic Management Plan
 North Roundabout Phase 3

Drawing No: 001(1)
Revision: 0

Drawn By: CY
Approved By: LF

Scale: 1:250
Date: 03 Aug 2023
Sheet Size: A1

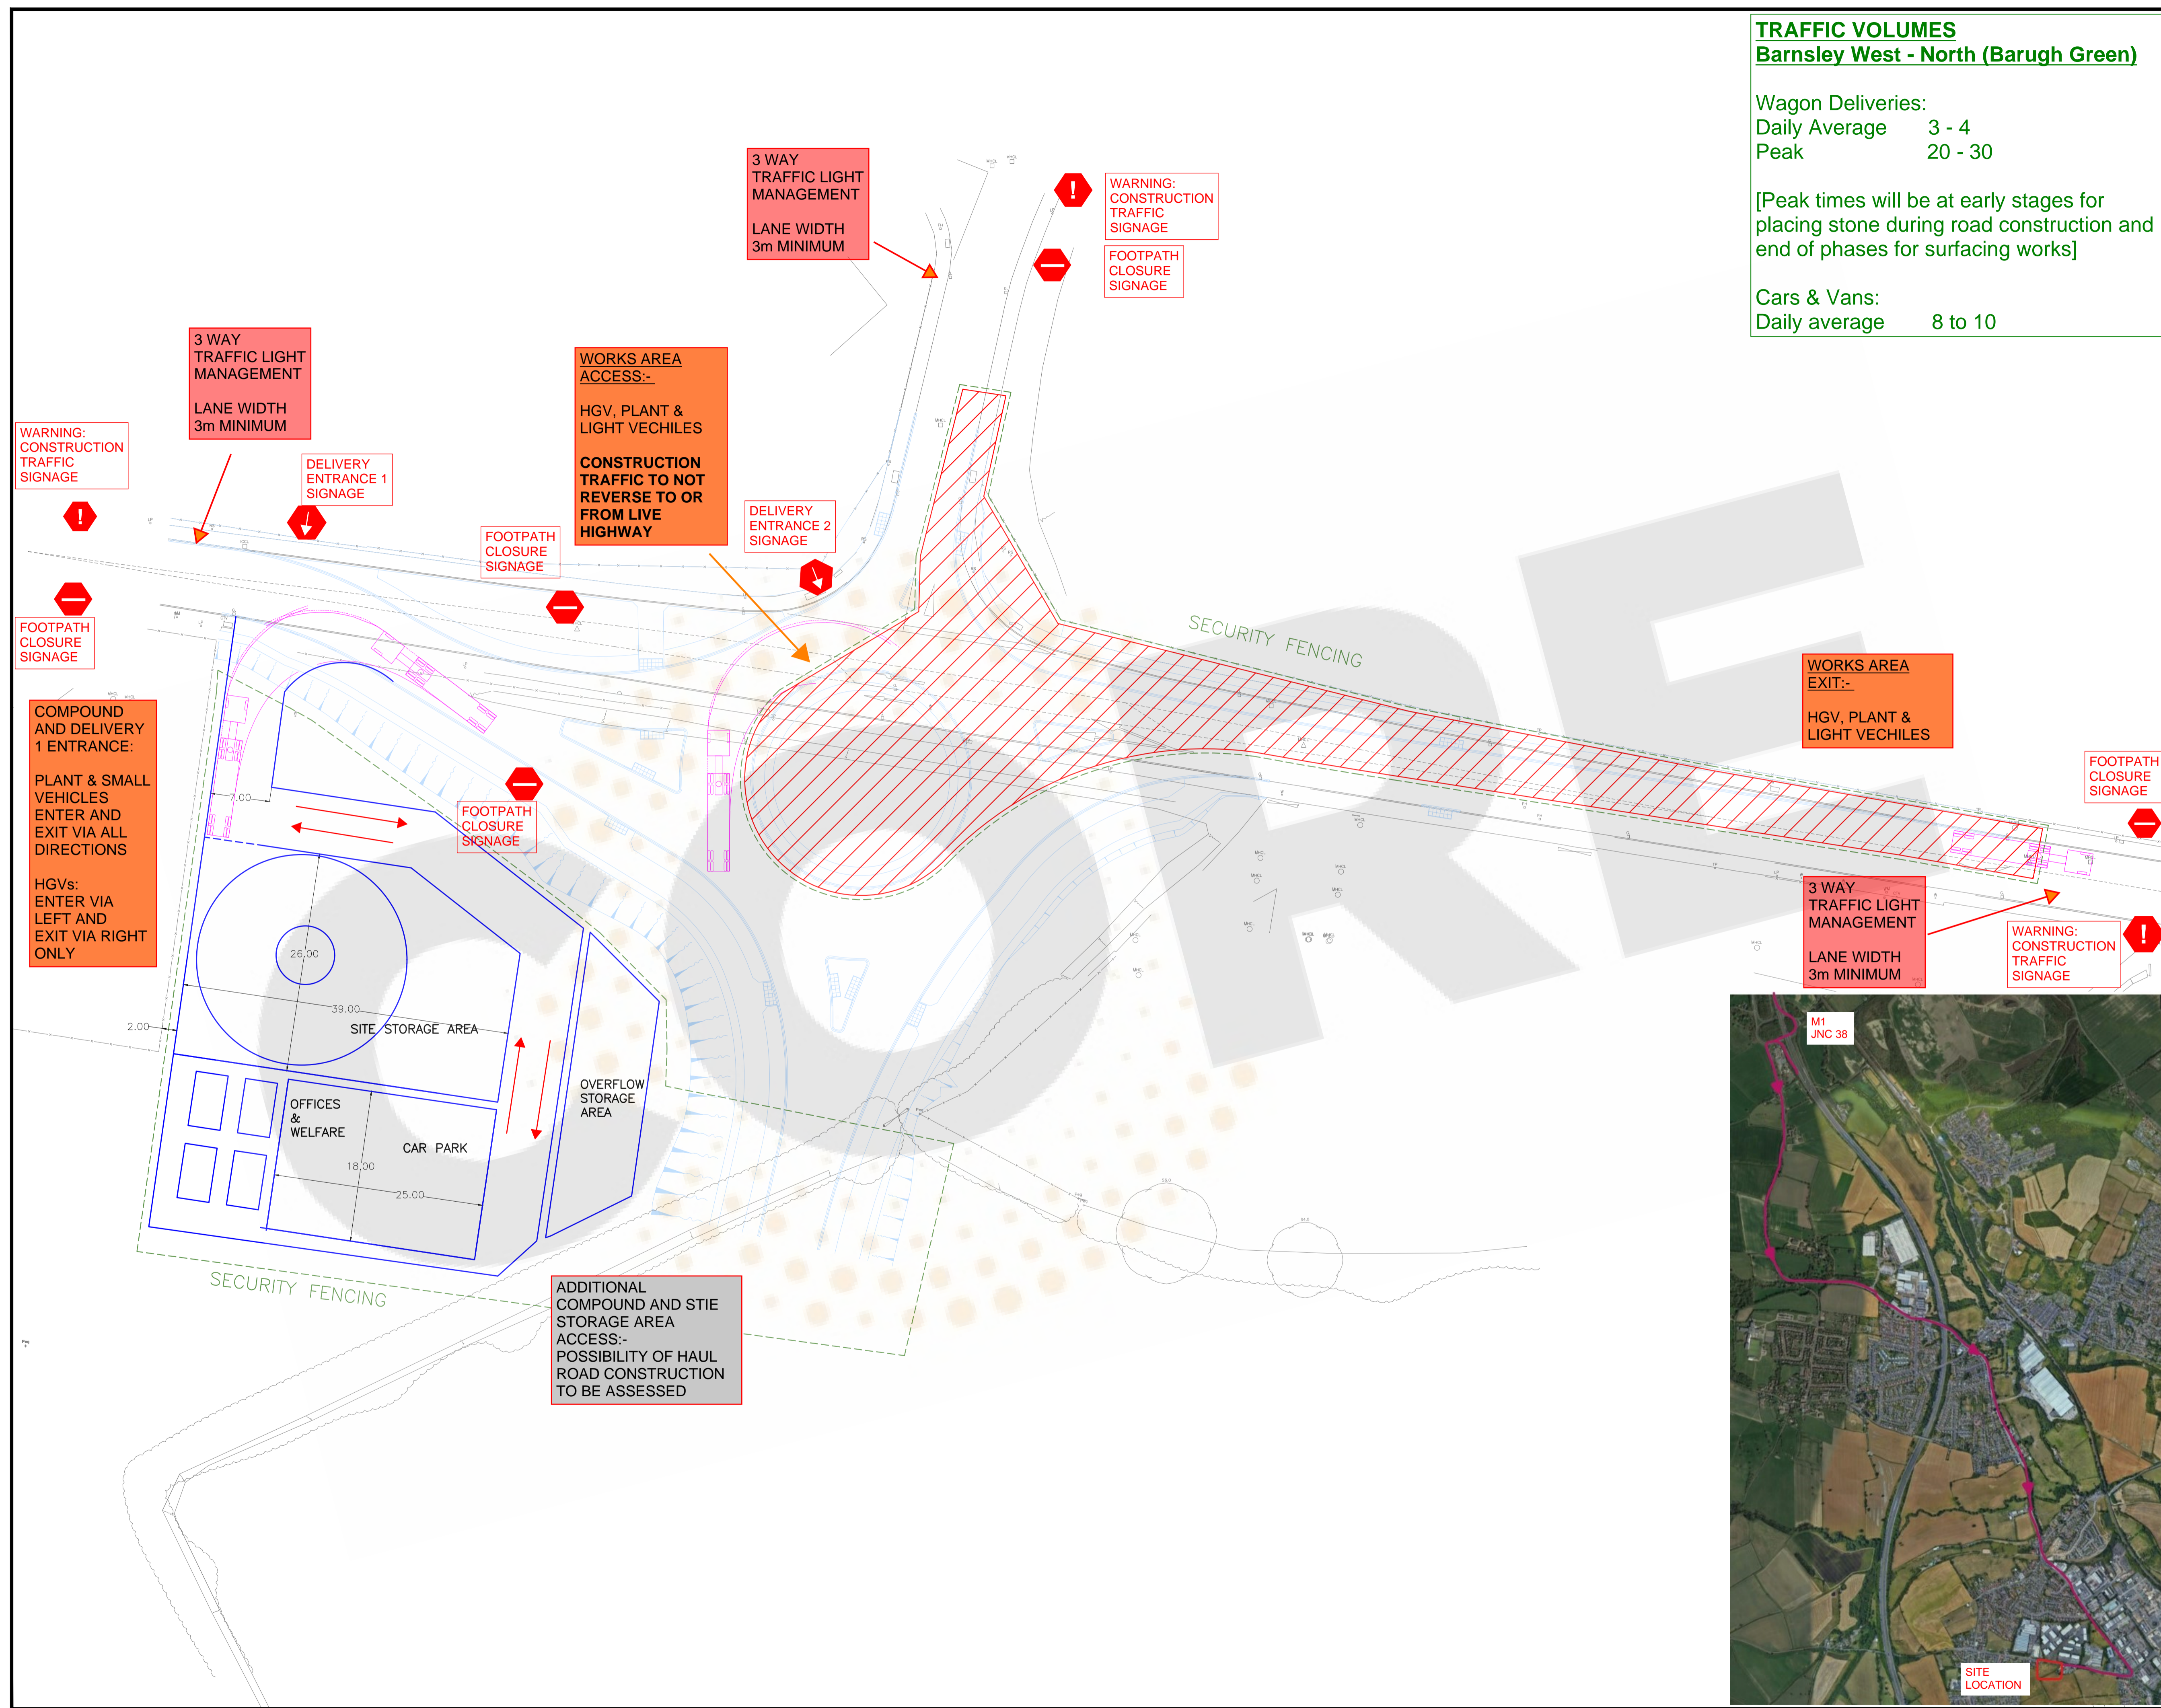

WARNING: CONSTRUCTION TRAFFIC SIGNAGE

FOOTPATH CLOSURE SIGNAGE

COMPOUND AND DELIVERY 1 ENTRANCE:
 PLANT & SMALL VEHICLES ENTER AND EXIT VIA ALL DIRECTIONS
 HGVs: ENTER VIA LEFT AND EXIT VIA RIGHT ONLY

3 WAY TRAFFIC LIGHT MANAGEMENT
 LANE WIDTH 3m MINIMUM

DELIVERY ENTRANCE 1 SIGNAGE

FOOTPATH CLOSURE SIGNAGE

WORKS AREA ACCESS:-
 HGV, PLANT & LIGHT VEHICLES
 CONSTRUCTION TRAFFIC TO NOT REVERSE TO OR FROM LIVE HIGHWAY

DELIVERY ENTRANCE 2 SIGNAGE

3 WAY TRAFFIC LIGHT MANAGEMENT
 LANE WIDTH 3m MINIMUM

WARNING: CONSTRUCTION TRAFFIC SIGNAGE

FOOTPATH CLOSURE SIGNAGE

WORKS AREA EXIT:-
 HGV, PLANT & LIGHT VEHICLES

FOOTPATH CLOSURE SIGNAGE

3 WAY TRAFFIC LIGHT MANAGEMENT
 LANE WIDTH 3m MINIMUM

WARNING: CONSTRUCTION TRAFFIC SIGNAGE

ADDITIONAL COMPOUND AND STIE STORAGE AREA ACCESS:-
 POSSIBILITY OF HAUL ROAD CONSTRUCTION TO BE ASSESSED
