



ARBORICULTURAL METHOD STATEMENT

to BS 5837:2012 at:

***Barnsley Hospital Education Centre,
Gawber Road,
Barnsley
S75 2EP***

This document describes how the trees will be protected and managed during the development of this site. It explains how and when the protection measures must be installed and maintained throughout the development.

A copy of this document report must be permanently available on site for the duration of all development activity and should be referenced for practical guidance on how to protect the retained trees at this site.

Prepared for:
JTP Architects

Date: *November 2024*

Reference: *AWA6328AMS*

*TMP006 – D
Template Revision 01
Auth By: APW
Date: 09/09/2024*



Contents

- 1. INTRODUCTION 3**
- 2. METHOD STATEMENT TIMELINE..... 5**
- 3. TREE MANAGEMENT..... 7**
- 4. TREE PROTECTION..... 7**
- 5. WORKS CLOSE TO RETAINED TREES 8**
- 6. SIGNATURE 10**

- APPENDIX 1: IMAGES AND FIGURES 11**
- APPENDIX 2: RELEVANT CONTACT DETAILS 14**
- APPENDIX 3: TREE DATA AND WORKS SCHEDULE 15**
- APPENDIX 4: TREE PROTECTION PLAN 16**

1. Introduction

1.1 Instruction

1.1.1 We were instructed by JTP Architects to prepare an arboricultural method statement for the proposed development at Barnsley Hospital Education Centre, Gawber Road, Barnsley.

1.2 Purpose

1.2.1 This method statement has been prepared in order to demonstrate that the development operations at this site can be undertaken with minimal risk of adverse impact on the trees to be retained.

1.2.2 This method statement conforms to BS 5837:2012 *Trees in relation to design, demolition and construction - Recommendations*. It is based on the arboricultural data, collected at a site visit during November 2024, detailed within Appendix 3 of this report.

1.3 Description of Development

1.3.1 It is proposed to build an extension to the existing building. The proposed development layout has been provided by my client and is the basis for the Tree Protection Plan at Appendix 4.

1.4 Details of Consent

1.4.1 Planning consent is subject to this method statement being agreed upon in advance by the Local Planning Authority. The contents of this report must be adhered to, before, during, and after the construction phase.

1.4.2 As such, no equipment, machinery or materials shall be brought onto the site in connection with the development until this arboricultural method statement detailing tree management and tree protection measures has been submitted to and approved by the Local Planning Authority.

1.5 Legal

- 1.5.1 The following advice is for guidance purposes only. Some trees are protected by legislation, and it is essential that the legal status of trees is established prior to carrying out works to them.
- 1.5.2 Unauthorised work to protected trees could lead to prosecution, resulting in enforcement action such as fines or a criminal record. Tree Preservation Orders, Conservation Areas, Planning Conditions, Felling Licences or Restrictive Covenants legally protect many trees in the UK.
- 1.5.3 An online search was undertaken with Barnsley Metropolitan Borough Council on 07/11/24 to check whether any trees at the site are protected by a Tree Preservation Order or are located within a Conservation Area. As of this date no trees at the site are protected by a Tree Preservation Order or are within a Conservation Area.
- 1.5.4 Due to the large potential penalties for illegally carrying out work to protected trees, before authorising any tree works a further check should be made with the Local Planning Authority to confirm if any trees are covered by a Tree Preservation Order or are within a Conservation Area. If either applies, then statutory permission is required before any works can take place (unless such work is approved as part of full planning permission).
- 1.5.5 The Multi-Agency Geographical Information for the Countryside (MAGIC) website was used to search for areas of ancient woodlands listed on the Ancient Woodland (DEFRA 2024), and a check for catalogued Ancient and Veteran trees using the woodland trust ancient tree inventory (ATI) (Woodland Trust 2024).
- 1.5.6 It was confirmed that there are no designated ancient woodlands or veteran or ancient trees within the survey area.
- 1.5.7 Trees provide a wide range of habitats for many species, some of which are legally protected such as bats, nesting birds, badgers and dormice. It is essential that appropriate care is taken to ensure that this legislation is not contravened.
- 1.5.8 When appointing a tree surgeon, only properly qualified and experienced companies should be used, who have adequate Public Liability and Employer's Liability Insurance.
- 1.5.9 All tree work should be carried out according to British Standard 3998:2010 Tree Work - Recommendations.

2. Method Statement Timeline

2.1 Overview of Sequence of Operations

2.1.1 In overview, it is necessary to undertake the following sequence of operations in relation to arboricultural input for development operations.

- 1 Method statement approved by the LPA
- 2 Undertake tree removal
- 3 Install tree protection fencing
- 4 Pre commencement meeting/ confirm fencing is as specified
- 5 Construct new development
- 6 Remove tree protection fencing

2.2 Specific Sequence of Operations

2.2.1 The following timeline table informs the key principles for development operations proceeding in relation to arboricultural requirements conditioned as part of this method statement.

2.2.2 The actions and timescales within this table must be adhered to in order to discharge the arboricultural method statement planning condition for this site.

2.2.3 The precise timing and order of some of the development operations may need to be changed due to site specific operational requirements, yet any operations that may affect the trees on the site must be done so under arboricultural supervision by a suitably qualified person appointed by the contractor.

Sequence of Operations		
Stages	Action	Arboricultural Input
1 Approval	This AMS is submitted to and approved in writing by the LPA.	If necessary, liaise with contractor and LPA to discuss methodologies detailed.
2 Tree Works	Tree removals and pruning works shall be carried out as the first operation on site, in accordance with Appendix 3 and as detailed in section 3.1.	Review the tree work requirements with the tree contractor. If necessary, liaise with the contractor on site during tree works.
3 Tree Protection	Installation of the tree protection fencing will take place as shown at Appendix 4, prior to any storage of plant, materials and machinery.	If necessary, liaise with the contractor installing the tree protection fencing until completed to the standard specified in this method statement.
4 Site Meeting	Following installation of tree protection fencing, the LPA shall be invited to inspect the fencing and tree works and discuss any other site operations that have implications for trees.	Meeting with a representative of the LPA and the site manager. Alternatively, contractor can confirm the fencing and tree works are as specified by taking photographs.
5 Construction	Undertake the construction of the new development.	If necessary, liaise with the local authority and the site foreman to ensure any issues are adequately resolved.
6 Site Finishing	Removal of tree protection fencing must only be undertaken when all site traffic and machinery has left the site.	If acceptable to the LPA, the contractor can take photographs of the site to give to the LPA to gain approval for the removal of the tree protection fencing.

3. Tree Management

3.1 Tree Works

- 3.1.1 Cherry T1 requires removal as it is situated within the footprint of the proposed extension.
- 3.1.1 The tree requiring removal is highlighted in red on the Tree Works Protection at Appendix 4 and is detailed in the Tree Data and Works Schedule at Appendix 3.
- 3.1.2 All tree work must be carried out according to British Standard 3998:2010 Tree Work - Recommendations.
- 3.1.3 When appointing a tree surgeon, only properly qualified and experienced companies should be used, who have adequate Public Liability and Employer's Liability Insurance.

4. Tree Protection

4.1 Tree Protection Fencing

- 4.1.1 The tree protection fencing for this site should be located as shown on the Tree Protection Plan at Appendix 4 (as illustrated with a thick purple line).
- 4.1.2 The tree protection fencing will be appropriate to the degree and proximity of likely construction works. In this instance, it is suggested that the most suitable protection for the trees could be provided by secured 'Heras' type fencing, of welded mesh panels on rubber or concrete feet (see Figures 1 and 2 at Appendix 1 for examples).
- 4.1.3 The precise fencing location may need to be slightly adjusted on site due to local site conditions but is not expected to differ from that shown on the Tree Protection Plan. The final fencing position must be agreed on by the LPA before the commencement of any site works.
- 4.1.4 The tree protection fencing details should be incorporated into relevant subsequent plans, method statements used for design purposes and construction drawings issued for use on site, to ensure that all interested parties are fully aware of the areas in which access

and works may and may not take place.

- 4.1.5 The fencing should be joined together using a minimum of two anti-tamper couplers, installed so that they can only be removed from inside the fence (see Figure 3 at Appendix 1 for an example). The fencing panels should be supported on the inner side by stabilizer struts, which should normally be attached to a base plate secured with ground pins or mounted on a block tray (see Figures 1 and 2 at Appendix 1 for examples).
- 4.1.6 The area enclosed by the fencing is referred to as the Construction Exclusion Zone (CEZ); this area should be considered a restricted area. No pedestrians, vehicles, storage of materials, equipment or machinery should be allowed within the CEZ unless specified in this method statement. The site manager must ensure that all personnel are aware of the restrictions that apply to the fenced-off area.
- 4.1.7 Once the fencing is erected, waterproof warning signs labelled 'Tree Protection Area' should be placed at 3m intervals to ensure that all personnel are aware of the restrictions that apply to the fenced-off area (see Figures 4 and 5 at Appendix 1 for example signs).
- 4.1.8 The tree protection fencing should be inspected for faults or damage by the site manager or other responsible named person on a regular basis and a written record kept. Any faults or defects should be repaired or replaced as soon as is reasonably practicable. The Tree Protection Fencing shall not be removed, breached or altered without prior written authorisation from the local planning authority and under arboricultural supervision by a suitable named responsible individual appointed by the site manager.

5. Works Close To Retained Trees

5.1 Drainage and Utilities

- 5.1.1 New drainage and underground utilities are to be positioned outside of the RPAs of retained trees, and above ground utilities will be routed away from areas where they are likely to interfere with the retained trees' crowns.
- 5.1.2 NJUG 10: Guidelines for the Planning, Installation and Maintenance of

Utility Services in Proximity to Trees should be considered when installing services.

5.2 Additional Precautions

- 5.2.1 Allowance should be made for operations outside of the CEZ that could indirectly impact on trees. Including space for site huts, temporary toilet facilities (including their drainage) and other temporary structures; and space for storing (whether temporary or long-term) materials.
- 5.2.2 Care must be taken to prevent contamination with chemical spillages, including petrol, diesel and oils. Cement mixers and any other toxic materials should not be permitted within the RPA of the trees. Any materials whose accidental spillage would cause damage to a tree should be stored and handled well away from the outer edge of its RPA.
- 5.2.3 Fires on the site should be avoided if possible. Where they are unavoidable, and approved by the Local environmental health authority, they should not be lit in a position where heat could affect foliage or branches. The potential size of a fire and the wind direction should be considered when determining its location, and it should be attended always until safe enough to leave.

5.3 Post Construction Landscaping

- 5.3.1 Many of the trees on site may be subject to some form of landscaping or seeding beneath their canopies after the development phase. At this stage the protective fencing will have been removed and the property may be occupied.
- 5.3.2 Landscaping works should be carried out in such a way as to avoid ground level changes or deep digging. Tractor mounted rotovation or other mechanised cultivation methods must not be used.
- 5.3.3 No heavy machinery should be brought into the vicinity of retained trees.
- 5.3.4 Herbicides should be appropriate for the purpose and should not be used in such a way as to damage any retained trees or vegetation.

6. Signature

I trust this report provides all the required information.

Signed



.....

Adam Winson
Chartered Arboriculturist, MSc, BSc (Hons), MICFor, AIEEM

15th November 2024

AWA Tree Consultants Limited
Union Forge
27 Mowbray Street
Sheffield
S3 8EN

www.awatrees.com

Appendix 1: Images and Figures

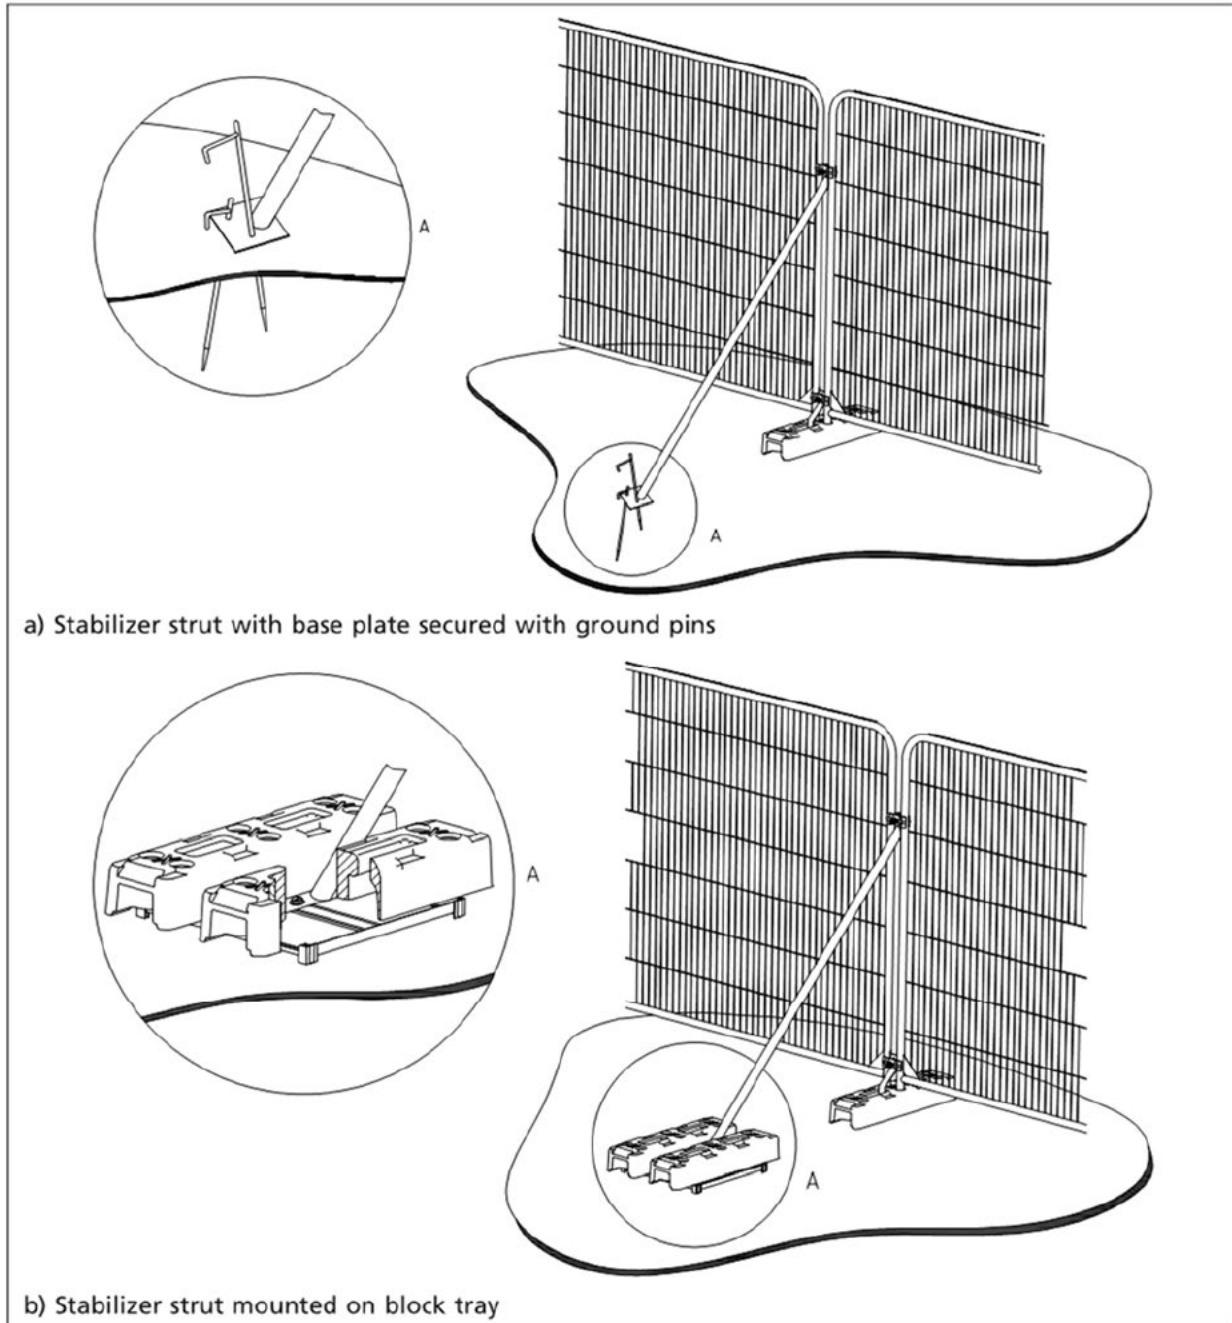


Figure 1: Secured 'Heras' type fencing with stabilizing system and fixed central pins (©BSI)



Figure 2: Secured 'Heras' type fencing with stabilizing system and anti-tamper couplers



Figure 3: Anti-tamper couplers to secure fencing and avoid unauthorised access



Figure 4: Warning sign for fencing

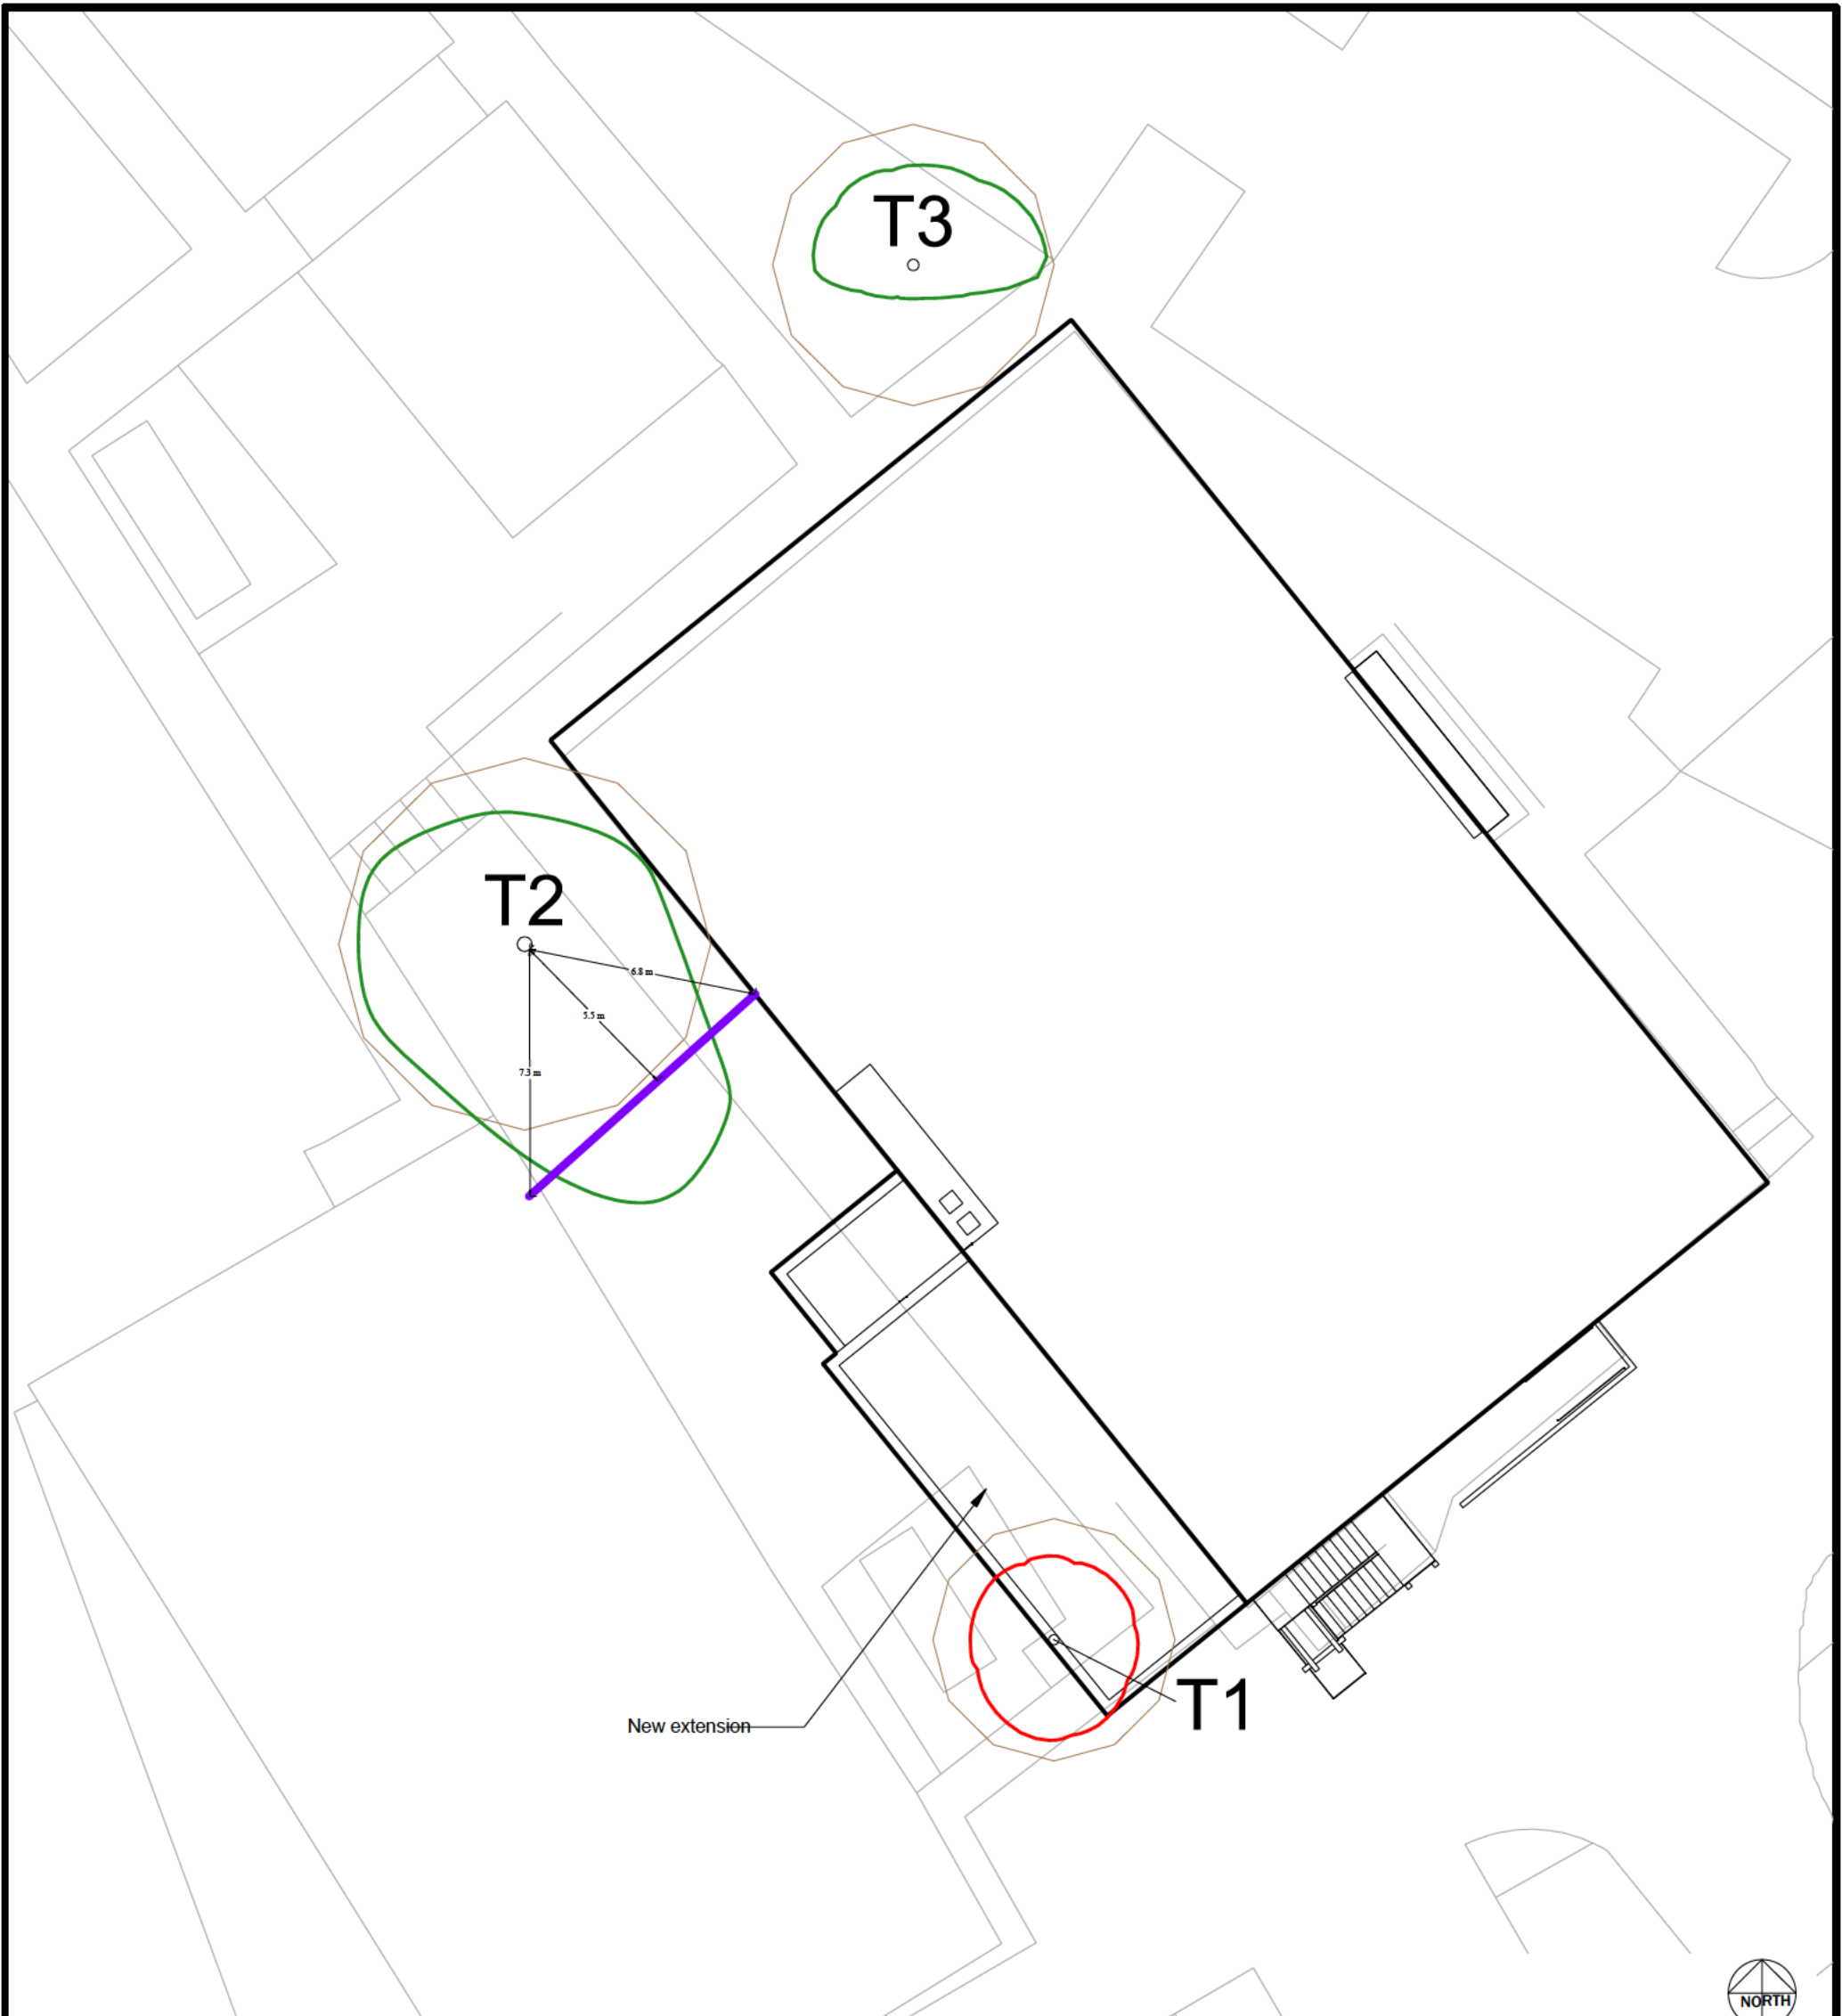


Figure 5: Example of A3 correx tree protection warning sign fixed to fencing panel


Appendix 2: Relevant Contact Details

Contact Name	Organisation/ Details	Contact Number	Contact E-mail
Michael Brown	JTP Architects	0114 270 0208	michaelbrown@jamestotty-partnership.co.uk
Adam Winson	AWA Tree Consultants Ltd	0114 272 1124	adam@awatrees.com
Edward Jowett	Barnsley Metropolitan Borough Council	01226 772 557	edwardjowett@barnsley.gov.uk

Tree ID	Tree Species		Maturity	Measurements				Crown (m)				Tree Condition				Value			Management			
	Common Name	Latin Name		Height (m)	Stems	Stem Diameter (mm)	Estimated	Crown height	N	E	S	W	Roots	Stem	Crown	Comments	Physiological	Structural	Life Expectancy	Amenity	Category	Works
T1	Cherry	<i>Prunus sp.</i>	Early-mature	7	5	120	No	2	2.5	2.5	3	2.5	No visual defects	Multiple stemmed at 1m, Slight lean, Old pruning wounds, Minor decay	Minor deadwood, Old pruning wounds	Surrounded by hard standing to south, east and west. Leaning south. Multiple pruning wounds. Previous reduction works to crown.	Good	Good	20 to 40 yrs	Moderate	C	Removal required to facilitate development
T2	Cherry	<i>Prunus sp.</i>	Early-mature	8	1	450	No	2	4	4.5	5.5	6	Exposed roots, Girdled roots, Bark damage, Bleeds, Suckers	Single stemmed, Vertical, Epicormic growths, Tight unions	Minor deadwood, Old pruning wounds	Large, exposed roots with historic bark damage. Suckers. Tight unions within crown. Included bark. Pruning wounds throughout crown. On slight banking which slopes down south to north. Bleeds. Close to contact with building.	Good	Good	10 to 20 yrs	Moderate	C	No works required
T3	Birch	<i>Betula pendula</i>	Semi-mature	13	1	340	No	3	3	4	1	3	Exposed roots, Bark damage	Single stemmed, Slight lean, Old pruning wounds, Epicormic growths	Minor deadwood	Slight lean to northwest. Crown in contact with lamppost to northeast.	Good	Good	20 to 40 yrs	Moderate	B	No works required



Heras tree protection fencing

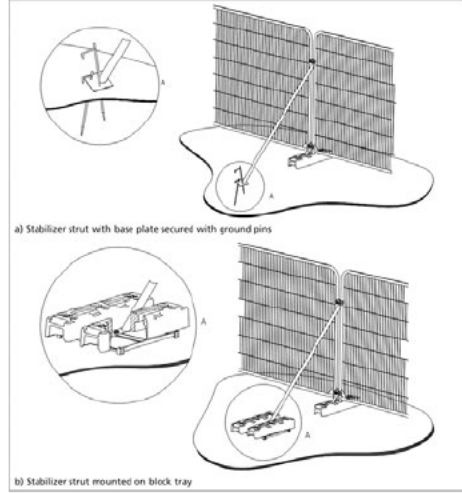

Heras tree protection fencing



Warning sign for fencing



**Appendix 5:
Tree Protection Plan**

Barnsley Hospital Education Centre, Gawber Road
Ref: AWA6328AMS

BRITISH STANDARD 5837:2012

SCALE: 1:200

PAPER: A3

	TREE/ TREE GROUP/ HEDGE TO BE RETAINED
	TREE/ TREE GROUP/ HEDGE TO BE REMOVED
	RPA: ROOT PROTECTION AREA
	TREE STEM
	TREE PROTECTION FENCING
