


Access to site is from the A6133 on to Keresforth Close. Access for residents will be maintained at all times and no site deliveries will be permitted between 6pm and 8am

Priority buildings to be demolished to enable mine grouting works to commence

Site made secure with perimeter fencing, existing fencing used where suitable

Temporary site compound & welfare facilities located on existing car park

Buildings to be demolished highlighted red

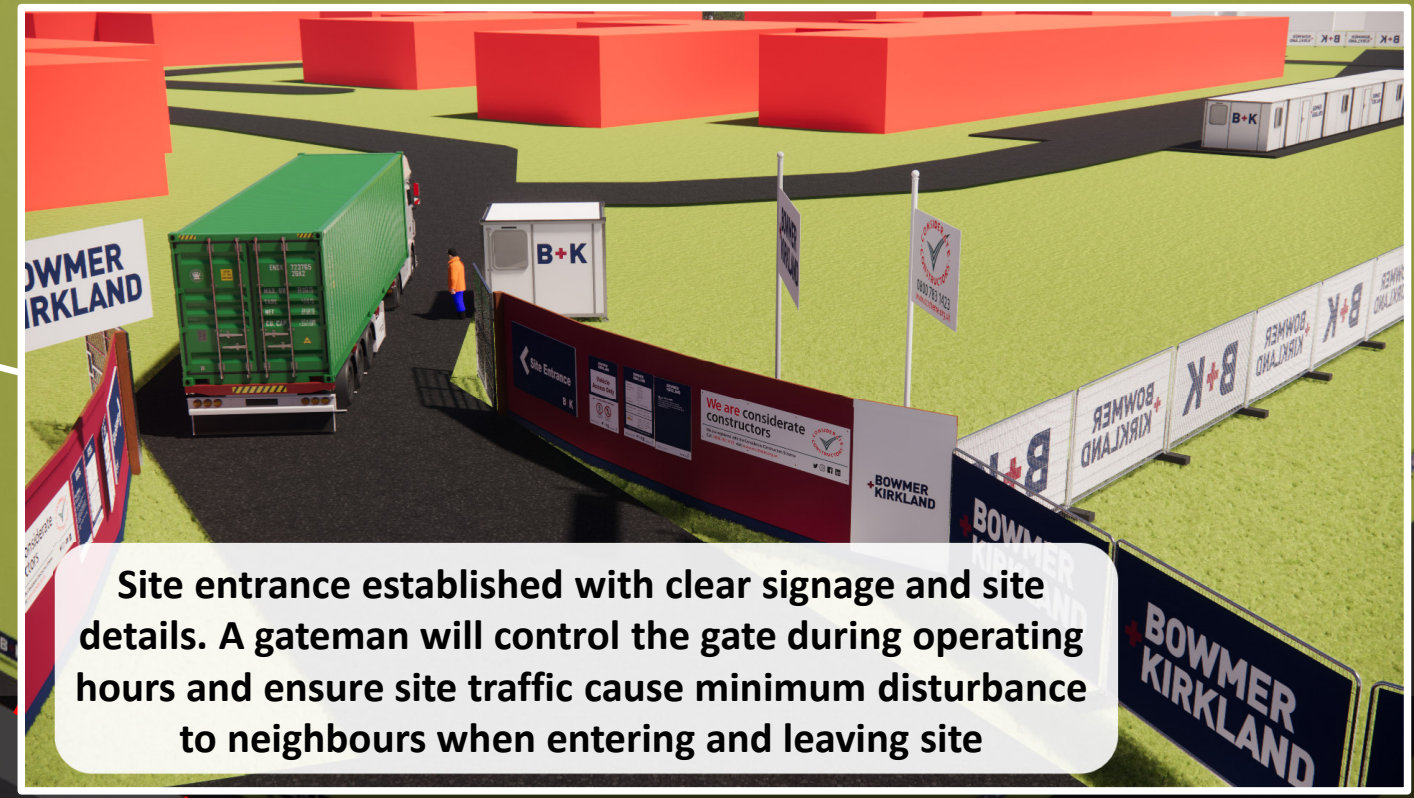


Site entrance established with clear signage and site details. A gateman will control the gate during operating hours and ensure site traffic cause minimum disturbance to neighbours when entering and leaving site

Site Logistics Plan 1 (Weeks -28 to -11)

Site Establishment, R+D Surveys, Disconnections & Demolition

Demolition of buildings continue, crushed demolition material is spread to form working platforms for construction phase

Mine grouting works commence and continue until start of construction phase

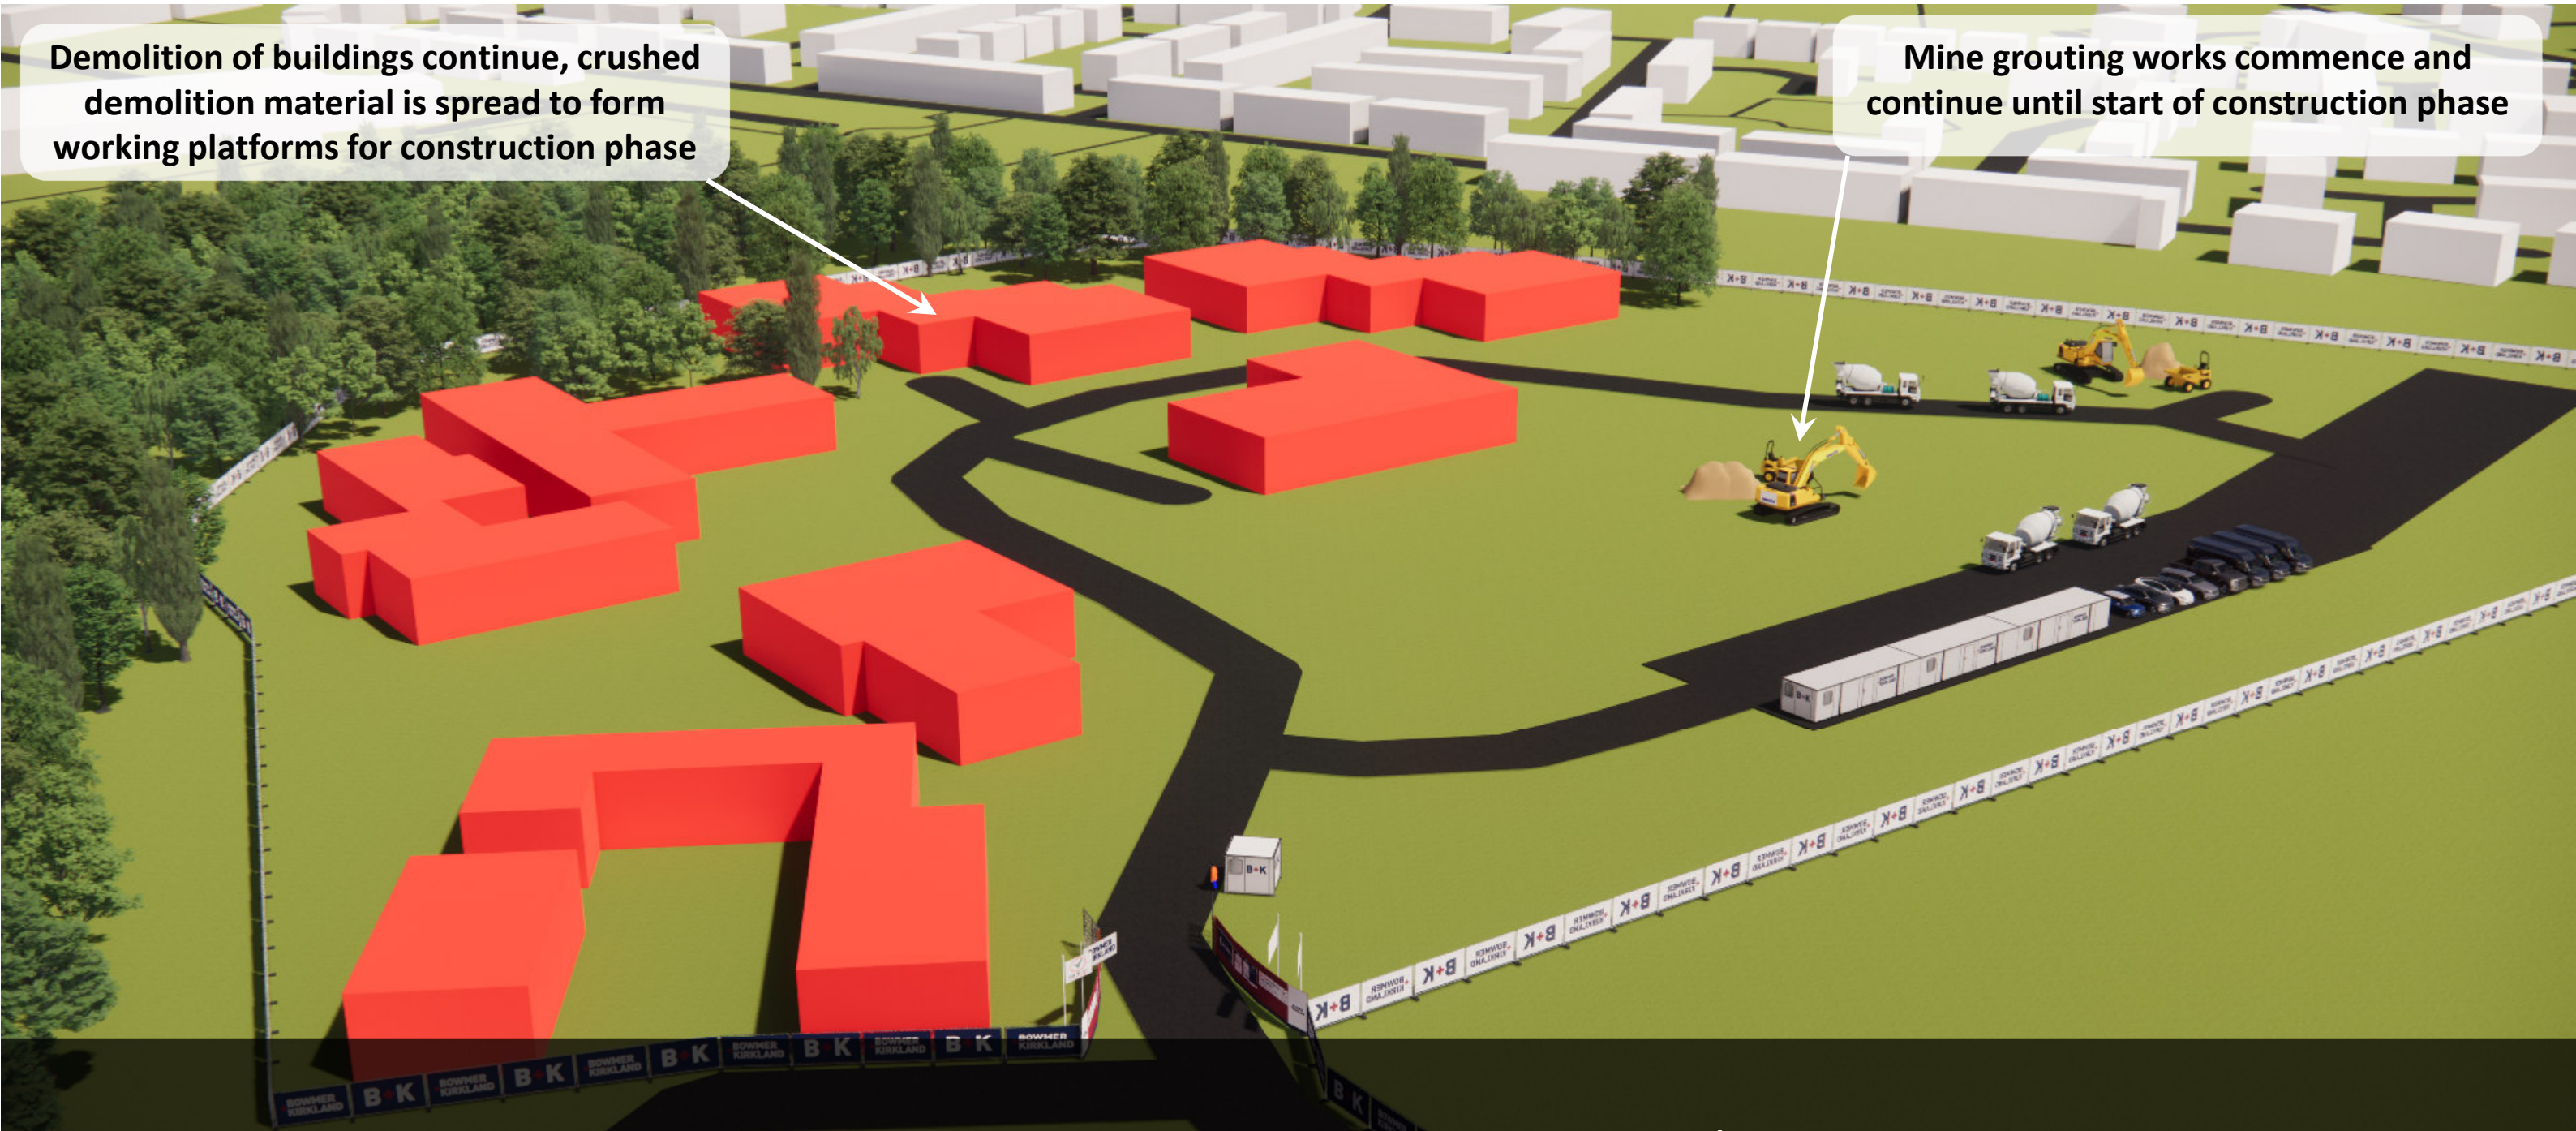

Site Logistics Plan 2 (Weeks -10 to -1)

Demolition and Mine Grouting

New car park constructed to base/ binder course

Construction traffic and turning area


Foundation construction to main school building

Temporary site compound remains from demolition phase until new car park construction complete

Site entrance and gateman arrangement remains in place from Demolition phase

Site Logistics Plan 3 (Weeks 1 to 8)


Construction Phase

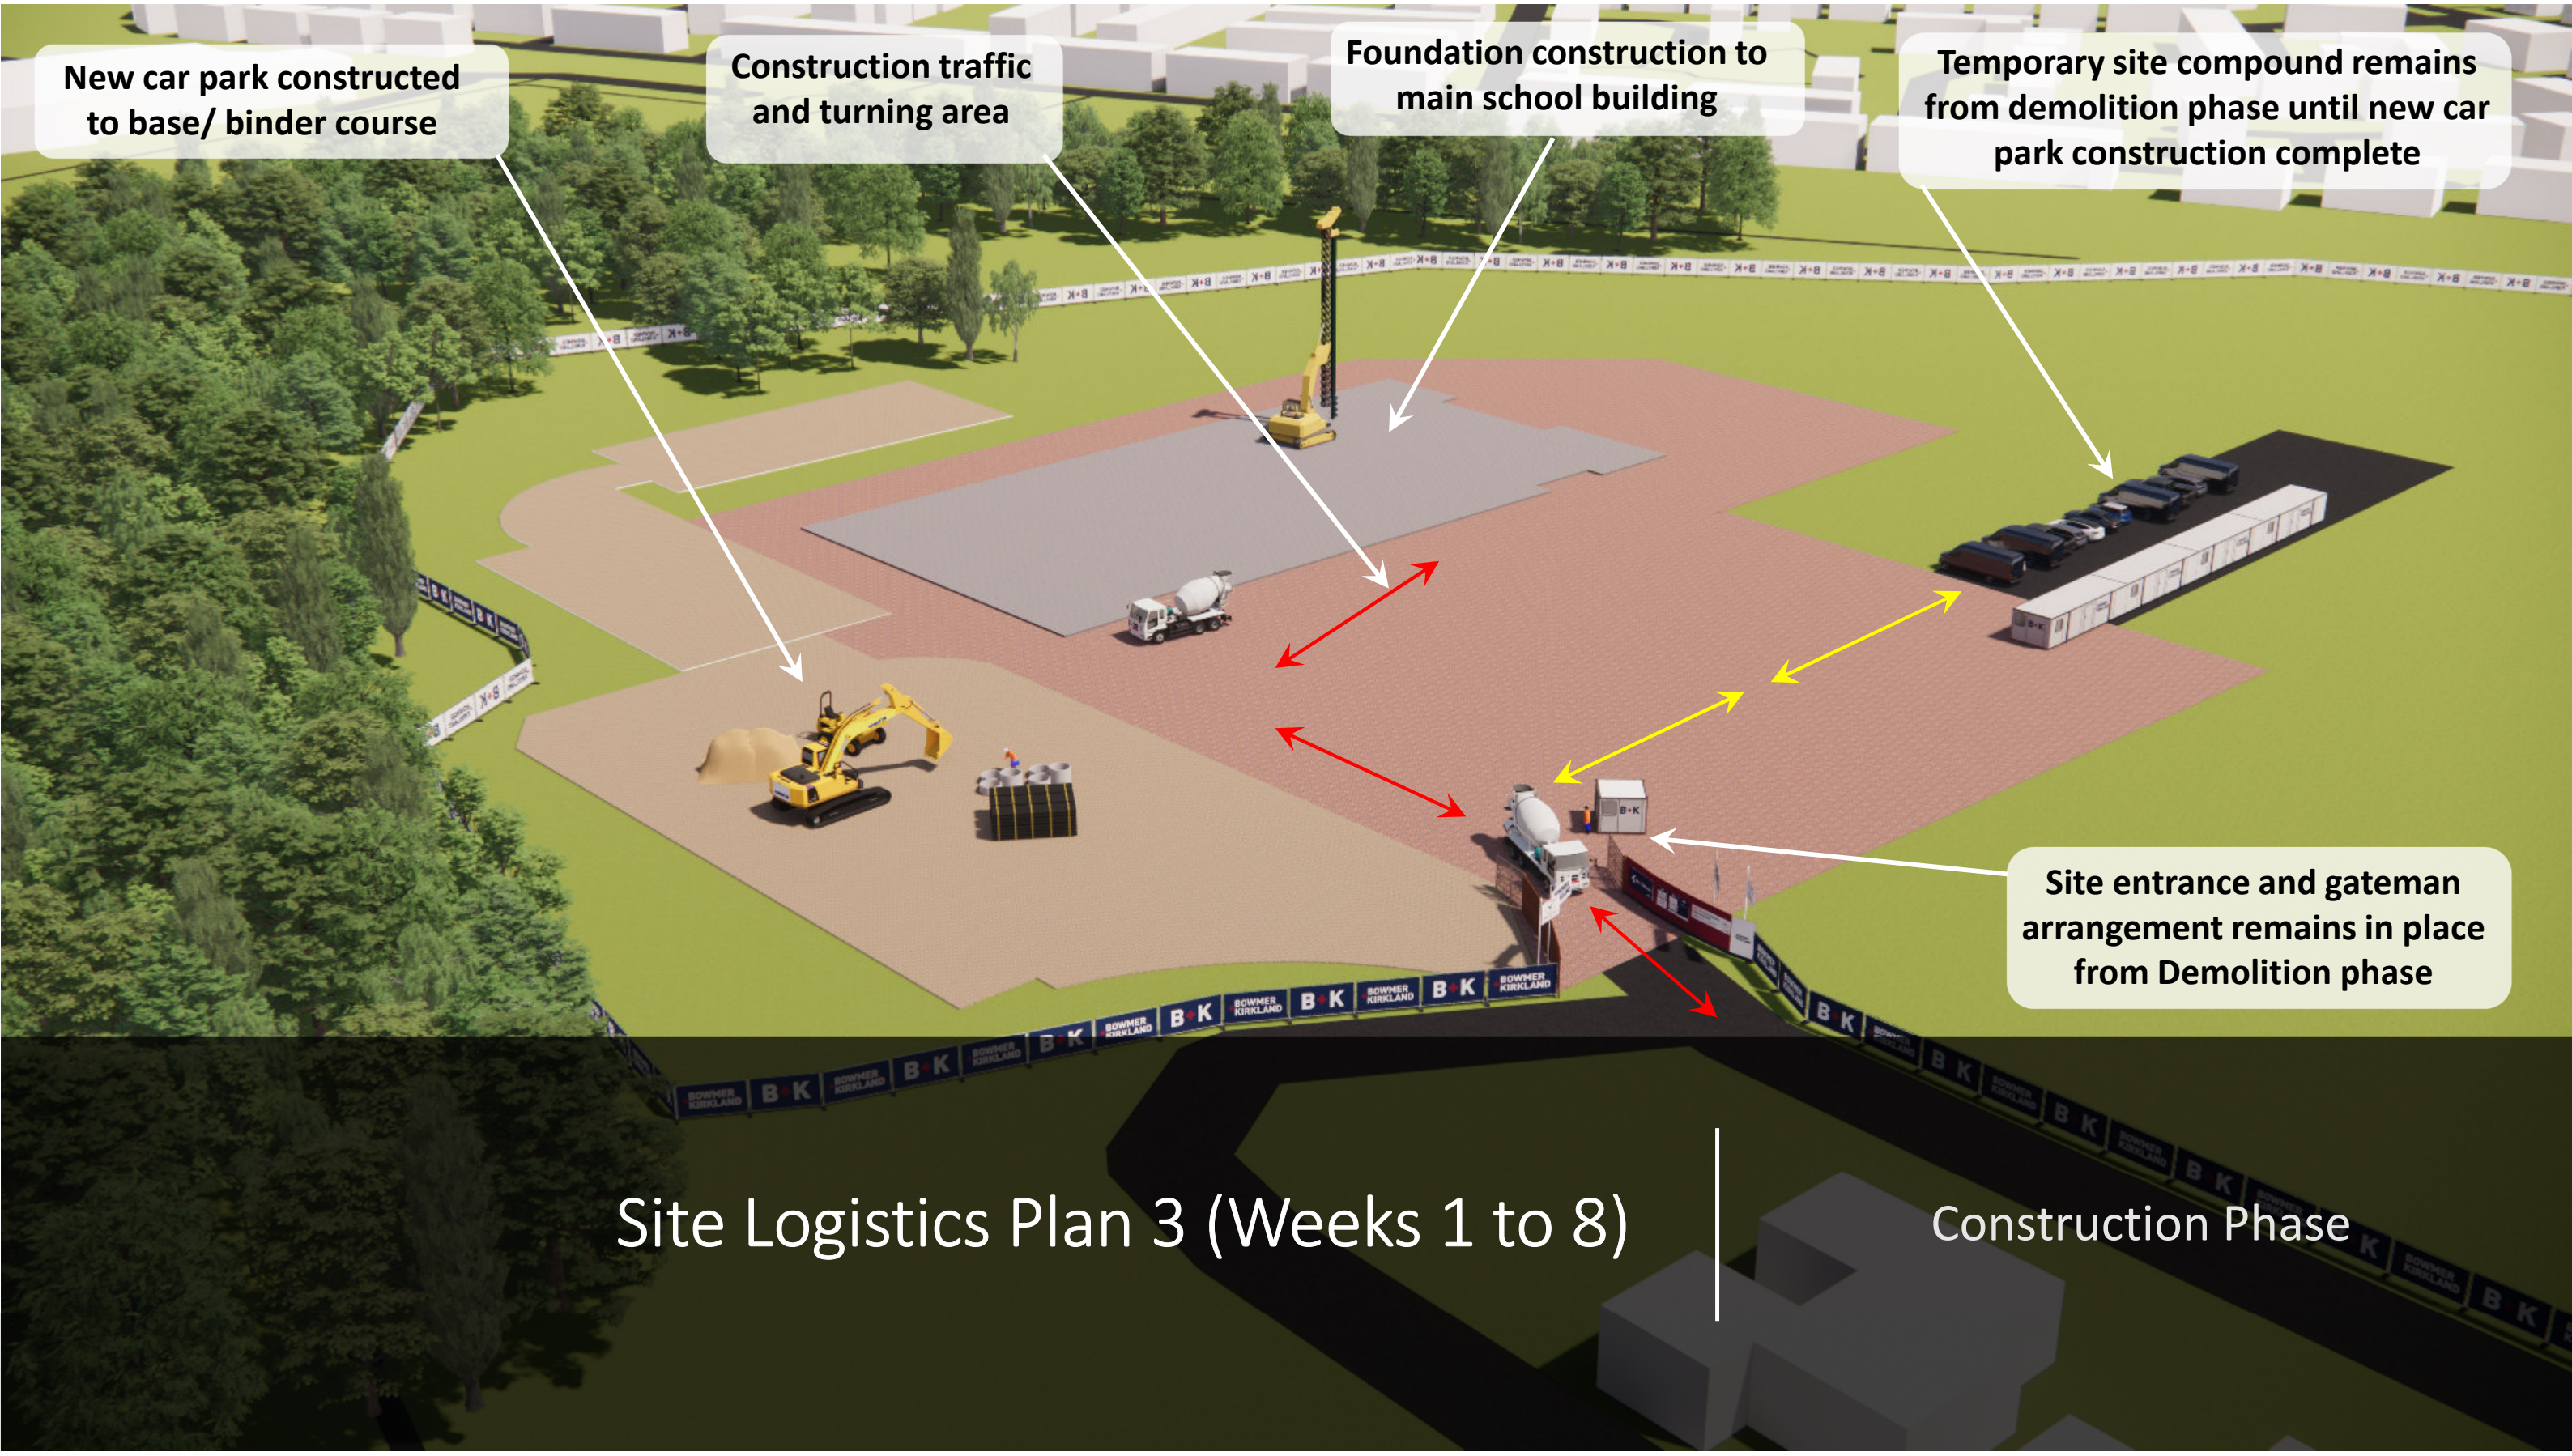

Section of new car park complete to binder course, allowing site compound relocation


Construction of slab to new Teaching block

Sports Hall foundations and slab constructed

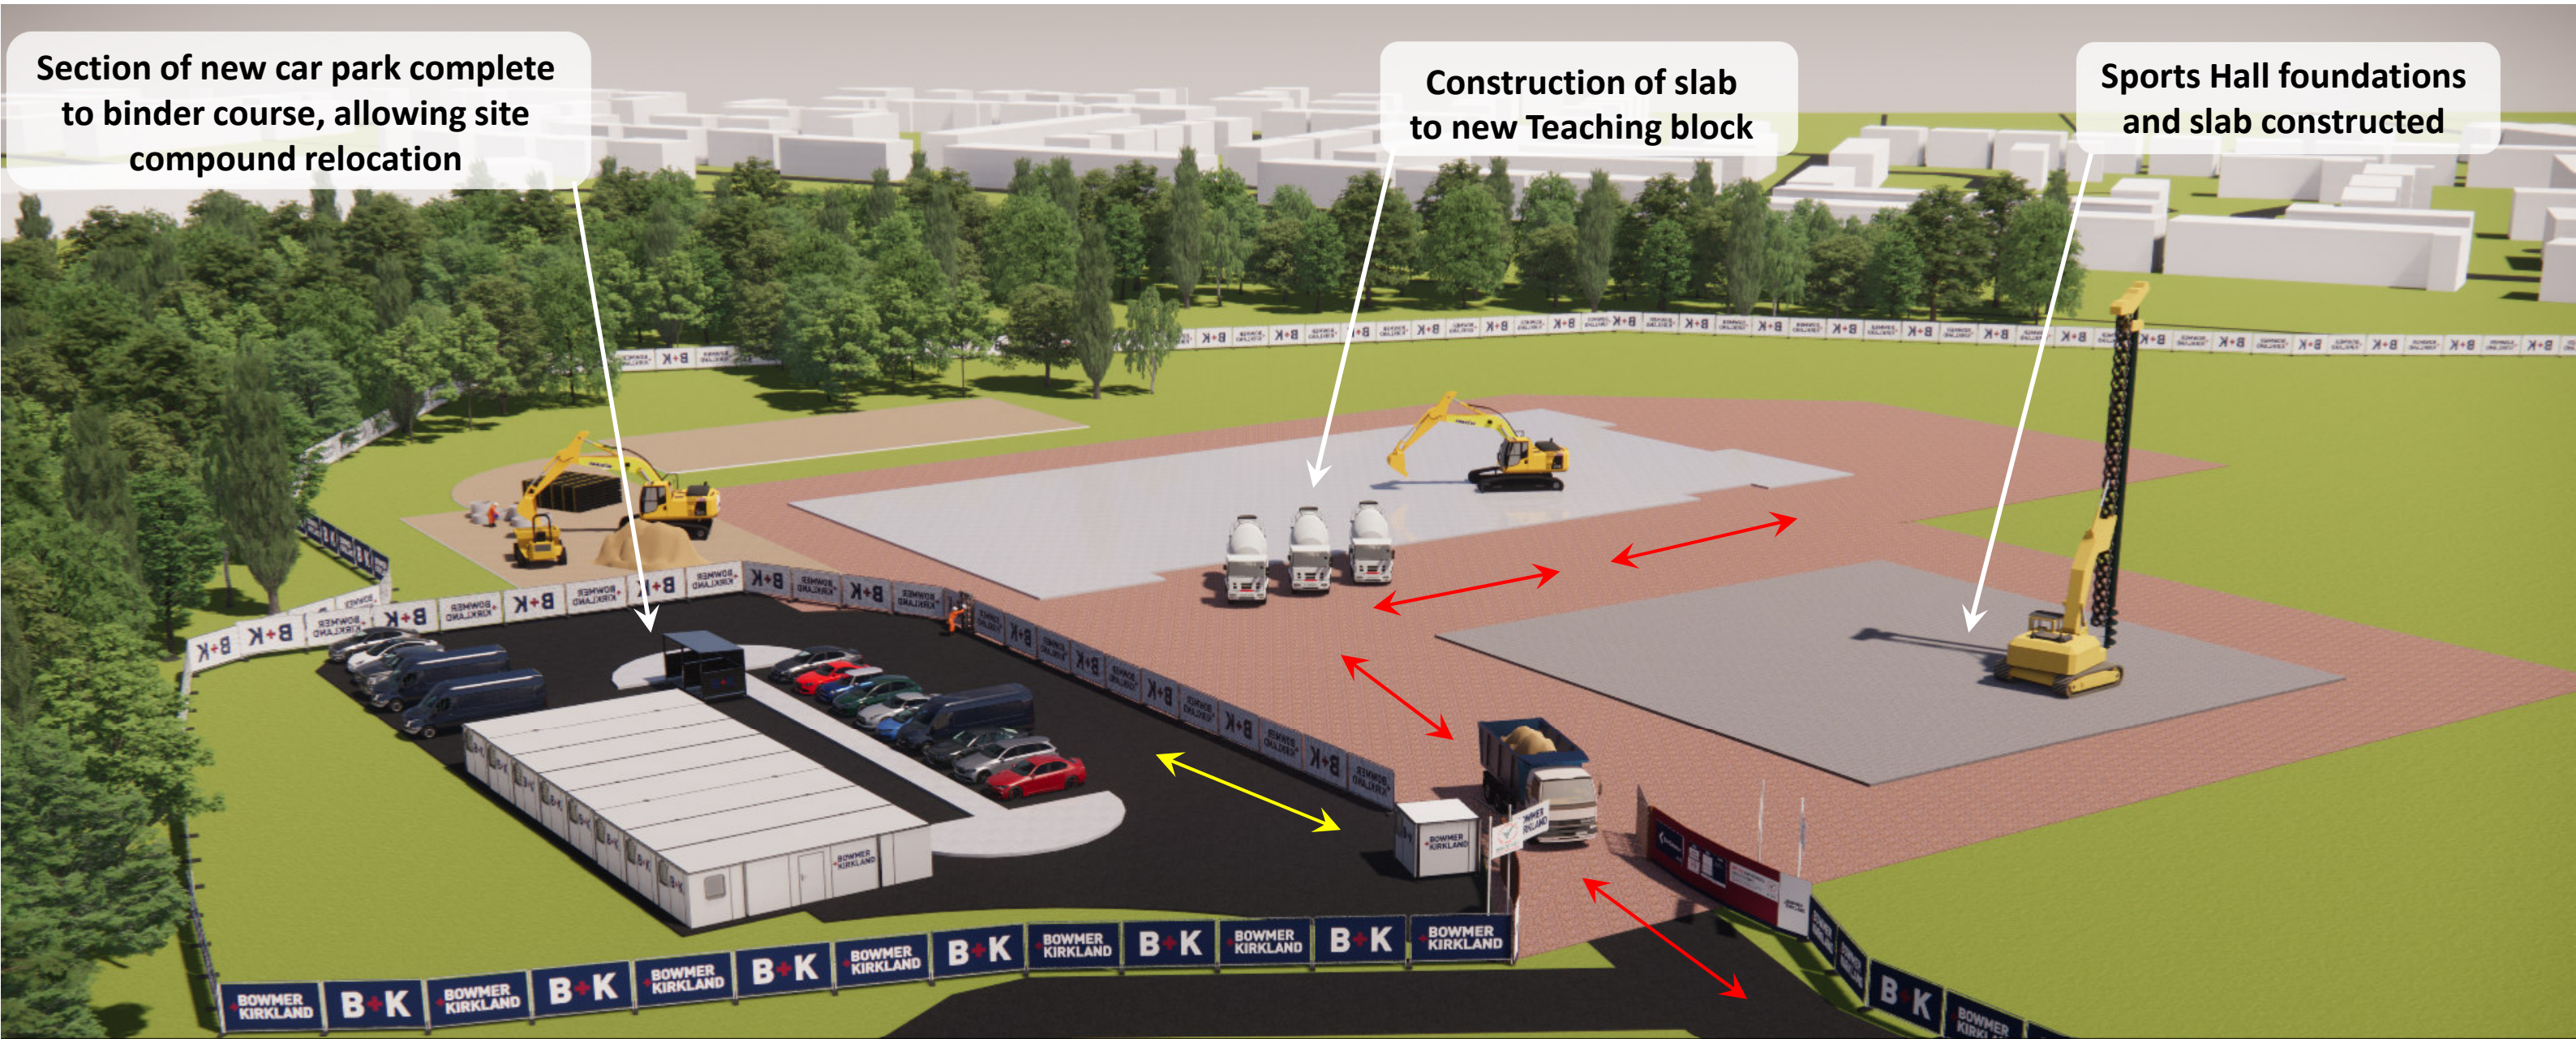

Site Logistics Plan 4 (Weeks 9 to 15)

Construction Phase

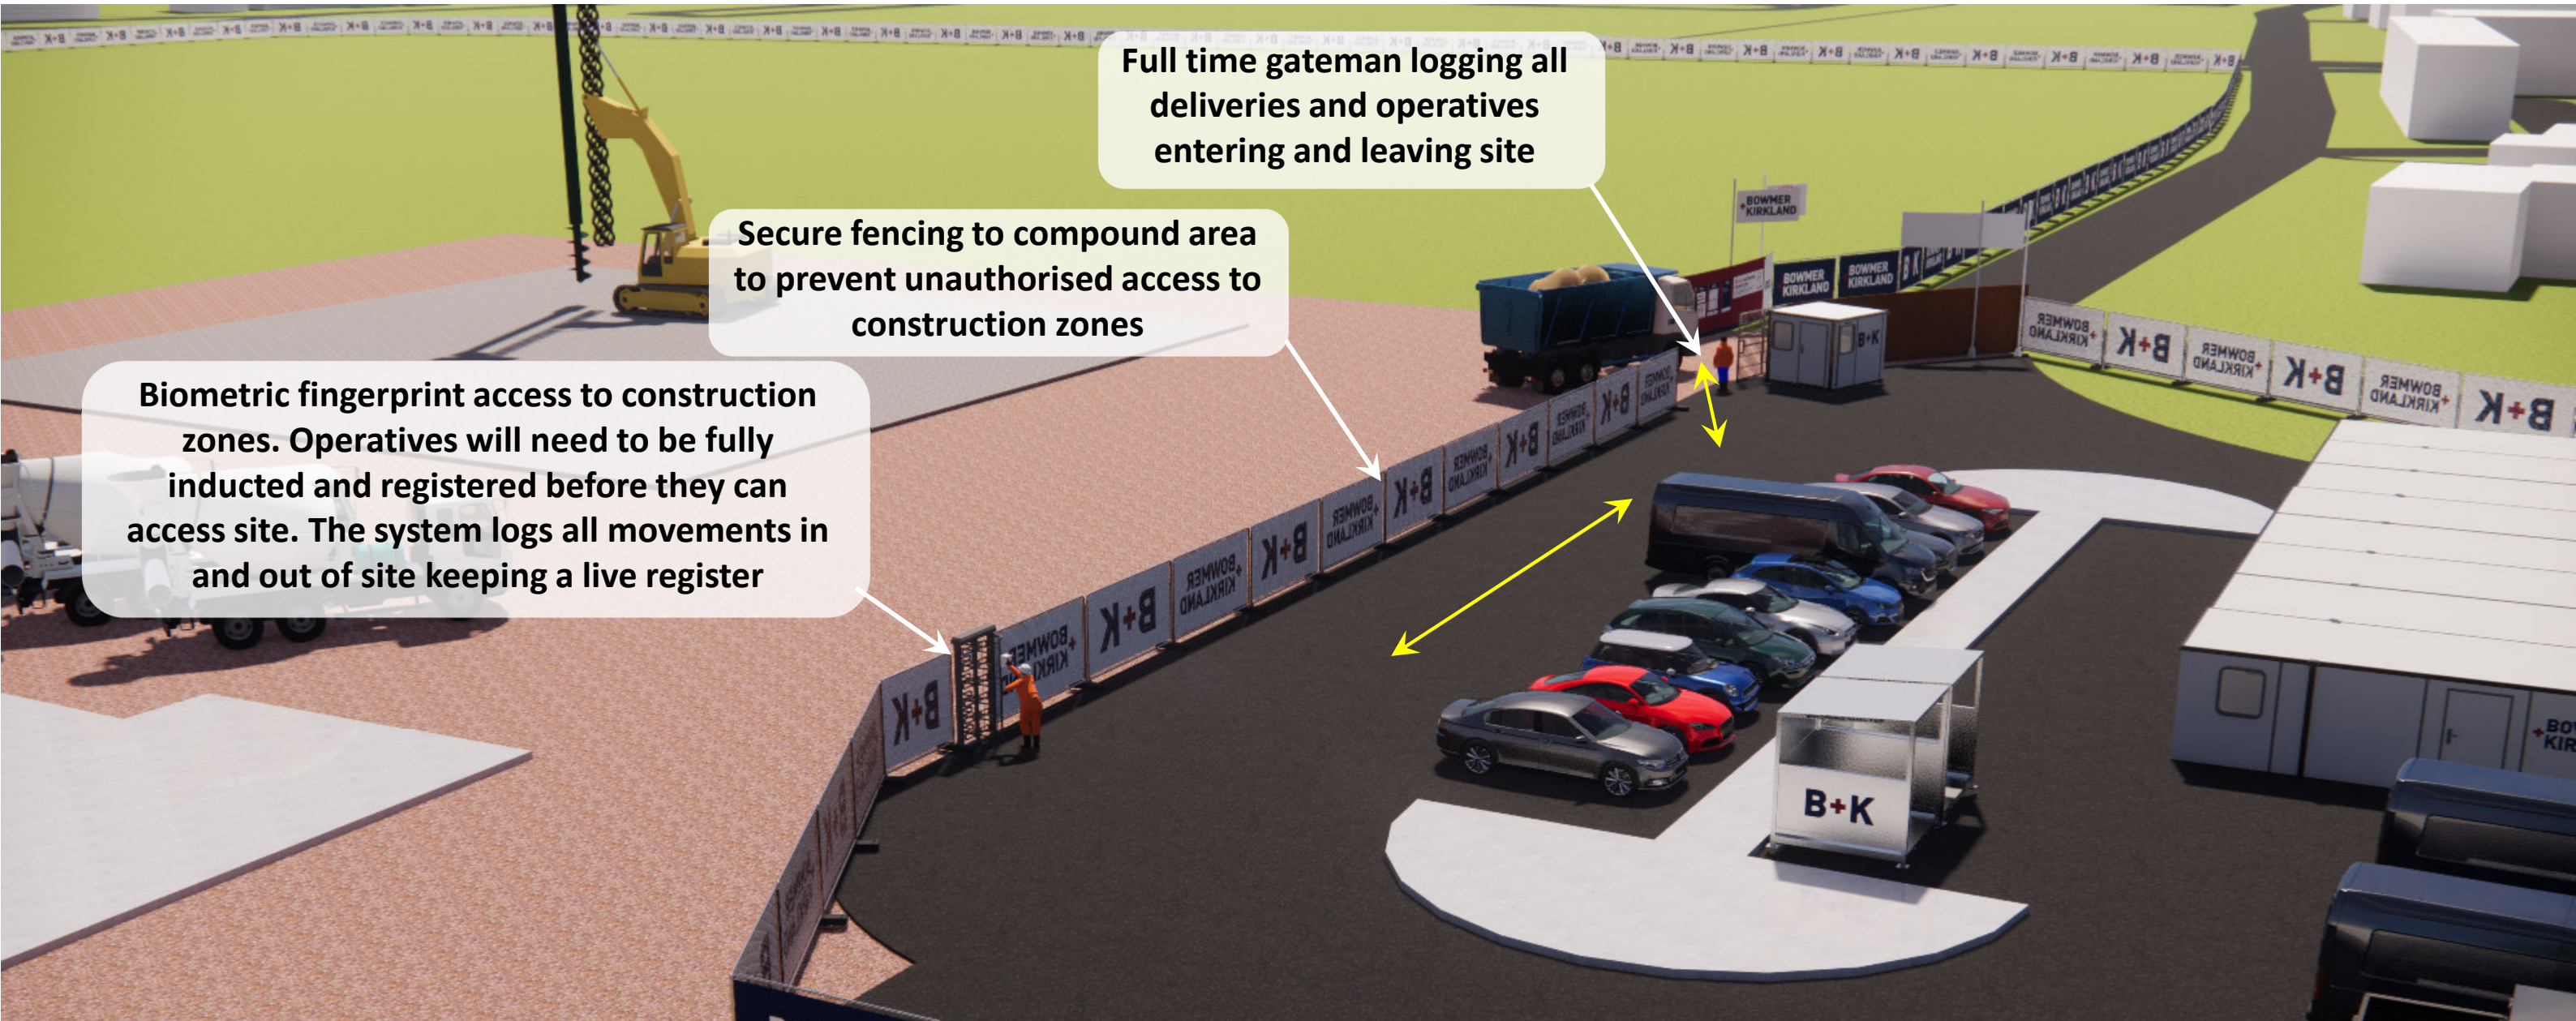

Full time gateman logging all deliveries and operatives entering and leaving site

Secure fencing to compound area to prevent unauthorised access to construction zones

Biometric fingerprint access to construction zones. Operatives will need to be fully inducted and registered before they can access site. The system logs all movements in and out of site keeping a live register


Site Logistics Plan 4a

Site Controls & Security

Construction of the new Teaching and Sports Blocks, commencing with Innovare timber frame

Delivery drop off and turning area and materials storage.
Later in the project during the fitting out stage the new MUGA will be constructed in this area. Hard landscaping around the building will be undertaken following completion of external facades and soft landscaping to the sports fields will be programmed to best suit seeding and establishment times

Additional parking area available

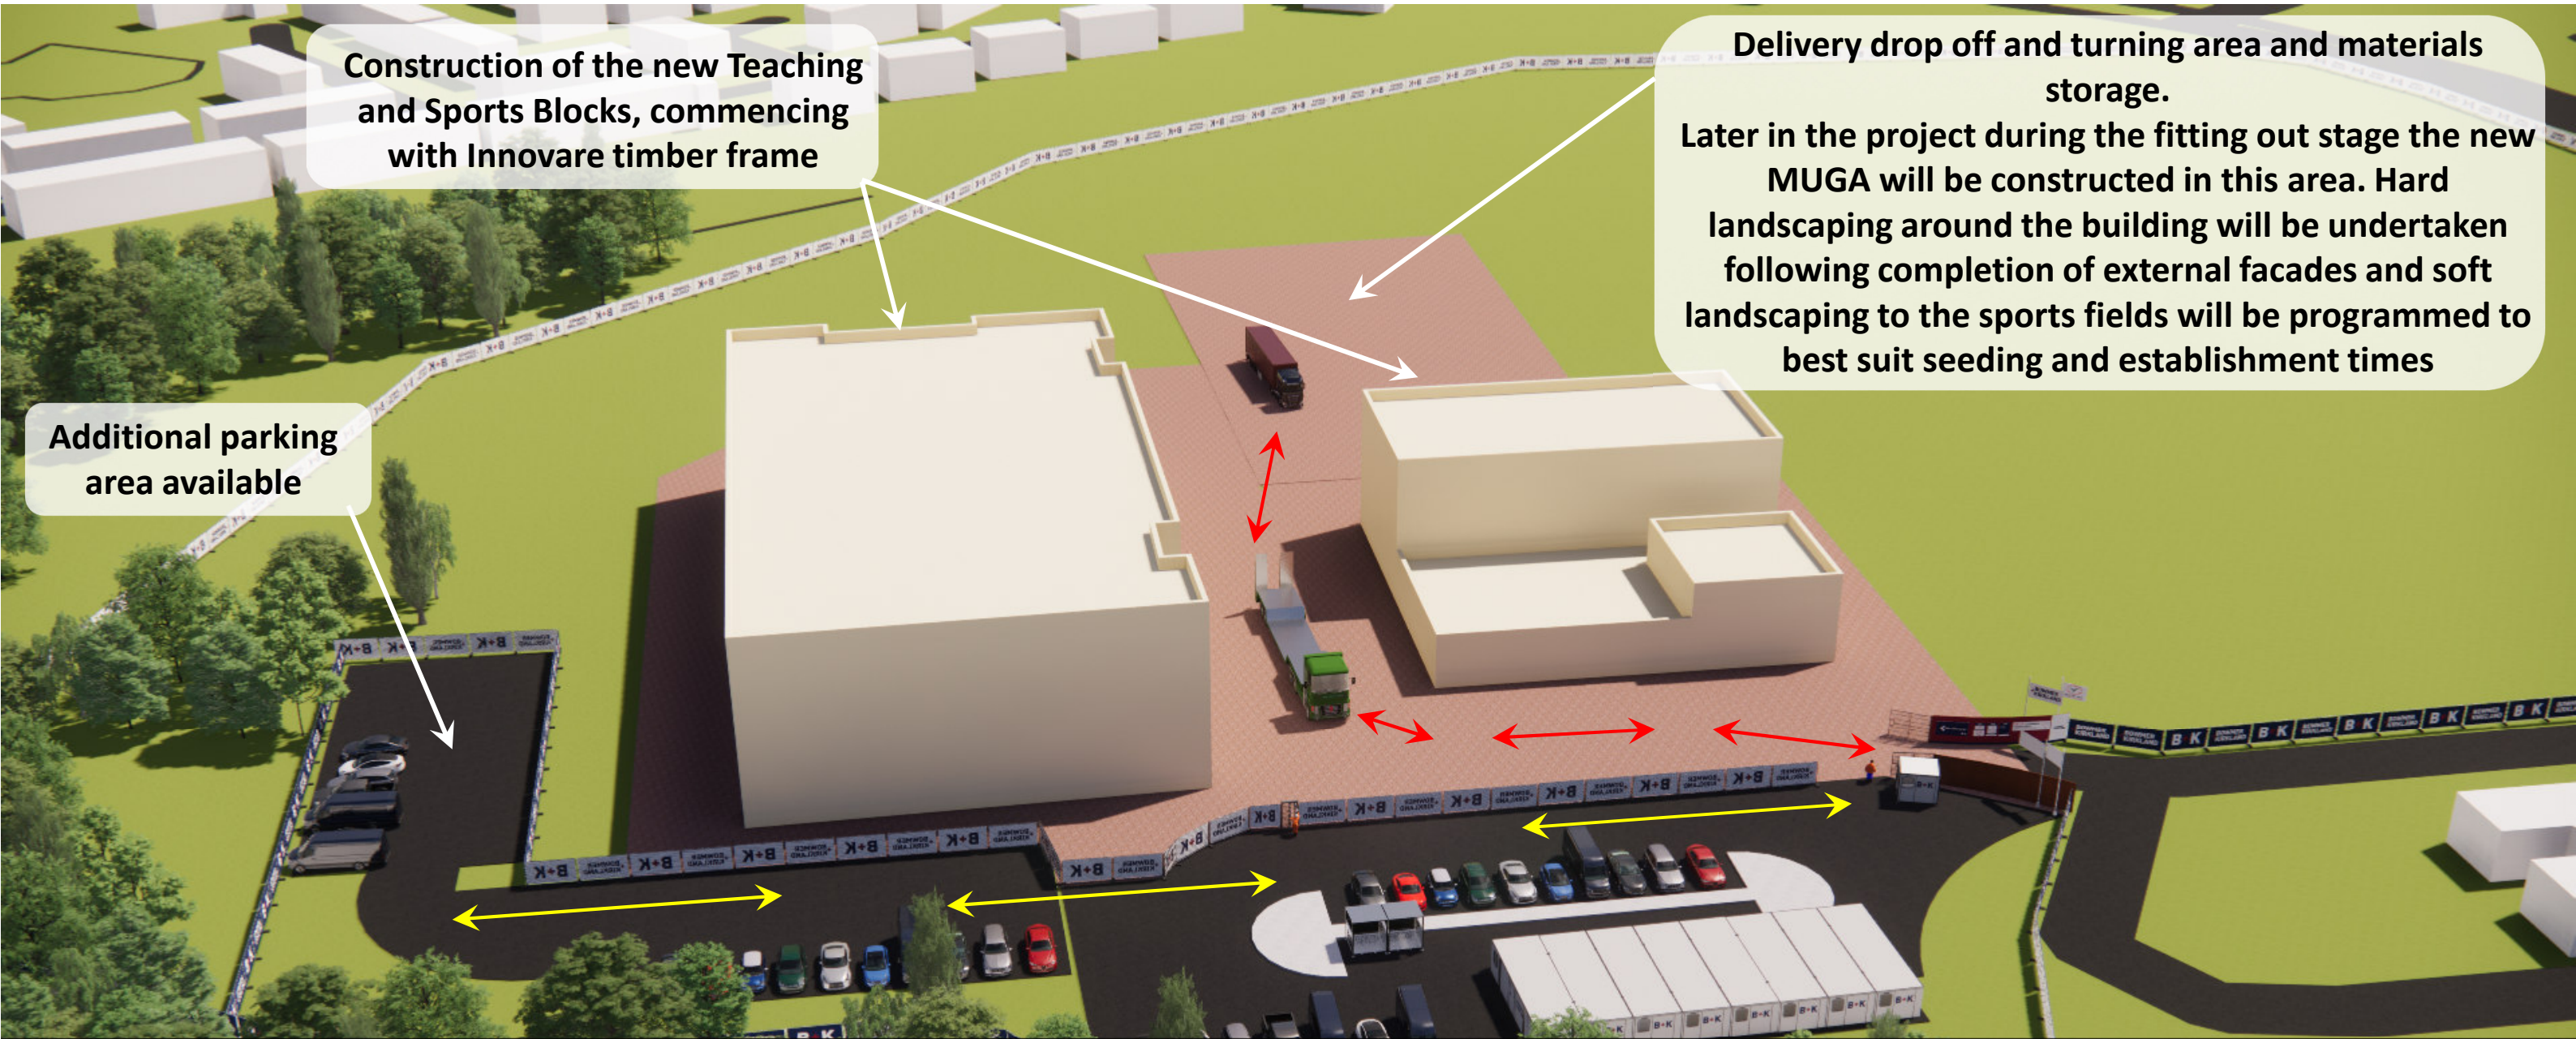

Site Logistics Plan 5 (Weeks 16 to Practical Completion)

Construction Phase



Site Handover & Practical Completion

22nd August 2023
