


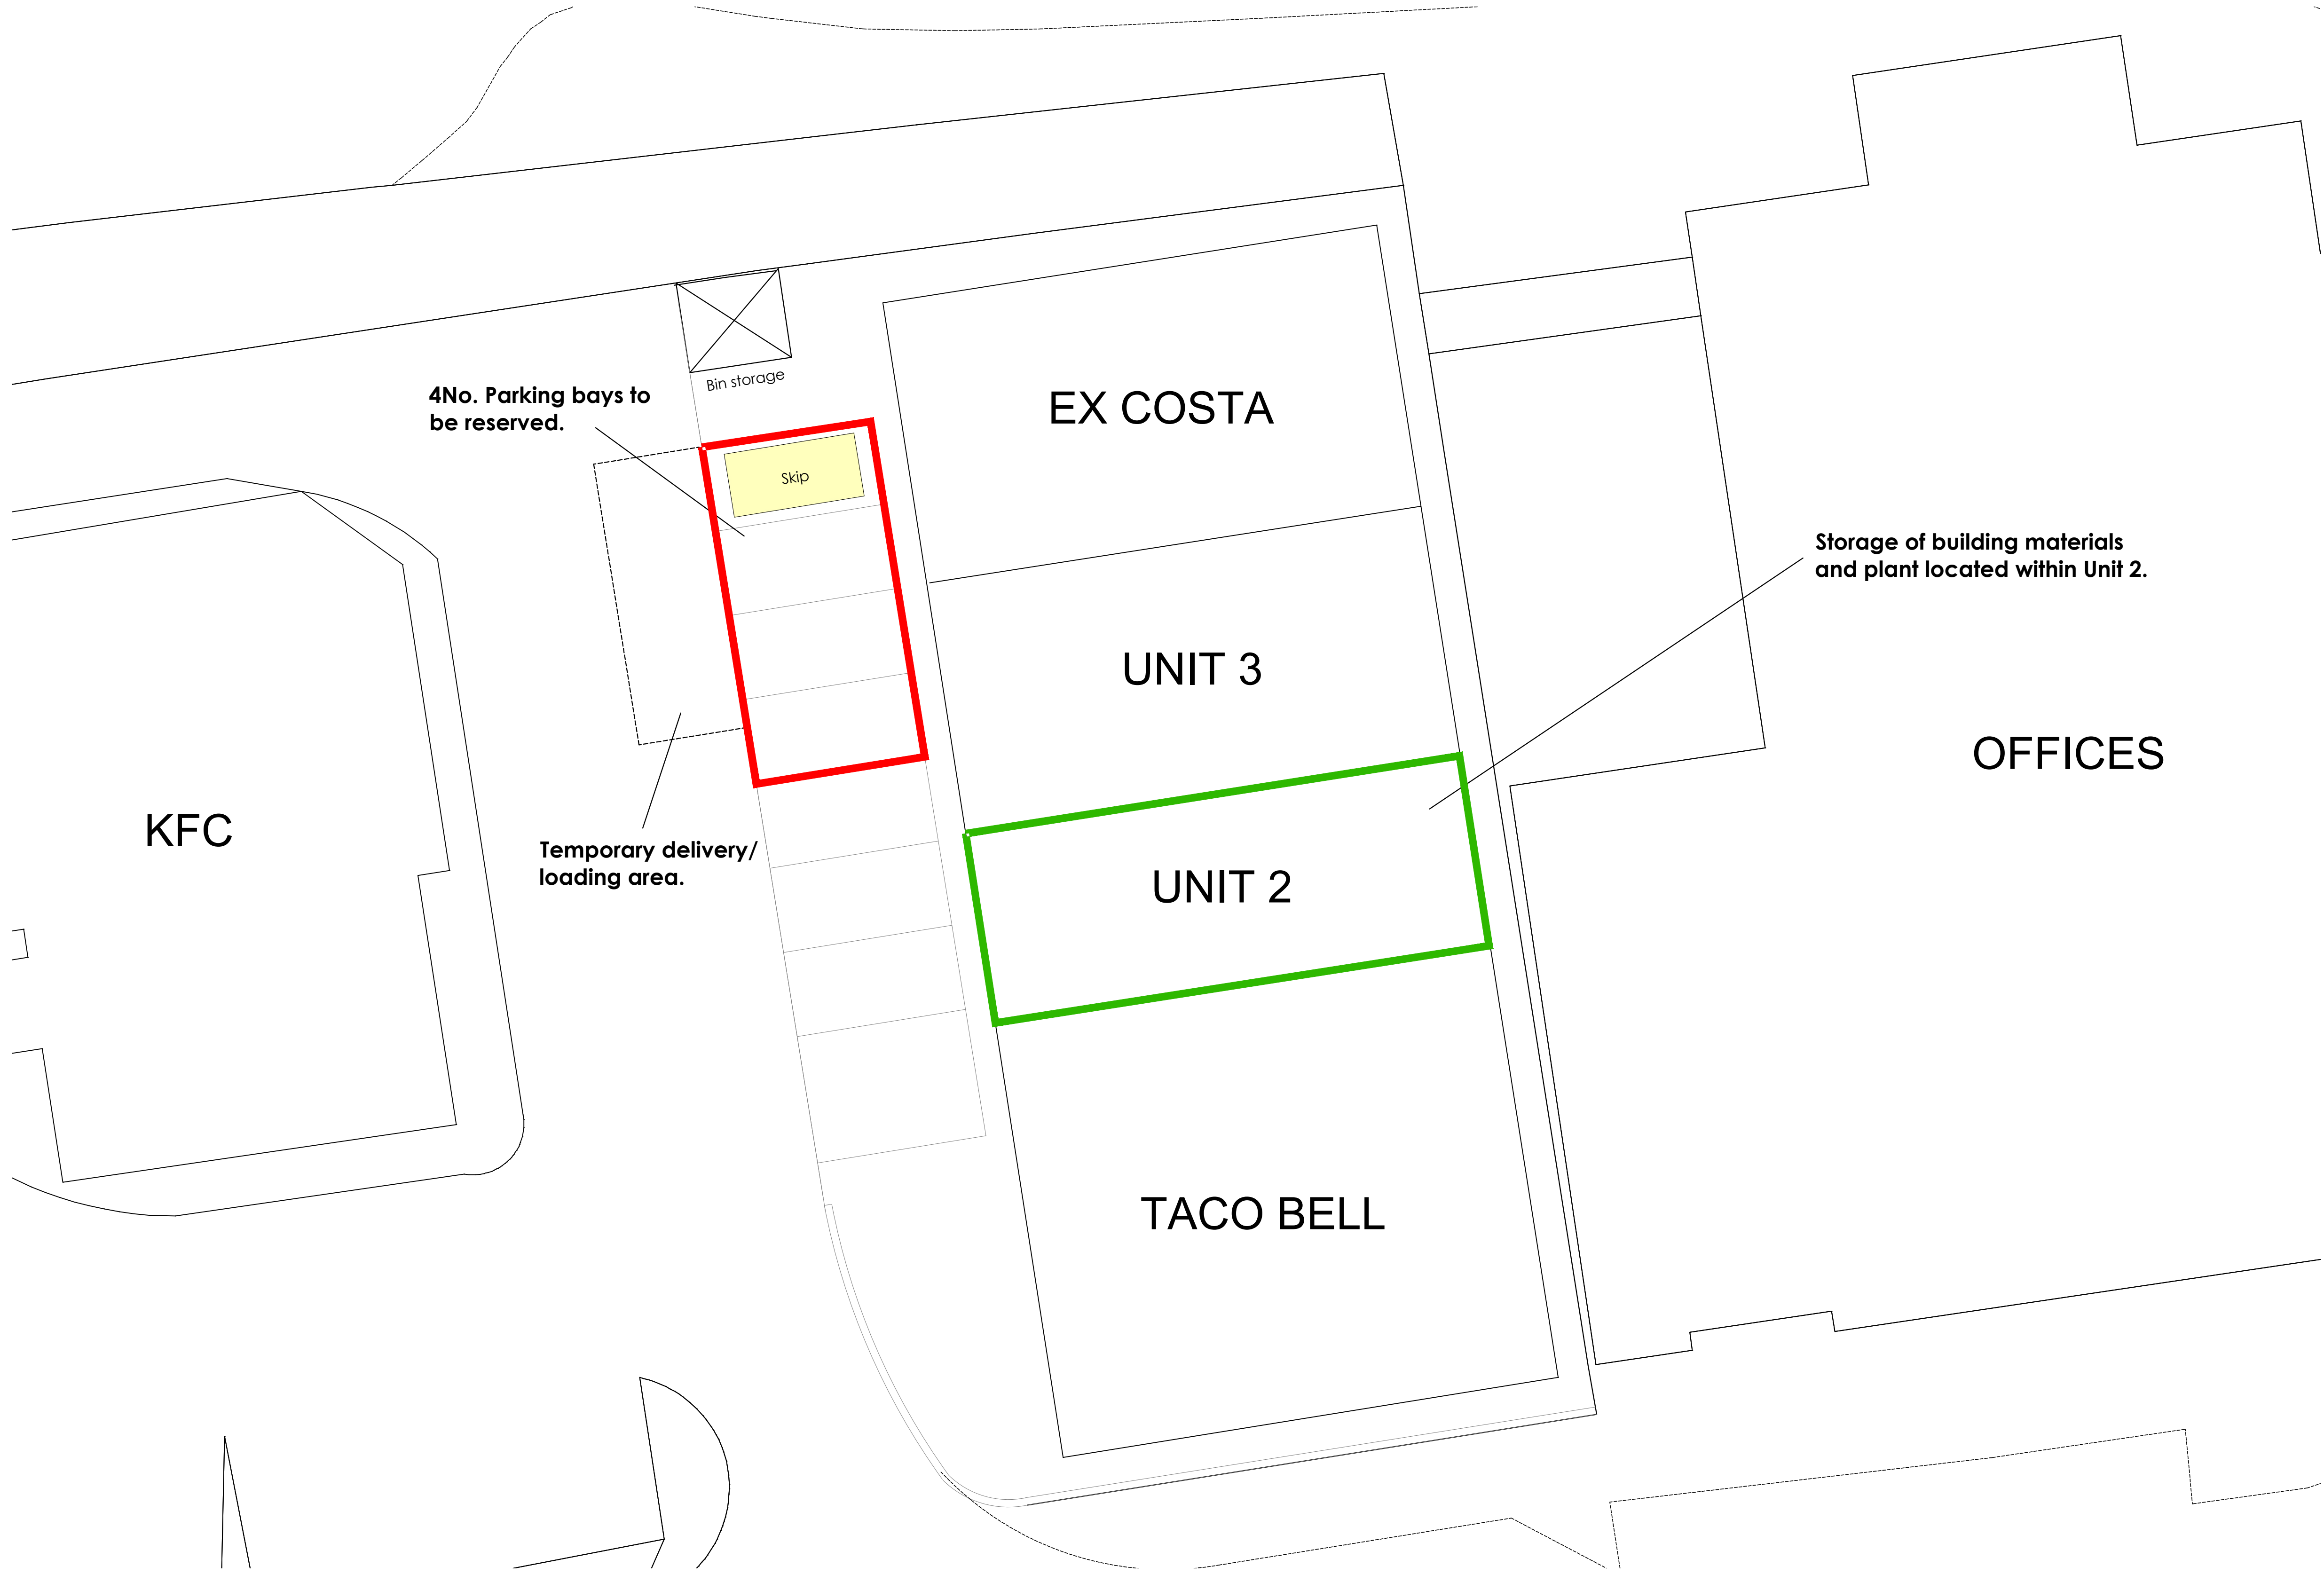

**CONSTRUCTION MANAGEMENT NOTES:**

**Employee/Contractor Parking:**  
3No. parking bays are to be reserved for contractor/employee vehicles for the duration of construction works.

**Construction Materials & Plant:**  
All construction and plant, tools and building materials to be stored securely within Unit 2. No plant or materials to be stored externally.

**Delivery/Loading Bay:**  
Temporary construction loading/unloading arrangements shown on this drawing shall be provided prior to commencement of development and retained for the entire construction.


**Access Maintained:**  
Vehicular and pedestrian access to adjoining premises to be maintained at all times.

**Skip & Waste Storage:**  
1No. parking bay to be reserved for external skip/compound.

All construction parking, loading and storage requirements shown shall be retained for the duration of the construction works.

A 07/09/26 Delivery/loading area moved.

Revisions



|                                               |                                                    |  |  |  |                                |                   |                |                |
|-----------------------------------------------|----------------------------------------------------|--|--|--|--------------------------------|-------------------|----------------|----------------|
| Project<br>Peel Street<br>Barnsley<br>S70 2RL | As Proposed:<br>CONSTRUCTION<br>MANAGEMENT<br>PLAN |  |  |  | A1 Scale<br>1:100              | A3 Scale<br>1:200 | Date<br>Aug 26 | Drawn By<br>NP |
|                                               |                                                    |  |  |  | PLANNING                       |                   |                |                |
|                                               |                                                    |  |  |  | Drawing Number<br>JBPS -1-P112 |                   | Revision<br>A  |                |
