

Balfour Beatty

A61 Barnsley Dilapidation Survey

10.57hrs, Friday 13th January 2023

Weather: Overcast with light showers

1) Northwest tie in: Damaged kerb



2) Northwest tie in: Blocked Aco Drain



3) Lane 1 Northbound: low chamber/water valve



4) North Tie in Island: Low chambers (3no)





5) Northwest tie in: Damaged kerb/standing water to pedestrian crossing





6) Northwest tie in: Damaged kerb



7) Northbound Lane 2: Low chamber with surrounding surfacing course damage



8) Northbound Lane 2 low chamber with surrounding surfacing course damage



9) North of Bridge, Northbound: Blocked gully



10) North of bridge, Northbound: Blocked gully



11) North Bridge joint, Lane 1: Failed/cracked surfacing course



12) Damage to west bridge parapet



13) South Bridge joint: Failed/Cracked surfacing course



14) South of Bridge, Northbound: Blocked gully



15) South of bridge, Northbound Lane 1 & 2 joint: Low chamber



16) South of bridge, Northbound Lane 1: Cracks to surface course nest to gully



17) South of bridge, Northbound Bus stop taper: failed/cracking to surface course around chamber & gully



18) South of bridge Northbound/Bus lay by taper: Damaged kerb



19) South of bridge, Northbound Lane 1: Damage to surfacing around chamber



20) South tie in pedestrian crossing island: low chamber with sunk tarmac surround



21) South tie in island: low/sunk tarmac surround around chamber



22) South tie in, Southbound bus lane: Cracking to bus lane surfacing & blocked gully





23) South tie in, East footway wall: Condition of existing wall



24) South Tie in East footway: low failed tarmac around chamber



25) South tie in, Southbound: damage to kerbs



26) South of bridge, East footway wall: Existing condition



27) South of bridge, Southbound: Blocked gully





28) South of bridge, southbound: failed surfacing course



29) South of bridge, southbound: Blocked gully



30) South of bridge, East footway wall: Existing wall condition





31) South of bridge, East footway wall: Existing wall condition





32) South of bridge, southbound: Failed/cracking to surfacing course




33) South of bridge, East footway: Existing wall condition



34) North of bridge, East footway: Existing footway tarmac/East Parapet



35) Northbridge joint, southbound lane: failed/cracking to surface course

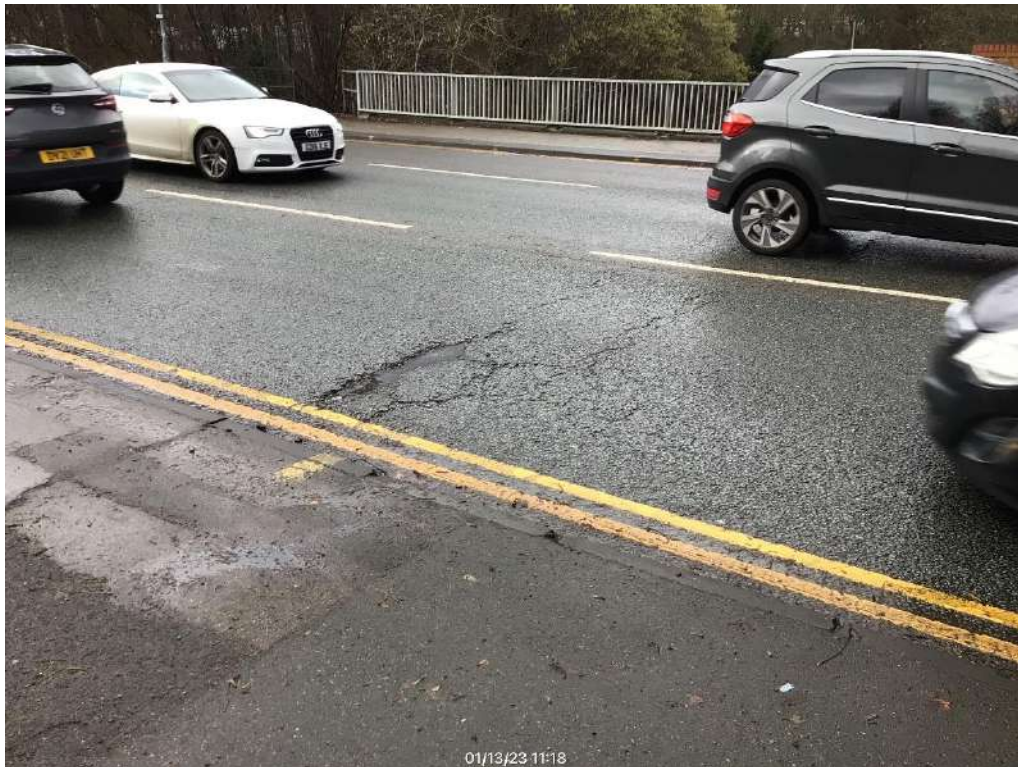

36) North of bridge, Southbound Lane: Blocked gully & damaged tarmac around chamber in footway



37) North of bridge, Southbound Lane: Damaged kerbs



38) North of bridge, East footway wall: Existing condition



39) North of bridge, East footway wall: Existing condition







40) North of bridge, Southbound: Damaged kerb



41) North of bridge, Southbound: Damaged/low kerbs from trench reinstatement works



42) Northeast tie in, East kerb line: damaged kerb

