


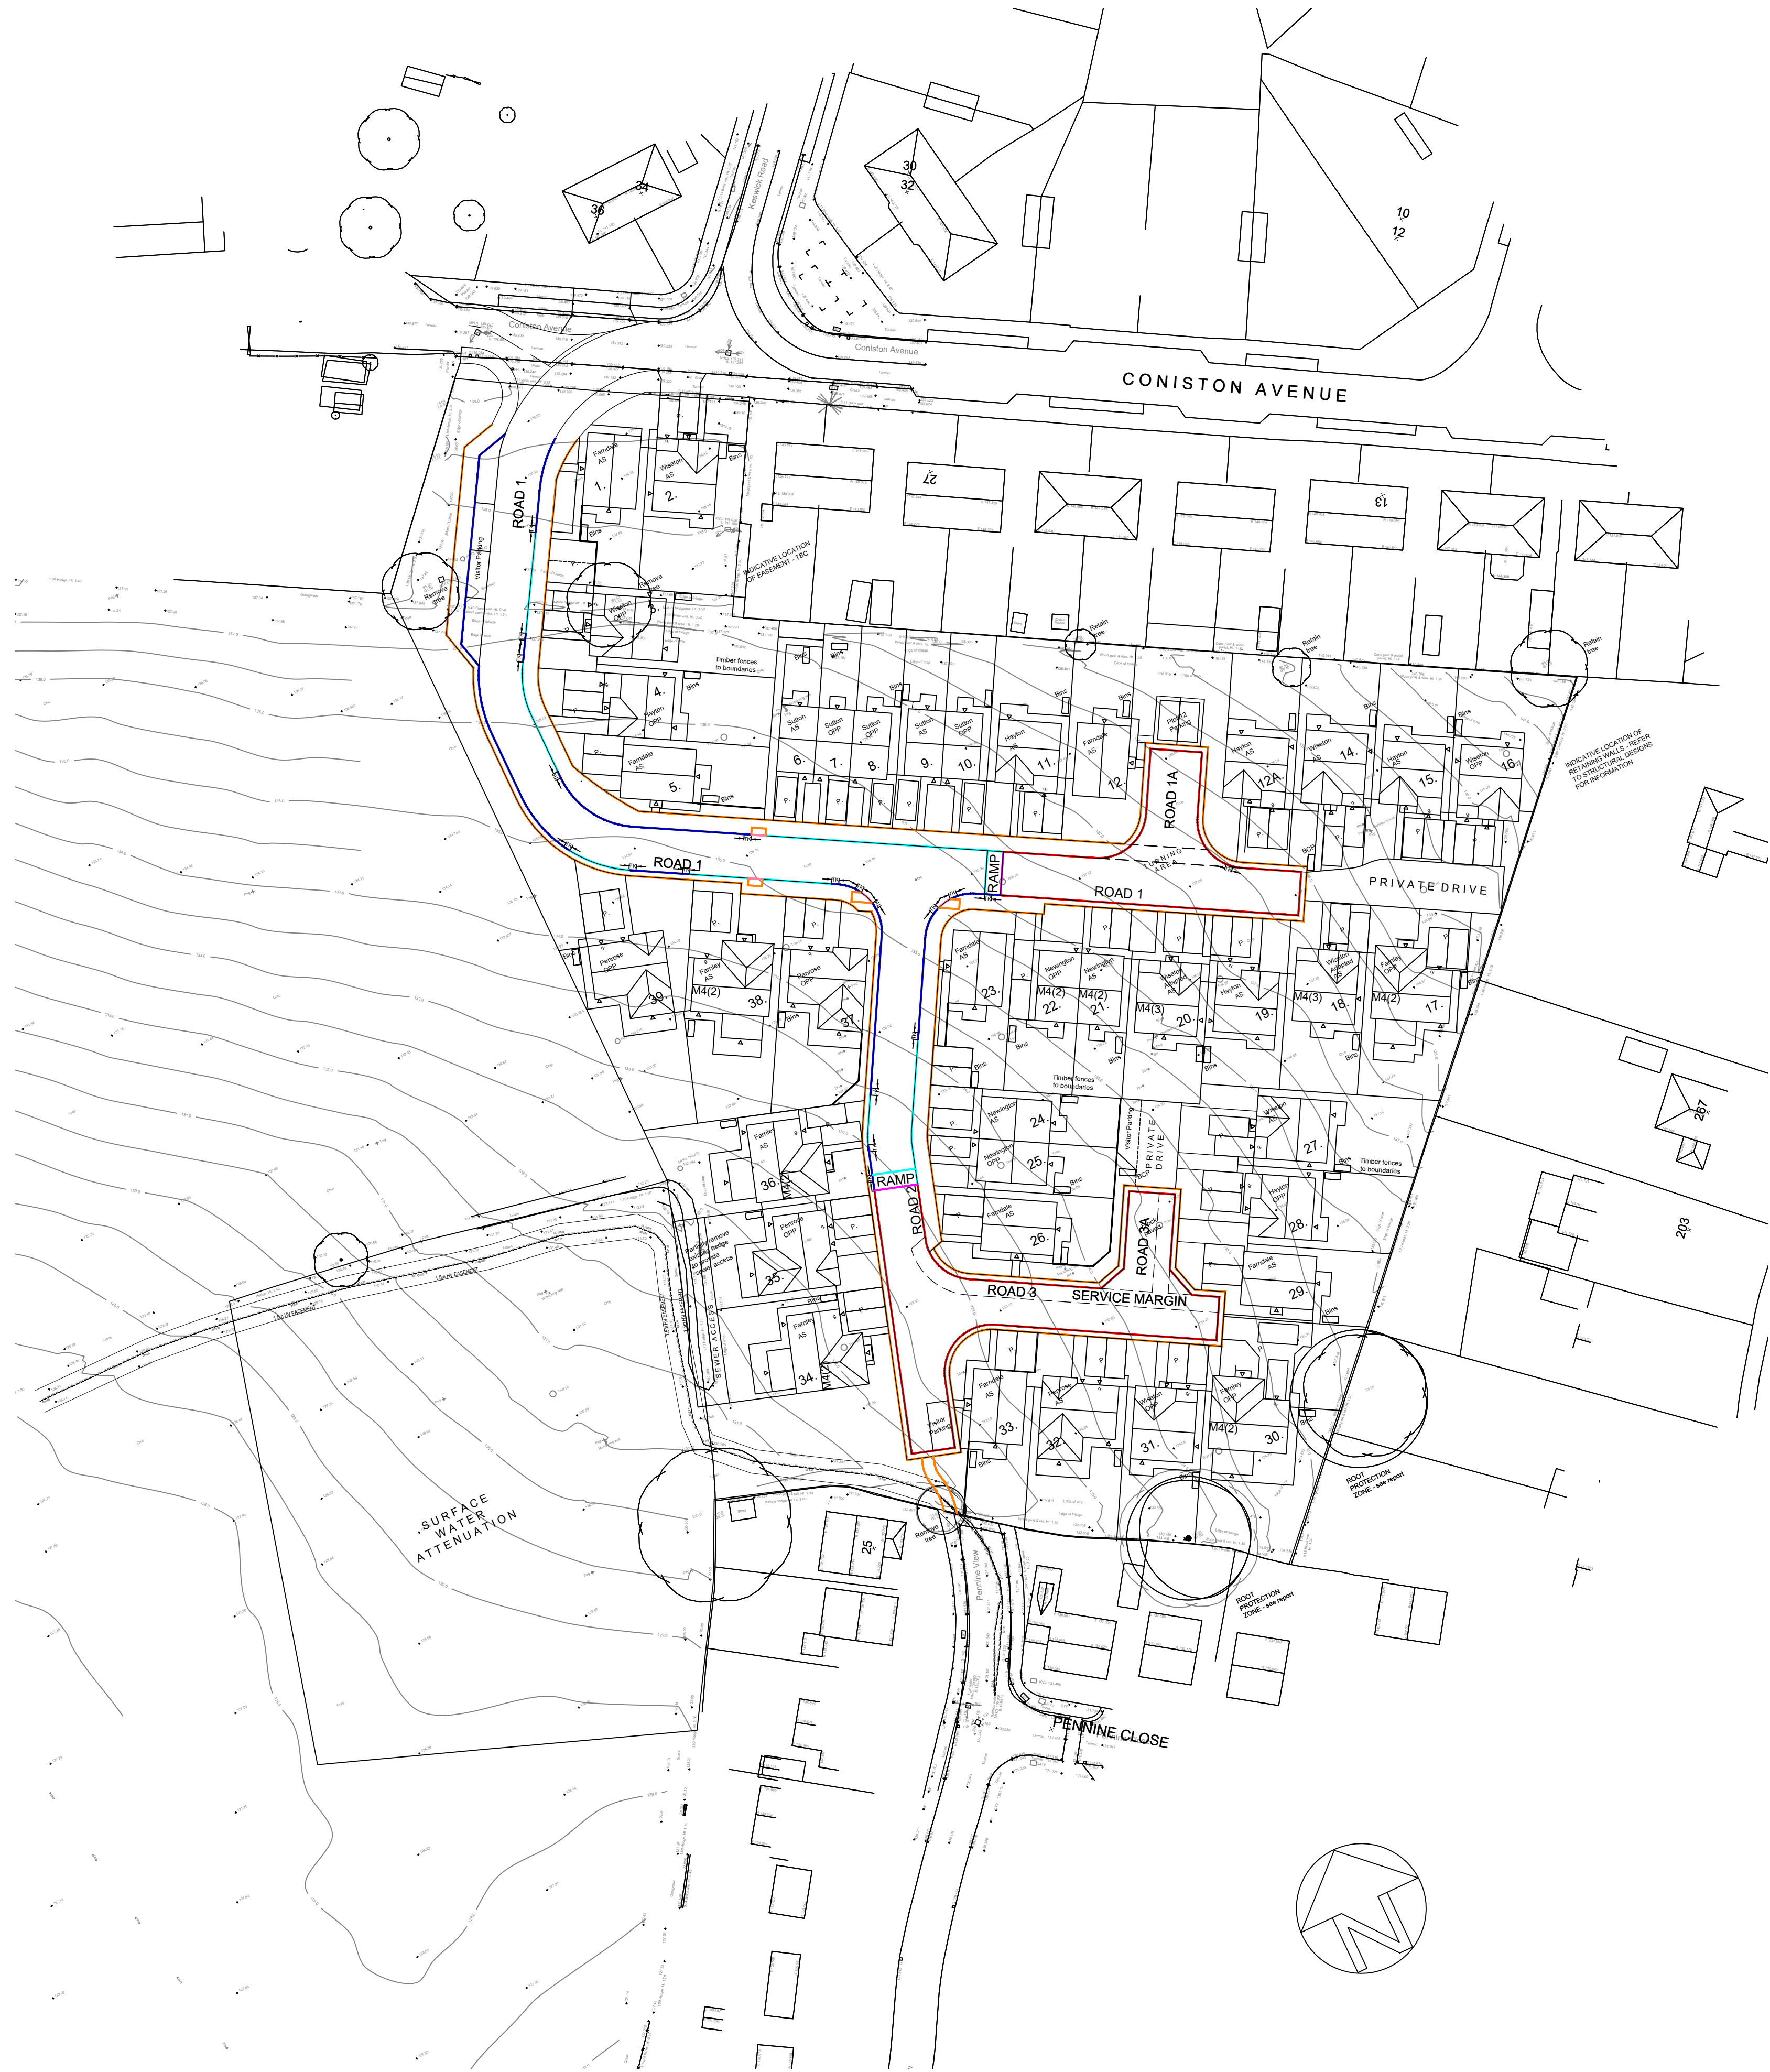

KEY: Precast Concrete Kerbs

- 125x255mm HALF BATTERED P.C. CONCRETE KERB WITH 100mm UPSTAND
- 150x50mm PRECAST CONCRETE EDGING-TYPE K118
- 175x125mm CHAMFERED P.C. CONCRETE KERB 25mm UPSTAND
- 150x125mm CHANNEL BLOCK - 450mm LONG
- 125x175mm KEYKERB IN CHARCOAL
- DROPPED KERB WITH 0-6mm UPSTAND
- TRANSITION KERBS

Note: See Latest Revision of Drawing Number E24/8080/009 For Standard Details

RISK ASSESSMENT: SIGNIFICANT RISKS THAT CANNOT BE DESIGNED OUT		
RISK	LEVEL OF RISK (MM)	SUGGESTED ACTION
DEEP EXCAVATIONS ASSOCIATED WITH NEW DRAINAGE WORKS	HIGH	ENSURE ALL EXCAVATIONS HAVE ADEQUATE TRENCH SUPPORTS
HANDLING LARGE DIAMETER MANHOLE RINGS AND CIRCULAR PIPES	HIGH	USE CORRECT LIFTING EQUIPMENT AND ENSURE OPERATIVES WEAR APPROPRIATE PROTECTIVE CLOTHING/HARD HATS/CORRECT PPE
CONTACT WITH SEWAGE	MED	OPERATIVES TO USE CORRECT BREATHING EQUIPMENT/CORRECT PPE
NOISE	MED	OPERATIVES TO USE CORRECT EAR PROTECTION/CORRECT PPE
DRAINAGE EXCAVATIONS ADJACENT EXISTING BOUNDARY STRUCTURES	HIGH	ENSURE CORRECT SUPPORTS ARE PROVIDED TO TRENCHES AND BUILDINGS WHERE REQUIRED
DRAINAGE EXCAVATION IN PUBLIC HIGHWAY	HIGH	ENSURE CORRECT USE OF TRENCH SUPPORTS IN EXCAVATION AND SCREEN BARRIERS TO PROTECT MEMBERS OF THE PUBLIC
MAINTAIN ACCESS TO ADJACENT PROPERTIES AND OCCUPIERS	HIGH	ENSURE WORKS ARE PROTECTED WITH BARRIERS AND SIGNS TO GUIDE THE PUBLIC AWAY FROM THE WORKS
DRAINAGE EXCAVATIONS NEAR TO EXISTING SERVICES	HIGH	ENSURE WORKS ARE PROTECTED WITH BARRIERS AND SIGNS TO GUIDE MEMBERS OF THE PUBLIC AWAY FROM THE AREA
WORKING IN CONFINED SPACES, WORKING IN DRAINS AND MANHOLES	HIGH	CONFINED SPACES WORKING TRAINED PERSONNEL ONLY TO CARRY OUT WORKS UNDER A PERMIT TO WORK SCHEME SUPERVISED BY CONTRACTOR, GAS TESTING TO TAKE PLACE BEFORE ALL ENTRIES TO CONFINED SPACES
WORKING IN HIGHWAYS / RISKS FROM VEHICLE AND PLANT	HIGH	ALL WORKS TO BE SIGNED AND FENCED FROM NORMAL VEHICULAR TRAFFIC, ALL WORKERS TO WEAR HIGH VISIBILITY CLOTHING, ALL PLANT TO HAVE VISUAL AND AUDIBLE WARNING SYSTEMS
ROAD AND DRAINAGE CONSTRUCTION	HIGH	ALL EXCAVATIONS TO BE ADEQUATELY FENCED OFF AND SUPPORTED DURING CONSTRUCTION, ALL OPERATIVES TO BE TRAINED IN CORRECT METHODS OF LIFTING AND WORK IN ACCORDANCE WITH LOLER REGS
IT IS ASSUMED THAT WORKS ASSOCIATED WITH THIS DESIGN WILL BE UNDERTAKEN BY A PERSON OR PERSONS WHO ARE COMPETANT AND HAVE THE REQUIRED LEVEL OF EXPERIENCE AND EXPERTISE		

Rev C Edging kerbs added to footpath link to Pennine View 22.05.26 MD
Rev B Taper kerbs amended 27.04.26 MD
Rev A Updated to suit latest ramp and footway arrangements 18.03.26 MD

Haigh Huddleston & Associates

Civil Structural Engineering Consultants

Unit 4, Midgley Business Park, Bar Lane, Midgley, WF4 4JJ t 01924 574074
e martin@haighhuddleston.co.uk

Client
BEN BAILEY HOMES

Project
CONISTON AVENUE, BARTON

Detail
KERBING TYPE PLAN

Dwn Chkd Date Scale Dwg No.
MD OCT'25 1:500@A1 E24/8080/37C
