



A 2.1 METER HIGH STEEL MESH SECURITY FENCE WILL BE ERECTED ALONG THE SITE PERIMETER TO WATH ROAD, AS SHOWN ON THIS PLAN. THE SITE PERIMETER TO THE SOUTH AND SOUTH EAST IS BOUND BY PRIVATE GARDENS AND IS NOT EASILY ACCESSIBLE DUE TO THE PRESENCE OF A RETAINING WALL. THEREFORE A SECURITY FENCE ALONG THIS BOUNDARY ISN'T CURRENTLY DEEMED NECESSARY AND WILL ALSO BE REVIEWED IF NECESSARY.

INITIAL ACCESS TO THE SITE WILL GAINED BY ALL PARTIES VIA THE EXISTING ACCESS POINT. DELIVERY OF THE SITE WELFARE CABIN AND STORAGE CABIN WILL BE FIRST, AND WILL BE PLACED IN THE LOCATION SHOWN ON THE PLAN. THE STORAGE AND WELFARE CABIN WILL REMAIN IN THIS LOCATION THROUGHOUT THE DURATION OF THE SCHEME ONLY TO REMOVED UPON COMPLETION OF THE SCHEME. AND BEING REMOVED VIA THE COMPLETED PRIVATE DRIVEWAY.




THE AREA NORTH OF THE CABINS TOWARDS WATH ROAD WILL BE USED FOR STAFF PARKING AND FOR SITE DELIVERIES, UNTIL THE FORMATION OF THE HOUSE TYPE B1 FOUNDATION AND OTHERS. AT WHICH POINT THE NEW ACCESS ROAD WILL BE FORMED (TO SUB BASE ONLY TO PREVENT MUD TRANSFER OFF SITE) - THIS WILL THEN FORM THE NEW SITE ACCESS AND SITE DELIVERY AREA. THE STEEL MESH SECURITY GATE WILL ALSO BE RELOCATED TO THE NEW ACCESS POINT AND THE ORIGINAL MADE SECURE. STAFF PARKING WILL ALSO BE RELOCATED TO THE DRIVEWAYS TO THE PROPOSED DWELLINGS - WHICH WILL BE CONSTRUCTED TO SUB BASE LEVEL - TO PREVENT MUD TRANSFER OFF SITE.

THERE WILL BE WATER ON SITE SO WHEEL WASHING WILL TAKE PLACE WHEN NECESSARY TO LIMIT THE IMPACT OF MUD ETC WHEN LEAVING THE SITE.

HOURS OF WORK WILL BE AS REQUIRED IN PLANNING CONDITION TO REDUCE THE IMPACT AND NOISE ON THE RESIDENTS IN CLOSE PROXIMITY TO THE DEVELOPMENT

A TREE PROTECTION FENCE IS SHOWN ON THE DRAWING AND IS TO BE IN PLACE PRIOR TO COMMENCEMENT AND IS TO REMAIN IN PLACE THROUGHOUT THE CONSTRUCTION PHASE AND WILL NOT BE MOVED OR RELOCATED - AND WILL HAVE SIGNAGE INDICATING THAT IT IS FOR TREE PROTECTION AND THAT NO MATERIALS ARE TO BE STORED OR ANY EXCAVATIONS ARE TO TAKE PLACE NEAR IT. ALL SITE STAFF WILL BE MADE AWARE OF THE NEED OF PROTECTION MEASURES WITH REGARD TO WORKING NEAR THE TREES SHOWN ON THE PLAN.

THE MAIN STORAGE OF BULK MATERIALS WILL BE AS SHOWN ON THE PLAN - ITS LOCATION IS TO AVOID THE VISUAL IMPACT ON LOCAL RESIDENTS AND WILL NOT EFFECT THE PROTECTED TREES DURING THE CONSTRUCTION PHASE.

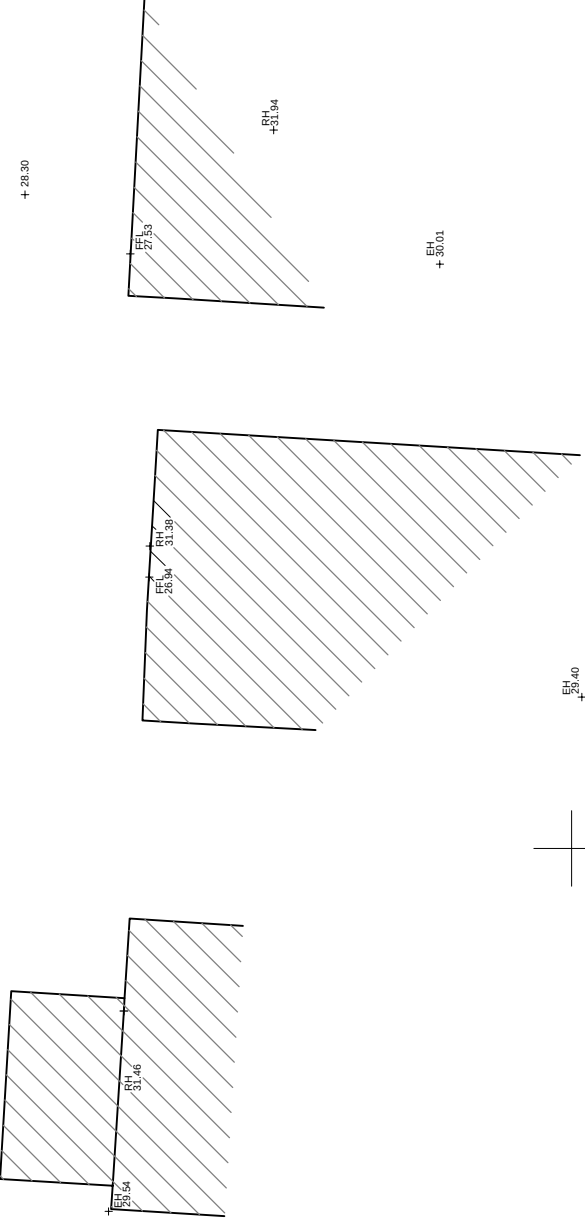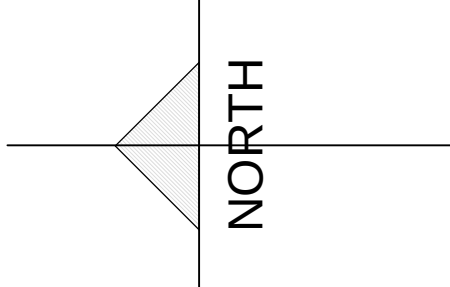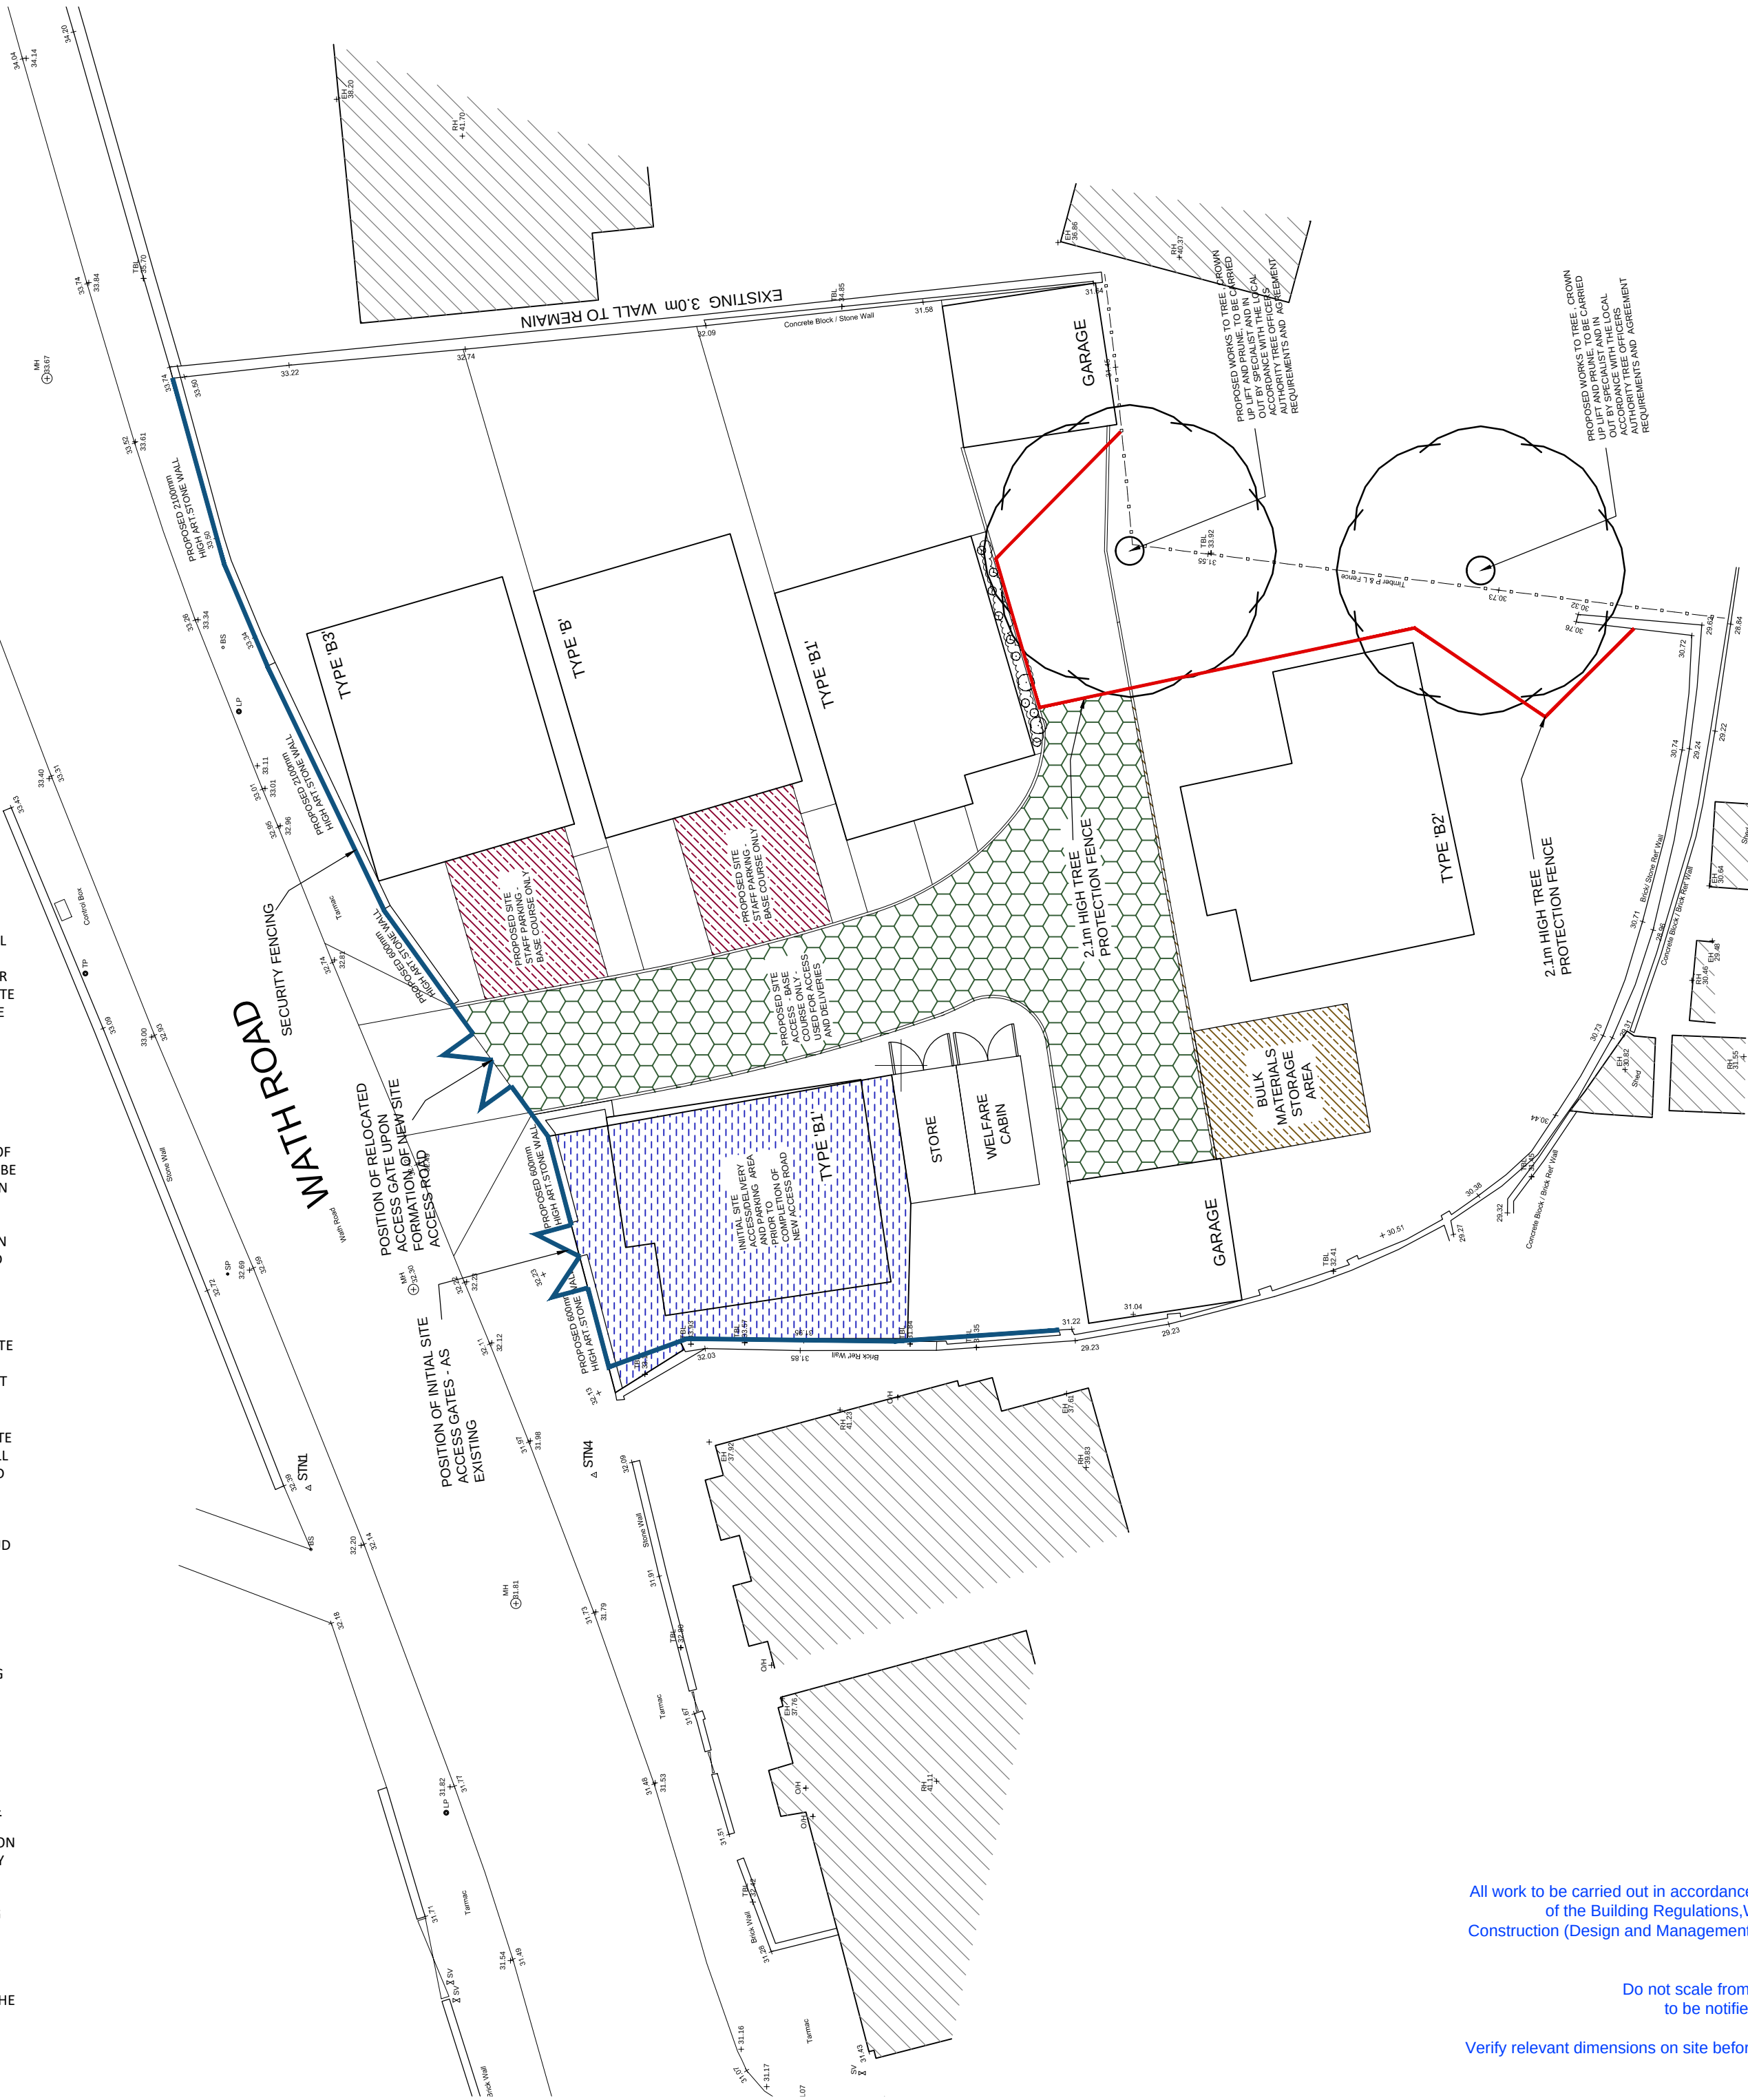

All work to be carried out in accordance with the requirements of the Building Regulations, Water Authority and the Construction (Design and Management) Regulations currently in force.

Do not scale from this drawing. Architect to be notified of any discrepancies.

Verify relevant dimensions on site before commencing work or preparing shop drawings.

Rev:	Description:	By:	Date:
Drawing Status:		PLANNING	
E ETON CONSTRUCTION 79A WELLGATE, ROTHERHAM, S60 2LZ Tel: 01709 365 964 Website: www.etonconstruction.com			
Project:		Development of land off Wath Road, Bolton Upon Dearne	
Drawing:		Proposed Site Set up - Layout	
Client:		Eton Homes Ltd	
COPYRIGHT – This drawing is subject to copyright and cannot be reproduced without the permission of the Company.			©
Scales:		Date:	
1:200 @A2		22.12.16	
Drawing Number:		Revision:	Drawn by:
EC06-36		-	MW
