


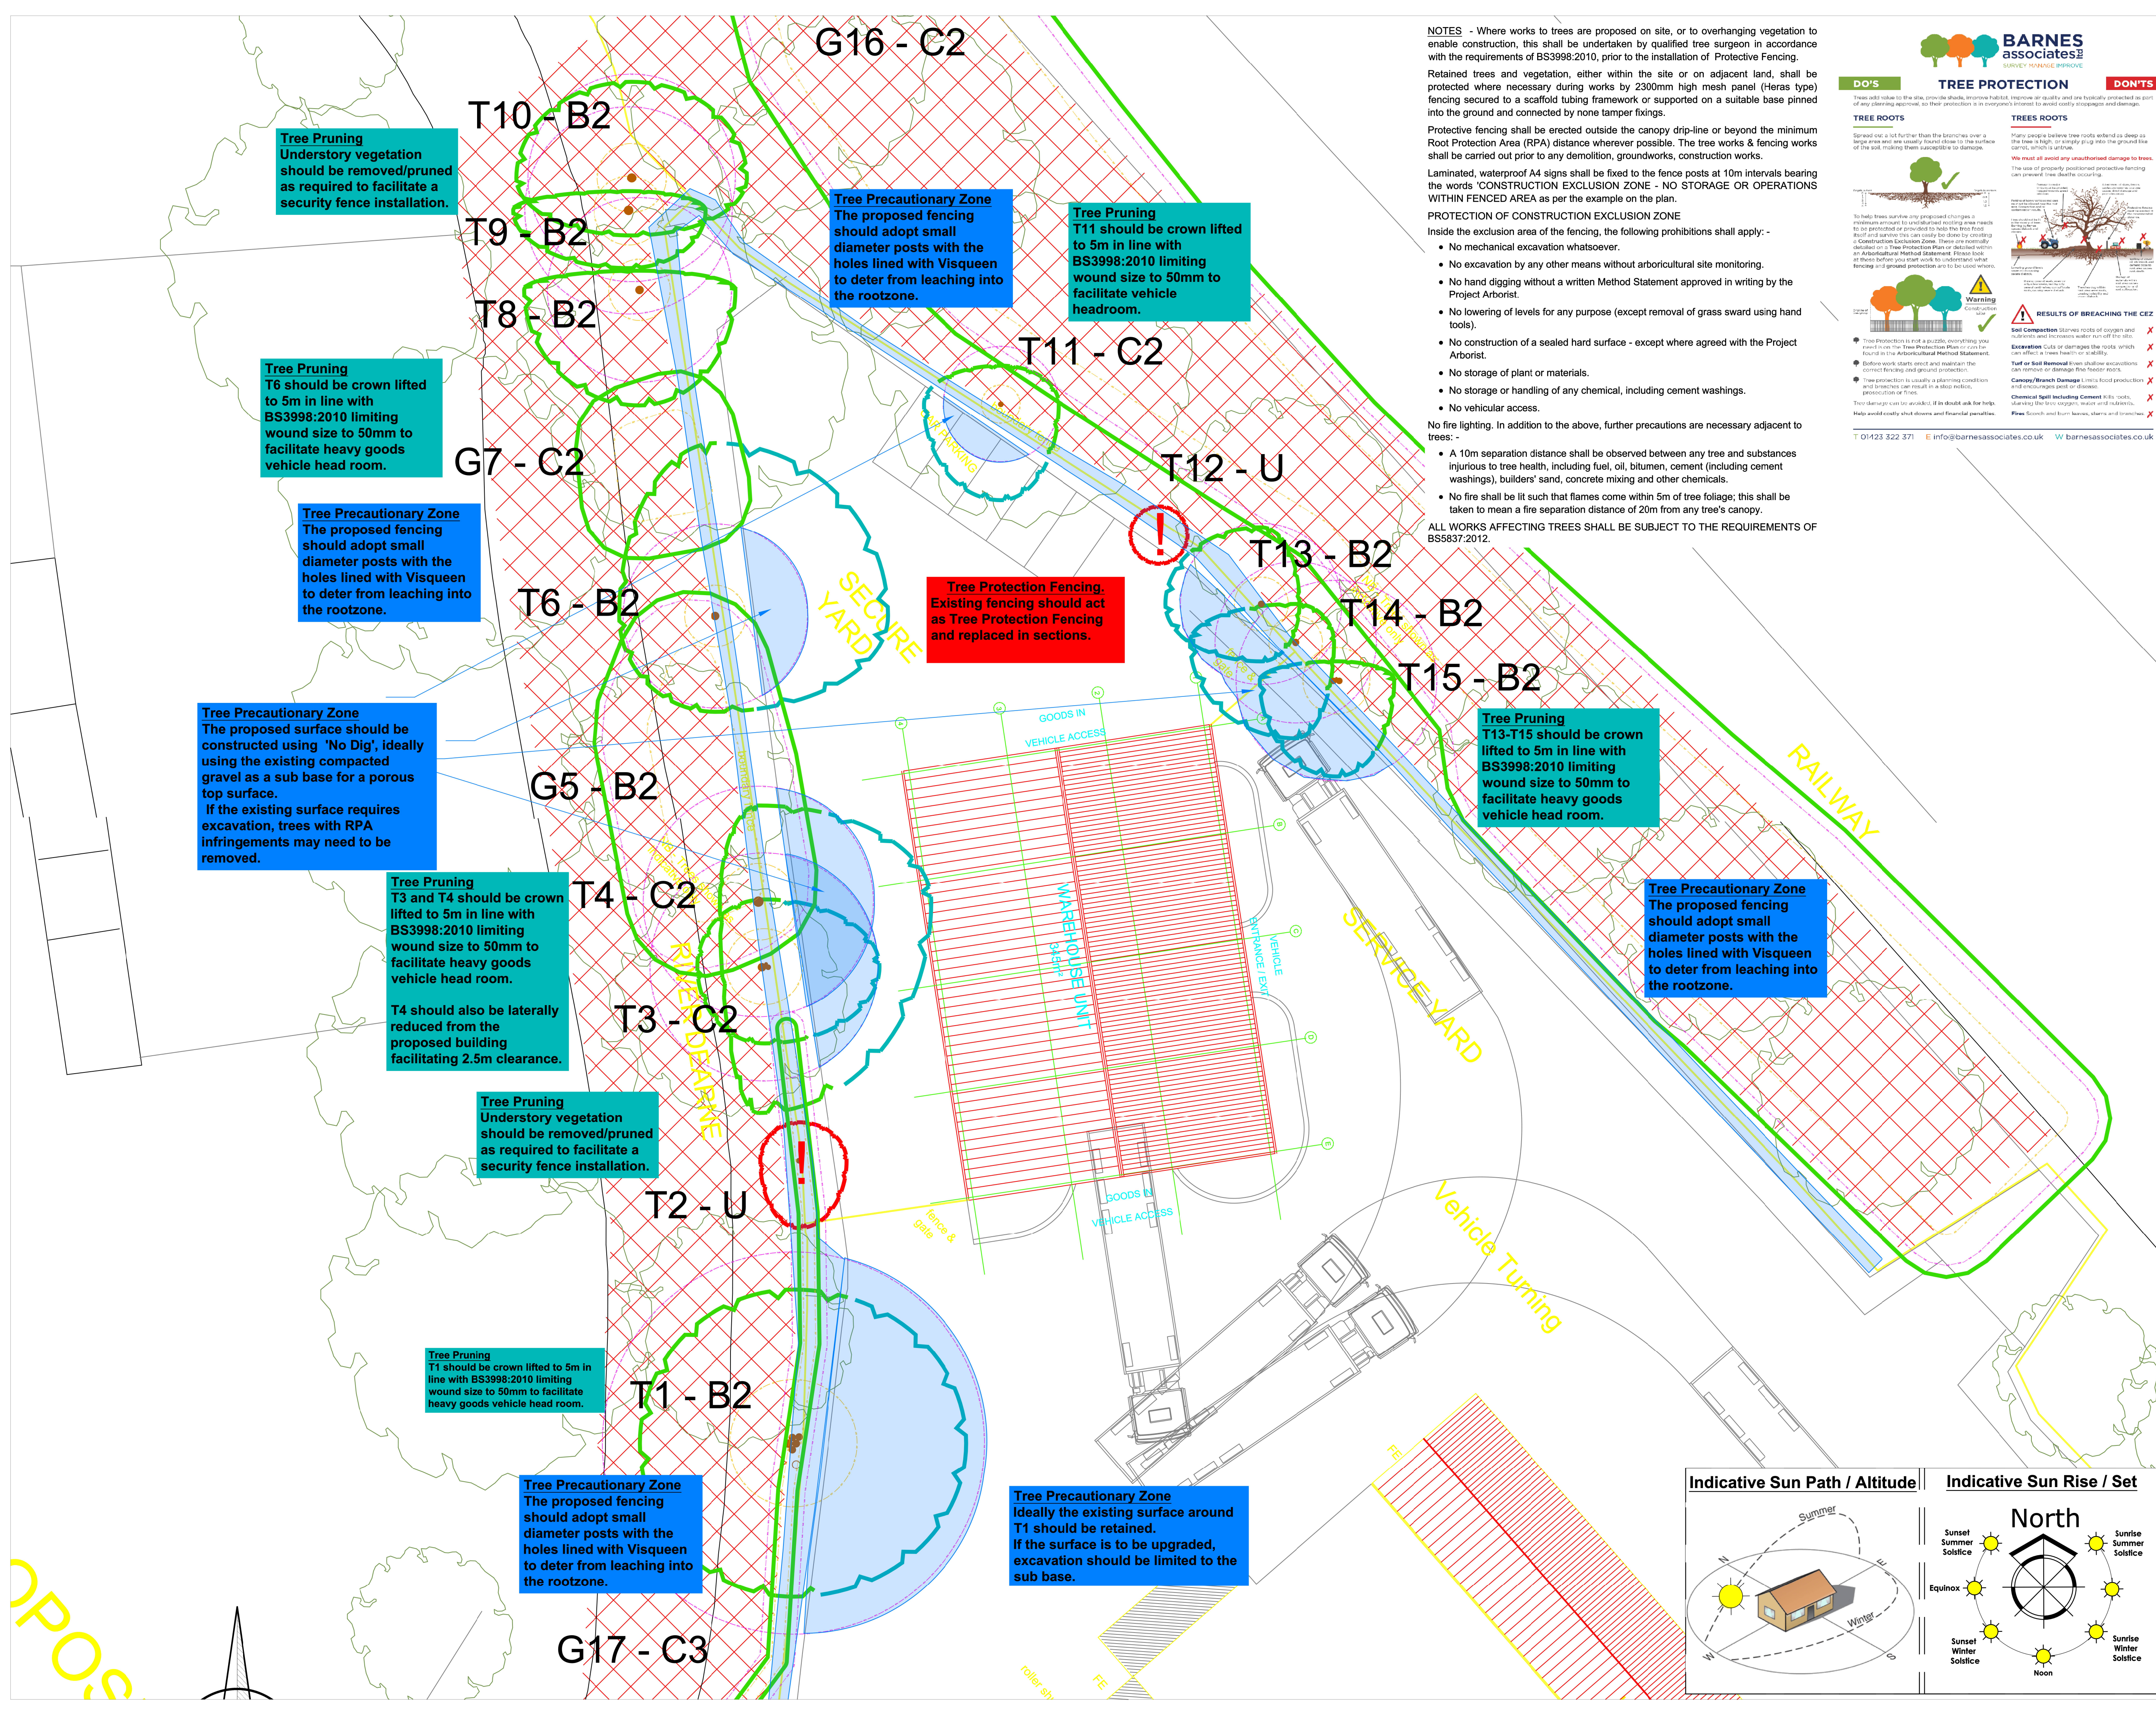

NOTES - Where works to trees are proposed on site, or to overhanging vegetation to enable construction, this shall be undertaken by qualified tree surgeon in accordance with the requirements of BS3998:2010, prior to the installation of Protective Fencing.

Retained trees and vegetation, either within the site or on adjacent land, shall be protected where necessary during works by 2300mm high mesh panel (Heras type) fencing secured to a scaffold tubing framework or supported on a suitable base pinned into the ground and connected by none tamper fixings.

Protective fencing shall be erected outside the canopy drip-line or beyond the minimum Root Protection Area (RPA) distance wherever possible. The tree works & fencing works shall be carried out prior to any demolition, groundworks, construction works.

Laminated, waterproof A4 signs shall be fixed to the fence posts at 10m intervals bearing the words 'CONSTRUCTION EXCLUSION ZONE - NO STORAGE OR OPERATIONS WITHIN FENCED AREA as per the example on the plan.

PROTECTION OF CONSTRUCTION EXCLUSION ZONE

Inside the exclusion area of the fencing, the following prohibitions shall apply:-

- No mechanical excavation whatsoever.
- No excavation by any other means without arboricultural site monitoring.
- No hand digging without a written Method Statement approved in writing by the Project Arborist.
- No lowering of levels for any purpose (except removal of grass sward using hand tools).
- No construction of a sealed hard surface - except where agreed with the Project Arborist.
- No storage of plant or materials.
- No storage or handling of any chemical, including cement washings.
- No vehicular access.

No fire lighting. In addition to the above, further precautions are necessary adjacent to trees:-

- A 10m separation distance shall be observed between any tree and substances injurious to tree health, including fuel, oil, bitumen, cement (including cement washings), builders' sand, concrete mixing and other chemicals.
- No fire shall be lit such that flames come within 5m of tree foliage; this shall be taken to mean a fire separation distance of 20m from any tree's canopy.

ALL WORKS AFFECTING TREES SHALL BE SUBJECT TO THE REQUIREMENTS OF BS5837:2012.

DO'S

TREE ROOTS

Trees add value to the site, provide shade, improve habitat, improve air quality and are typically protected as part of any planning approval, so their protection is in everyone's interest to avoid costly stoppage and damage.

To help trees survive any proposed changes a minimum amount to undisturbed rooting area needs to be protected or provided to help the tree from root and survive this can only be done by creating a Construction Exclusion Zone. These are normally defined on a Tree Protection Plan or decided within an Arboricultural Method Statement. Please look at them before you start work to understand what fencing and ground protection are to be used where.

Warning

Ground protection

DON'TS

TREE ROOTS

Many people believe tree roots extend as deep as the tree is high, or simply plug into the ground like a carrot, which is untrue.

We must all avoid any unauthorised damage to trees.

The use of properly positioned protective fencing can prevent tree deaths occurring.

RESULTS OF BREACHING THE CEZ


- Soil Compaction starves roots of oxygen and nutrients and increases water run off the site.
- Excavation cuts or damages the roots which can affect a tree's health or stability.
- Turf or Soil Removal from shallow excavations can remove or damage fine feeder roots.
- Canopy/Branch Damage Limits food production and encourages pest or disease.
- Chemical Spill including Cement kills roots, starves the tree oxygen, water and nutrients.
- Fire Scorch and burn leaves, stems and branches.

The damage can be avoided if it is avoided ask the help. Help avoid costly shut downs and financial penalties.

T: 01423 322 371 E: info@barnesassociates.co.uk W: barnesassociates.co.uk

© Barnes Associates Ltd. This plan should be viewed in **COLOUR**, please do not scale from this drawing, all dimensions should be checked on site, any errors or divergences should be brought to the attention of Barnes Associates Ltd. All right described in Chapter IV of the Copyright, Design & Patents Act 1988 have been generally asserted and copyright of this plan remains with Barnes Associates Ltd until all fees are paid in full.

Individual Tree Symbols

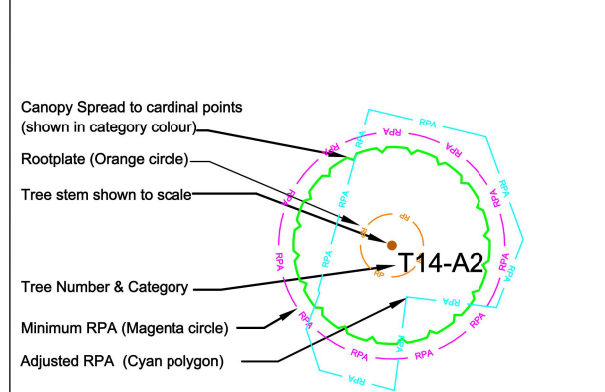

Tree Protection Methods

Construction Exclusion Zone (CEZ)
Indicated by the red Net Hatching. These are 'NO-GO ZONES' for site works, storage and operatives.
To be protected by appropriate Fencing and/or Ground protection. These areas shall be identified with signage.

Tree Precautionary Zone - (TPZ)
Indicated by Blue shading.
Tree root activity is likely in these areas and will need to be appropriately protected before the start of the works.
Materials and methods need to limit excavation, root loss or damage to soils.

Notes:

Plan is based upon the supplied topographical Survey Plan. Copies of this plan are available in CAD Formats .dwg & .dxf upon request.

Drainage/Utility layout not provided.

Existing/Proposed level data not provided.

Excavation dimensions/battering not provided.

No detailed cross sections/drawings provided of structures.

Revision	Description
A	05/09/2024 Preliminary Issue

N

1:150

0m

Client:

PB Architects

Drawn at:

Project:

Darton Business Park, S75 5QX

Title:

Tree Protection Plan

Drawing No:

BA24208TPP

Scale:

1:150 @ A1

Date:

05/09/2024

Drawn By:

MM

Checked:

TG

Approved:

SB

BARNES associates

SURVEY MANAGE IMPROVE

Ground Floor 5 St James Square
Boroughbridge YO51 9AS
T 01423 322371
E info@barnesassociates.co.uk
W barnesassociates.co.uk
Company number 10438116
Registered in England and Wales

Arboricultural Association

Chartered Institute of Horticulture

BALI

Arboricultural Association

Chartered Institute of Horticulture

BALI
