New Roundabouts
Higham Common Rd & Barugh Green Rd (Rev 2)

STRATA STERLING BARNSLEY WEST

12/09/23
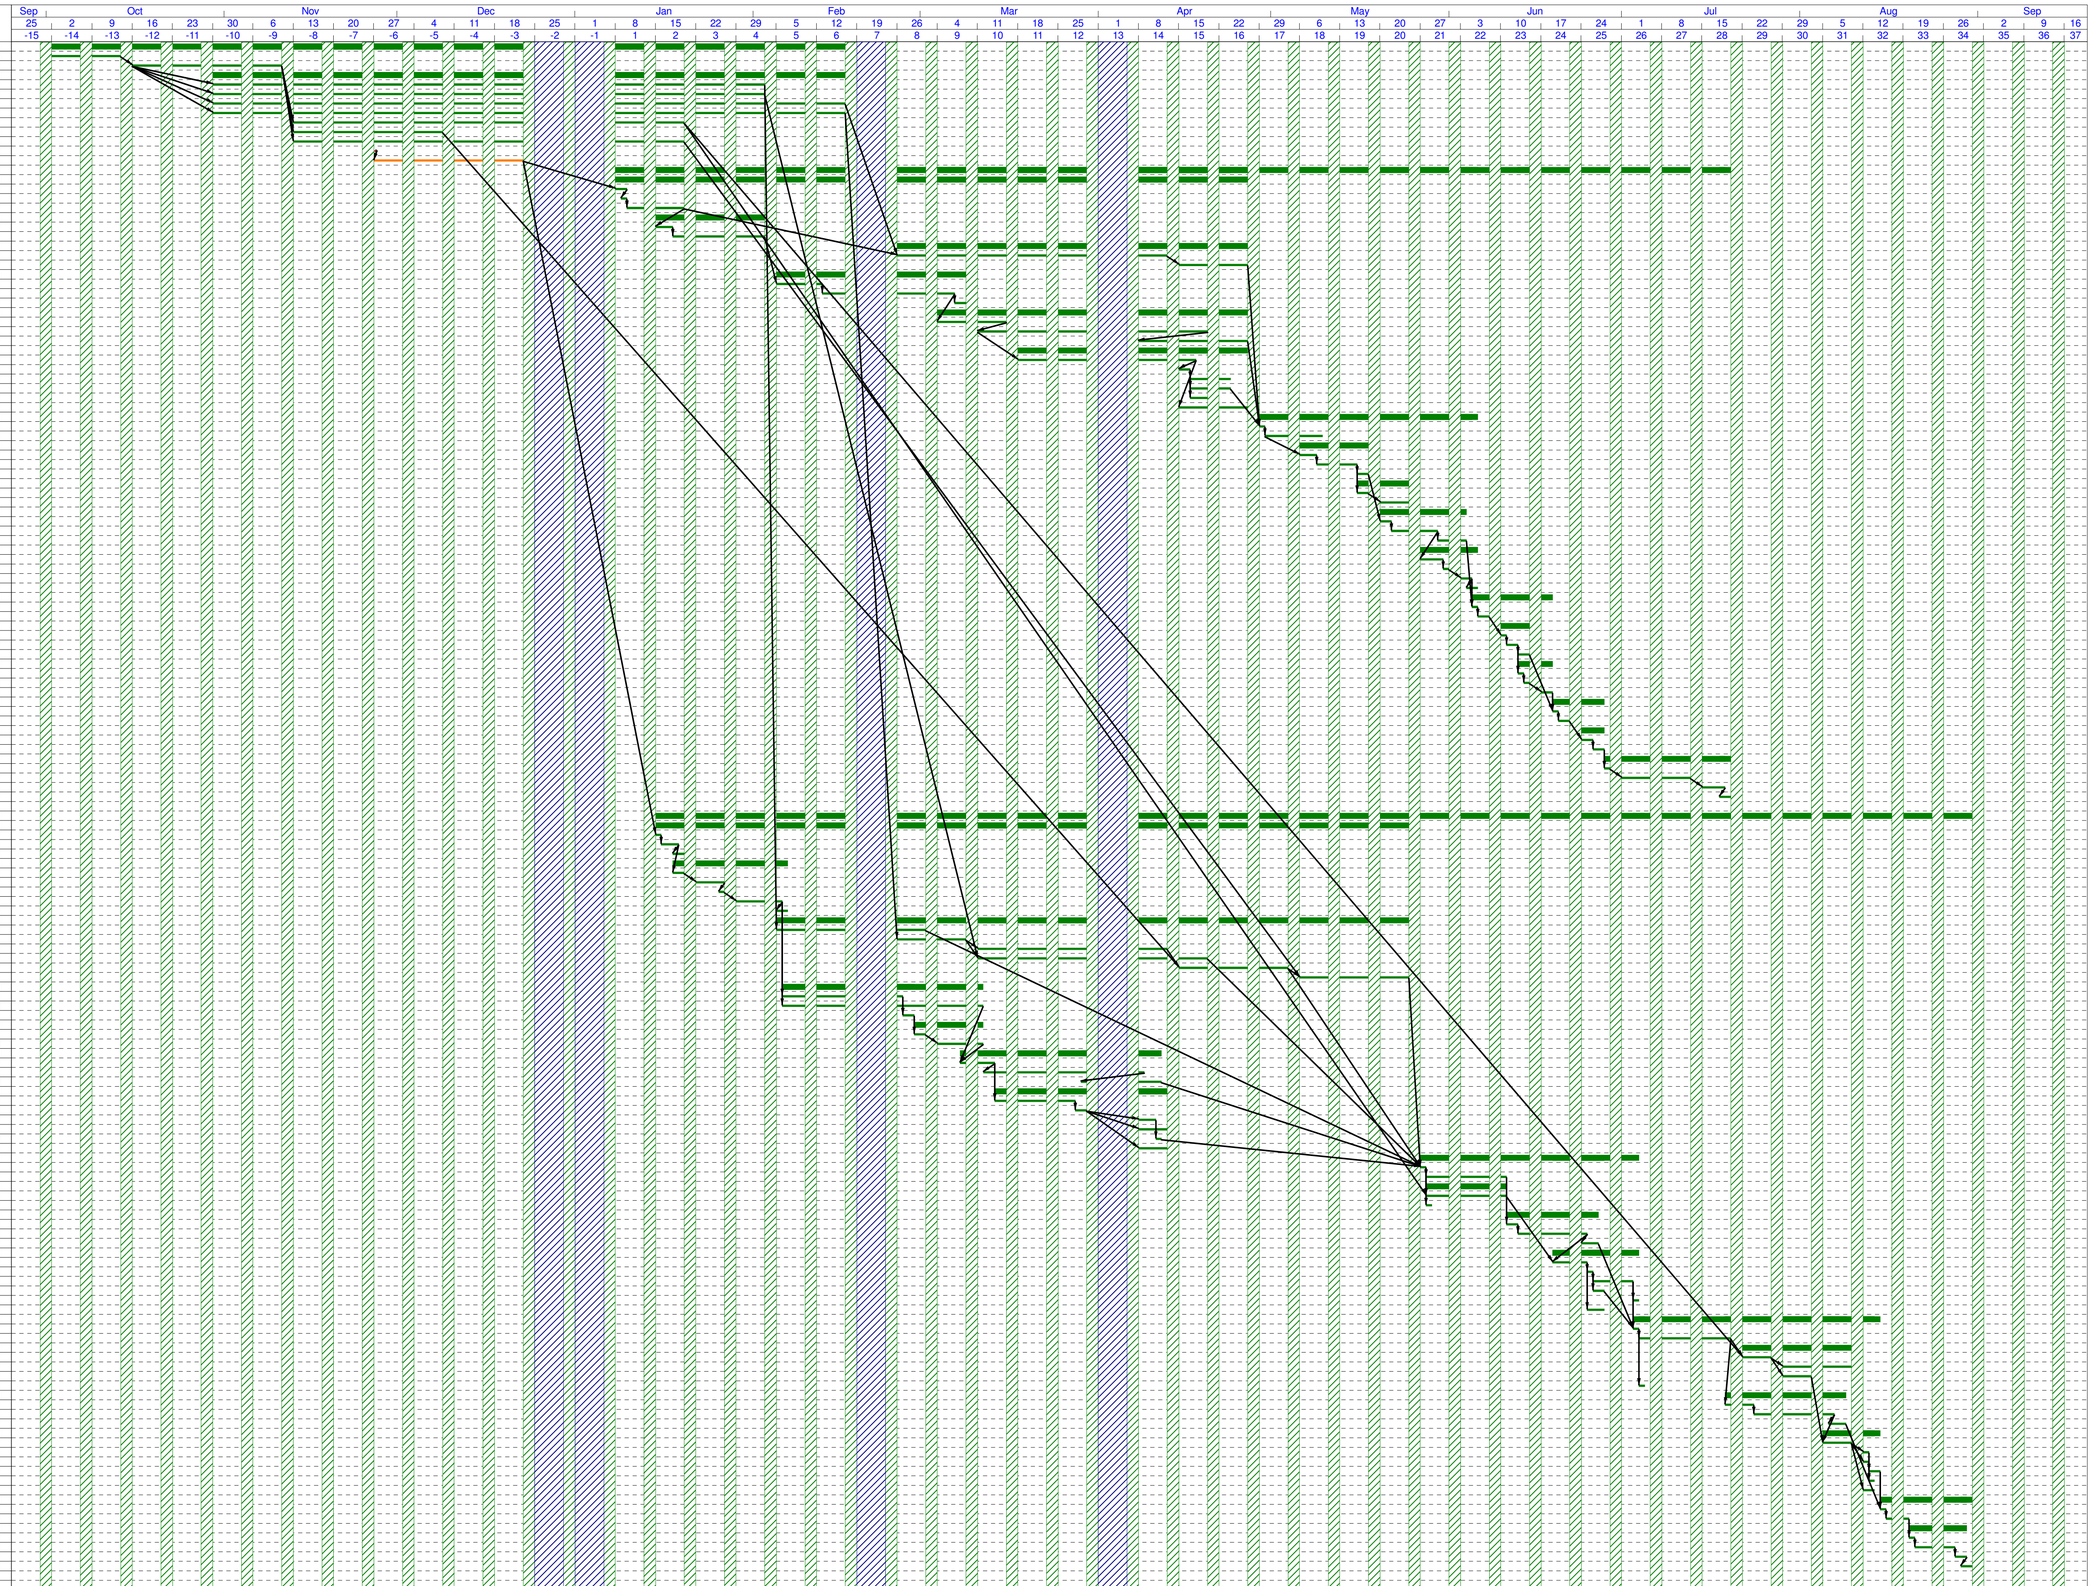
ID	Name	Start	Duration	Finish
1	**Service Preparation Works**	**02/10/23**	**90d**	**16/02/24**
2	Update and Complete all C4s	02/10/23	10d	13/10/23
3	Payment to Utility Companies	16/10/23	20d	10/11/23
4	**Discuss/Agree Utility Programme of Works**	**30/10/23**	**70d**	**16/02/24**
5	NPG Lead Time	30/10/23	60d	02/02/24
6	NGN Lead Time	30/10/23	60d	02/02/24
7	YWA Lead Time (HCR)	30/10/23	70d	16/02/24
8	YWA Lead Time (BGR)	30/10/23	70d	16/02/24
9	BT Openreach Lead Time	13/11/23	40d	19/01/24
10	Zayo Lead Time	13/11/23	20d	08/12/23
11	Virgin Lead Time	13/11/23	40d	19/01/24
12	Notice of Award	27/11/23	0d	27/11/23
13	Mobilisation	27/11/23	20d	22/12/23
14	High Common Road	08/01/24	130d	19/07/24
15	Area 1	**08/01/24**	**70d**	**26/04/24**
16	Site Establishment	08/01/24	2d	09/01/24
17	Traffic Management	09/01/24	1d	09/01/24
18	Site Clearance	10/01/24	8d	19/01/24
19	**Earthworks**	**15/01/24**	**15d**	**02/02/24**
20	Topsoil	15/01/24	3d	17/01/24
21	Cut/Fill	18/01/24	12d	02/02/24
22	**Service Diversions**	**26/02/24**	**40d**	**26/04/24**
23	YWA (off-site)	26/02/24	30d	12/04/24
24	YWA (on-site)	15/04/24	10d	26/04/24
25	**Surface Water Drainage**	**05/02/24**	**20d**	**08/03/24**
26	Manholes - 2G	05/02/24	6d	12/02/24
27	Pipework - 2G	13/02/24	12d	06/03/24
28	Gullys	07/03/24	2d	08/03/24
29	**Road Construction**	**04/03/24**	**35d**	**26/04/24**
30	Type 1 Sub-base	04/03/24	10d	15/03/24
31	Kerbs/Channels - 2G	11/03/24	25d	19/04/24
32	Tarmac	08/04/24	15d	26/04/24
33	**Footpath/RAB border**	**18/03/24**	**25d**	**26/04/24**
34	Edging	18/03/24	18d	17/04/24
35	Type 1 Sub-base	15/04/24	2d	16/04/24
36	Block Paving	17/04/24	5d	23/04/24
37	Tarmac	17/04/24	5d	23/04/24
38	Tactiles	17/04/24	3d	19/04/24
39	Grass Verge	15/04/24	10d	26/04/24
40	**Area 2**	**29/04/24**	**28d**	**05/06/24**
41	Traffic Management	29/04/24	1d	29/04/24
42	Site Clearance	30/04/24	8d	09/05/24
43	**Attenuation Tank**	**06/05/24**	**10d**	**17/05/24**
44	Excavation & Preparation	06/05/24	3d	08/05/24
45	Installation	09/05/24	5d	15/05/24
46	Backfill	16/05/24	2d	17/05/24
47	**Surface Drainage**	**16/05/24**	**7d**	**24/05/24**
48	Gullys & Manholes	16/05/24	2d	17/05/24
49	Pipework	20/05/24	5d	24/05/24
50	**Road Construction**	**20/05/24**	**11d**	**03/06/24**
51	Type 1 Sub-base	20/05/24	2d	21/05/24
52	Kerbs/Channels	22/05/24	6d	29/05/24
53	Tarmac	30/05/24	3d	03/06/24
54	**Footpath**	**27/05/24**	**8d**	**05/06/24**
55	Edging	27/05/24	4d	30/05/24
56	Type 1 Sub-base	31/05/24	1d	31/05/24
57	Tarmac	03/06/24	2d	04/06/24
58	Grass Verge	04/06/24	2d	05/06/24
59	**Area 3**	**05/06/24**	**10d**	**18/06/24**
60	Traffic Management	05/06/24	1d	05/06/24
61	Site Clearance	06/06/24	2d	07/06/24
62	**Road Construction**	**10/06/24**	**5d**	**14/06/24**
63	Type 1 Sub-base	10/06/24	1d	10/06/24
64	Kerbs/Channels	11/06/24	2d	12/06/24
65	Tarmac	13/06/24	2d	14/06/24
66	**Footpaths**	**13/06/24**	**4d**	**18/06/24**
67	Edgings	13/06/24	1d	13/06/24
68	Type 1 Sub-base	14/06/24	1d	14/06/24
69	Tarmac	17/06/24	2d	18/06/24
70	**Area 4**	**19/06/24**	**7d**	**27/06/24**
71	Traffic Management	19/06/24	1d	19/06/24
72	Site Clearance	20/06/24	2d	21/06/24
73	**Road Construction**	**24/06/24**	**4d**	**27/06/24**
74	Type 1 Sub-base	24/06/24	2d	25/06/24
75	Tarmac	26/06/24	2d	27/06/24
76	**Area 5**	**28/06/24**	**16d**	**19/07/24**
77	Traffic Management	28/06/24	1d	28/06/24
78	Surfacing	01/07/24	10d	12/07/24
79	Road Marking	15/07/24	4d	18/07/24
80	Clear Site & Snags	18/07/24	2d	19/07/24
81				
82	**Barugh Green Road**	**15/01/24**	**155d**	**30/08/24**
83	**Area 1**	**15/01/24**	**85d**	**24/05/24**
84	Site Establishment	15/01/24	1d	15/01/24
85	Site Clearance	16/01/24	3d	18/01/24
86	Excavate footpath & kerbs	18/01/24	2d	19/01/24
87	**Earthworks**	**18/01/24**	**14d**	**06/02/24**
88	Topsoil	18/01/24	2d	19/01/24
89	Cut/Fill	22/01/24	5d	26/01/24
90	Trial Holes	26/01/24	1d	26/01/24
91	Turnover	29/01/24	6d	05/02/24
92	Geogrid Stitching	05/02/24	2d	06/02/24
93	**Service Diversions**	**05/02/24**	**70d**	**24/05/24**
94	NPG (off-site)	05/02/24	15d	01/03/24
95	YWA (off-site)	26/02/24	10d	08/03/24
96	YWA (on-site)	11/03/24	20d	12/04/24
97	NGN (off-site)	11/03/24	25d	19/04/24
98	Zayo (on-site)	15/04/24	15d	03/05/24
99	Virgin (on-site)	06/05/24	15d	24/05/24
100	**Surface Drainage**	**06/02/24**	**20d**	**11/03/24**
101	Manholes	06/02/24	10d	26/02/24
102	Pipework	06/02/24	20d	11/03/24
103	Gullys	27/02/24	2d	28/02/24
104	**Foul Drainage**	**29/02/24**	**8d**	**11/03/24**
105	Manholes	29/02/24	2d	01/03/24
106	Pipework	04/03/24	6d	11/03/24
107	**Road Construction**	**08/03/24**	**20d**	**11/04/24**
108	Type 1 Sub-base	08/03/24	4d	13/03/24
109	Kerbs/Channels	12/03/24	15d	08/04/24
110	Tarmac	29/03/24	5d	11/04/24
111	**Footpath/RAB border**	**14/03/24**	**17d**	**12/04/24**
112	Edging	14/03/24	10d	27/03/24
113	Type 1 Sub-base	28/03/24	2d	29/03/24
114	Block Paving	08/04/24	3d	10/04/24
115	Tarmac	08/04/24	5d	12/04/24
116	Tactiles	11/04/24	1d	11/04/24
117	Grass Verge	08/04/24	5d	12/04/24
118	**Area 2**	**27/05/24**	**28d**	**03/07/24**
119	Traffic Management	27/05/24	1d	27/05/24
120	Site Clearance	28/05/24	10d	10/06/24
121	**Services**	**28/05/24**	**10d**	**10/06/24**
122	BT Openreach(Ducts by CORE)	28/05/24	10d	10/06/24
123	Surface Drainage	28/05/24	1d	28/05/24
124	**Road Construction**	**11/06/24**	**12d**	**26/06/24**
125	Type 1 Sub-base	11/06/24	2d	12/06/24
126	Kerbs/Channels	13/06/24	8d	24/06/24
127	Tarmac	24/06/24	3d	26/06/24
128	**Footpath/RAB border**	**19/06/24**	**11d**	**03/07/24**
129	Edging	19/06/24	4d	24/06/24
130	Type 1 Sub-base	25/06/24	1d	25/06/24
131	Block Paving	26/06/24	5d	02/07/24
132	Tarmac	26/06/24	2d	27/06/24
133	Tactiles	03/07/24	1d	03/07/24
134	Grass Verge	25/06/24	3d	27/06/24
135	**Area 3**	**03/07/24**	**31d**	**14/08/24**
136	Traffic Management	03/07/24	1d	03/07/24
137	Site Clearance	04/07/24	12d	19/07/24
138	**Services**	**22/07/24**	**15d**	**09/08/24**
139	BT Openreach (Ducts by CORE)	22/07/24	5d	26/07/24
140	BT Openreach (JBNs & Cables)	29/07/24	10d	09/08/24
141	Virgin	29/07/24	5d	02/08/24
142	Surface Drainage	04/07/24	1d	04/07/24
143	**Road Construction**	**19/07/24**	**15d**	**08/08/24**
144	Type 1 Sub-base	19/07/24	3d	23/07/24
145	Kerbs/Channels	24/07/24	10d	06/08/24
146	Tarmac	06/08/24	3d	08/08/24
147	**Footpath/RAB border**	**05/08/24**	**8d**	**14/08/24**
148	Edging	05/08/24	5d	09/08/24
149	Type 1 Sub-base	12/08/24	1d	12/08/24
150	Block Paving	12/08/24	1d	12/08/24
151	Tarmac	13/08/24	2d	14/08/24
152	Tactiles	13/08/24	1d	13/08/24
153	Grass Verge	12/08/24	2d	13/08/24
154	**Area 4**	**15/08/24**	**12d**	**30/08/24**
155	Traffic Management	15/08/24	1d	15/08/24
156	Site Clearance	16/08/24	2d	19/08/24
157	**Road Construction**	**20/08/24**	**8d**	**29/08/24**
158	Type 1 Sub-base	20/08/24	1d	20/08/24
159	Tarmac	21/08/24	5d	27/08/24
160	Road Lining	28/08/24	2d	29/08/24
161	Clear Site & Snags	29/08/24	2d	30/08/24
162				
163				
164
