BMBC
CORRESPONDENCE ROOM
P+T DM
NO Cha
18 FEB 2016
Received by: LJ
ORIGINAL COPY

P. Dimelow
B.A. hons Dip Arch. M.A.
Architectural Design and
Planning Consultant

E Mail. pdimelow@live.co.uk

Dept of Planning
& MBC
PO Box 634
Barnsley

February 17. 2016

2016 - 0057

Fao Steve Kirkham.

Further to our telephone conversation. my client has been able to find the borehole information for the development of shops and flats adjacent hope this complies with your request for further information.
As discussed if our application is successful we will provide any further details or information.

Many thanks

Peter Dimelow.

Ash Barn
Finkle Street
Wortley
Sheffield.
S35 7DH 0114 2884937
Mobile: 07710 554691

DAILY RETURN
(Drilling)

1 OF 3

GDC

Date 31/1/12 Working Day No. 1

Contract Name FORMER PHOENIX GYM, RAMSGATE

Contract No. 5010

Dayworks Were Executed Today

Daywork No.

Hole No.	Depth	Casing	Dia	Angle	From	To	Description
							MOBILISED CATAGRANDER C6
							DRAWN UP WATER PUMP
							DRAWN CREW, ANCILLARY
							PLANT AND EQUIPMENT AND
							TOOLING/HIRE WATER STANDPIPE
							AND LICENCE.
1	21.00	2.00	100MM	V	0.00	1.40	MADE GROUND / FILL
					1.40	2.00	CLAY
					2.00	7.10	SANDSTONE
					7.10	7.60	DARK MUDSTONE
					7.60	16.10	SANDSTONE
					16.10	16.80	COAL
					16.80	18.90	SANDSTONE
					18.90	19.80	COAL
					19.80	21.00	SANDSTONE.
							FLUSH FLUSH THROUGHOUT.
							(WATER)

1	21.00	2.00	SHEET TOTAL	CREW	PLANT
—	—	—	PREVIOUS SHEET TOTAL	D. EDWARDS	CATAGRANDER C6
1	21.00	2.00	CUMULATIVE TOTAL	A. HOLFIELD	2" PUMP
					VW VAN

Signed by G.D.C. J Edwards Date 31-1-12

Signed by CLIENT Date

CLIENT COPY - WHITE
Q.S. COPY - YELLOW
SITE COPY - PINK

NO CLAIM CAN BE ACCEPTED UNLESS REPORTED IN WRITING WITHIN 14 DAYS OF THIS RETURN

DAILY RETURN
(Drilling)

2 OF 3

GDC

Date 31/1/12 Working Day No. 1

Contract Name PHOENIX LYNN

Contract No. 5010

Dayworks Were Executed Today

Daywork No.

Hole No.	Depth	Casing	Dia	Angle	From	To	Description
2	21.60	2.20	100mm	V	0-00	1.40	MADE GROUND/ FILL
					1.40	2.20	CLAY
					2.20	6.60	SANDSTONE
					6.60	7.20	COAL
					7.20	17.90	SANDSTONE
					17.90	18.50	COAL
					18.50	21.60	SANDSTONE/ MUDSTONE
							FULL WATER FLUSH TIMEVERTICAL
3	21.00	2.20	100mm	V	0-00	2.20	FILLING
					2.20	7.00	SANDSTONE
					7.00	7.60	DARK MUDSTONE
					7.60	17.90	SANDSTONE
					17.90	18.80	COAL
					18.80	21.00	SANDSTONE
							FULL WATER FLUSH TIMEVERTICAL

2	41.60	4.40	SHEET TOTAL	CREW	PLANT
1	21.00	2.00	PREVIOUS SHEET TOTAL	D. EDWARDS A. HALIFAX	CR (c/w Pump) 2" PUMP V-W VAN
3	63.60	6.40	CUMULATIVE TOTAL		

Signed by G.D.C. Date 31-1-12

Signed by CLIENT Date

CLIENT COPY - WHITE
Q.S. COPY - YELLOW
SITE COPY - PINK

NO CLAIM CAN BE ACCEPTED UNLESS REPORTED IN WRITING WITHIN 14 DAYS OF THIS RETURN

DAILY RETURN
(Drilling) 3 of 3

GDC

Date 31/1/12 Working Day No. 1

Contract Name RIDGEWAY WIND

Contract No. SC10

Dayworks Were Executed Today

Daywork No.

Hole No.	Depth	Casing	Dia	Angle	From	To	Description
S	21.00	2.50	100mm	V	0.00	1.70	FILL
					1.70	2.50	CLAY
					2.50	6.50	SANDSTONE/ MUDSTONE
					6.50	7.70	COAL
					7.70	17.70	SANDSTONE/ MUDSTONE
					17.70	18.00	COAL
					18.00	21.00	SANDSTONE/ MUDSTONE
							FULL WATER FLUSH THROUGHOUT
4	21.00	2.80	100 m	V	0.00	1.40	MADE
					1.40	2.80	CLAY
					2.80	7.50	SANDSTONE
					7.50	7.70	DARK MUDSTONE
					7.90	16.60	SANDSTONE
					16.60	16.80	COAL
					16.80	19.00	SANDSTONE
					19.00	20.00	COAL
					20.00	21.00	SANDSTONE
							FULL WATER FLUSH RETURNS
							CUTTINGS WATER WATER OVER TO
							FORCAPTED FIRST, SECURED
							PUMP AND REMAINDER.
2	42.00	5.20	SHEET TOTAL				CREW: D. KINGSMILL, A. HOLLINGWORTH
3	63.60	6.40	PREVIOUS SHEET TOTAL				PLANT: C6 (c/w PUMP), 2" PUMP, UW VAN
5	105.60	11.70	CUMULATIVE TOTAL				

Signed by G.D.C. Date 31-1-12

Signed by CLIENT Date

CLIENT COPY - WHITE
Q.S. COPY - YELLOW
SITE COPY - PINK

NO CLAIM CAN BE ACCEPTED UNLESS REPORTED IN WRITING WITHIN 14 DAYS OF THIS RETURN

DAILY RETURN
(Drilling) 1 of 2

GDC

Date 1/2/12 Working Day No. 2

Contract Name PITCAIRN LOW

Contract No. 5810

Dayworks Were Executed Today

Daywork No.

Hole No.	Depth	Casing	Dia	Angle	From	To	Description
6	21.00	2.70	100mm	V	0.00	2.70	RUBBISH
					2.70	7.10	SANDSTONE/ MUDSTONE
					7.10	7.50	DARK MUDSTONE
					7.50	16.90	SANDSTONE
					16.90	17.70	COAL
					17.70	18.50	SANDSTONE
					18.50	19.70	COAL
					19.70	21.00	SANDSTONE.
							FULL FLUSH THROUGHOUT.
8	21.00	1.50	100mm	V	0.00	0.80	FILL
					0.80	1.50	CLAY
					1.50	7.00	SANDSTONE
					7.00	7.50	DARK MUDSTONE
					7.50	18.50	SANDSTONE
					18.50	19.50	COAL
					19.50	21.00	SANDSTONE.
							FULL FLUSH THROUGHOUT.
2	42.00	3.70	SHEET TOTAL		CREW		PLANT
5	105.60	11.70	PREVIOUS SHEET TOTAL		D. EDWARDS		CK (clw pump)
7	147.60	15.40	CUMULATIVE TOTAL		A. HEATHCOTE		4" pump
							VW WAN

Signed by G.D.C. Date 1-2-12

Signed by CLIENT Date

CLIENT COPY - WHITE
O.S. COPY - YELLOW
SITE COPY - PINK

NO CLAIM CAN BE ACCEPTED UNLESS REPORTED IN WRITING WITHIN 14 DAYS OF THIS RETURN

DAILY RETURN
(Drilling) 2 OF 1

GDC

Date 1/2/12 Working Day No. 2

Contract Name PHOENIX 1000

Contract No. SC10

Dayworks Were Executed Today

Daywork No.

Hole No.	Depth	Casing	Dia	Angle	From	To	Description
9	21.00	2.00	100mm	V	0.00	1.00	FILL
					1.00	2.00	CLAY
					2.00	6.90	SANDSTONE
					6.90	7.30	DARK MUDSTONE
					7.30	16.50	SANDSTONE
					16.50	16.90	COAL
					16.90	18.50	SANDSTONE
					18.50	19.40	COAL
					19.40	21.00	SANDSTONE
							FLUSH FILLED THROUGHOUT.
10	21.00	2.00	100mm	V	0.00	0.60	FILL
					0.60	2.00	CLAY
					2.00	18.40	SANDSTONE
					18.40	19.70	COAL
					19.70	21.00	SANDSTONE.
							FLUSH FILLED THROUGHOUT.
	ALL BOREHOLES TESTED FOR GAS, NO GAS RECORDED						ALL BH. BACKFILLED WITH ARISINGS WITH A CEMENT/ BENTONITE TRAP AT SURFACE.
	MATERIALS USED		CPC (25kg) - 9 BAGS				BH NO.7 NO DRILLING DUE TO
			BENTONITE (25kg) - 2 BAGS				SUSPECTED GAS MAIN

2	42.00	4.00	SHEET TOTAL	CREW	PLANT
7	147.60	15.40	PREVIOUS SHEET TOTAL	D. ENVIRONS	C6 (c/w Pump)
9	189.60	19.40	CUMULATIVE TOTAL	A. HOWELLS	2" PUMP
					UW VAN

Signed by G.D.C. Date 1-2-12

Signed by CLIENT Date

CLIENT COPY - WHITE
Q.S. COPY - YELLOW
SITE COPY - PINK

NO CLAIM CAN BE ACCEPTED UNLESS REPORTED IN WRITING WITHIN 14 DAYS OF THIS RETURN

DAILY RETURN
(Drilling)

GDC 1 OF 1

Date 1/12/12 Working Day No. 3

Contract Name PHOENIX INN

Contract No. 5C10

Dayworks Were Executed Today

Daywork No.

Hole No.	Depth	Casing	Dia	Angle	From	To	Description
							ALL WORK COMPLETED TO
							CONTRACT AND CLIENT
							SATISFACTION.
							DEMOBILISED CAIRAGOR C6,
							WATER PUMP, CREW,
							AUXILIARY PLANT AND
							EQUIPMENT.


				CREW	PLANT
			SHEET TOTAL	D. EDWARDS	C6 (c/w PUMP)
			PREVIOUS SHEET TOTAL	A HALFORD	2" PUMP
9	189.60	19.40	CUMULATIVE TOTAL		VW VAN

Signed by G.D.C. [signature] Date 1-2-12

Signed by CLIENT Date

CLIENT COPY - WHITE
Q.S. COPY - YELLOW
SITE COPY - PINK

NO CLAIM CAN BE ACCEPTED UNLESS REPORTED IN WRITING WITHIN 14 DAYS OF THIS RETURN

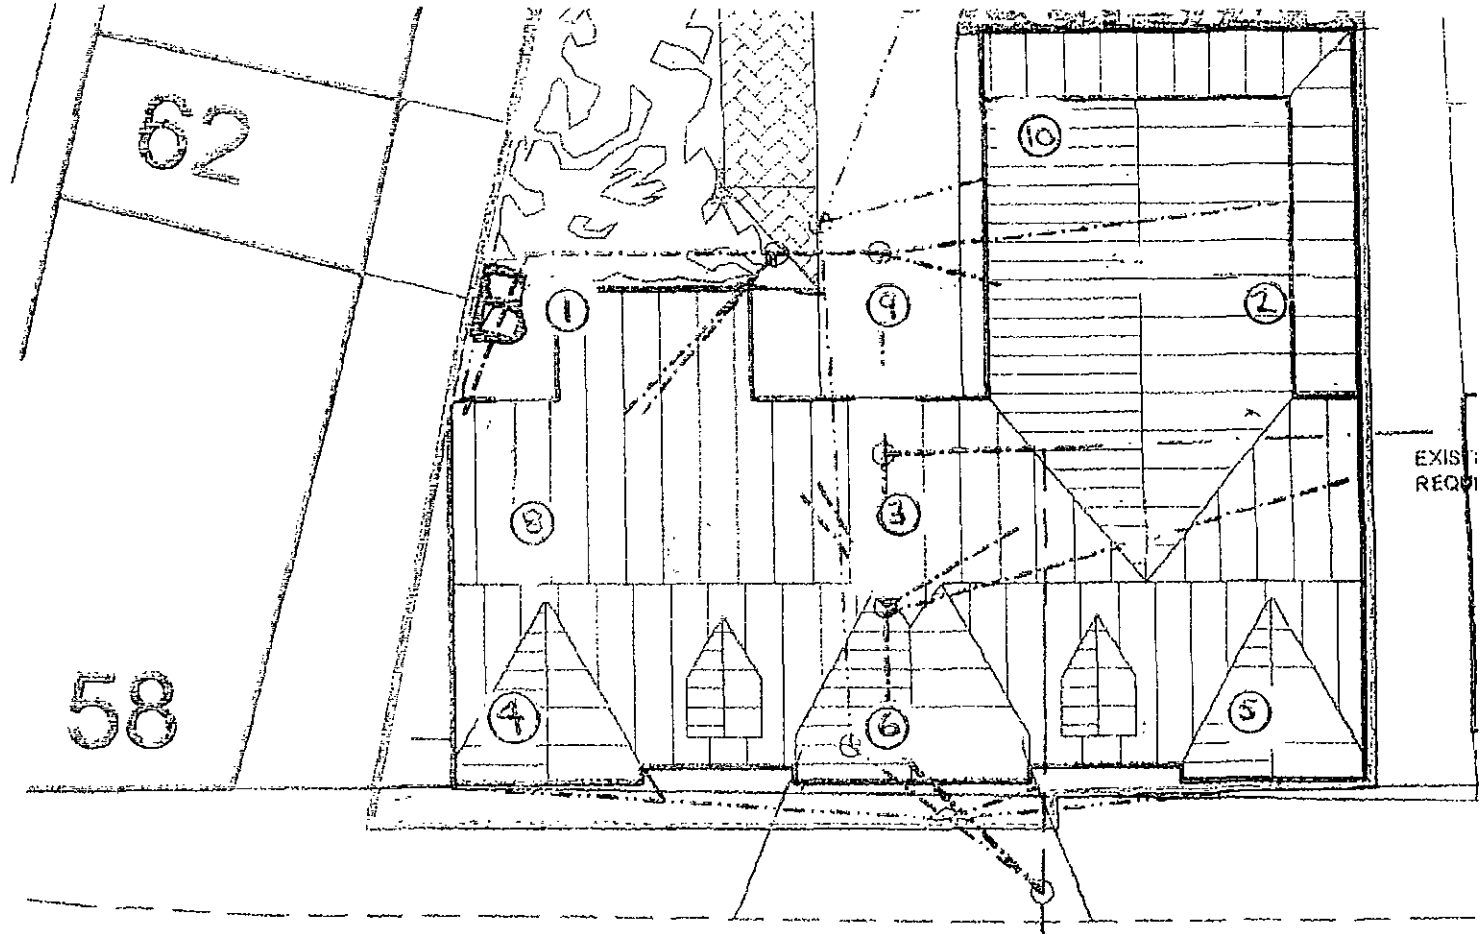

BARUGH GREEN ROAD

APPROX LINE OF EXISITNG COMB
TAKEN FROM YWA SEWER RECOF

SITE PLAN
