
Percolation Tests - Land Adjacent Glebe Farm – Feb 2019

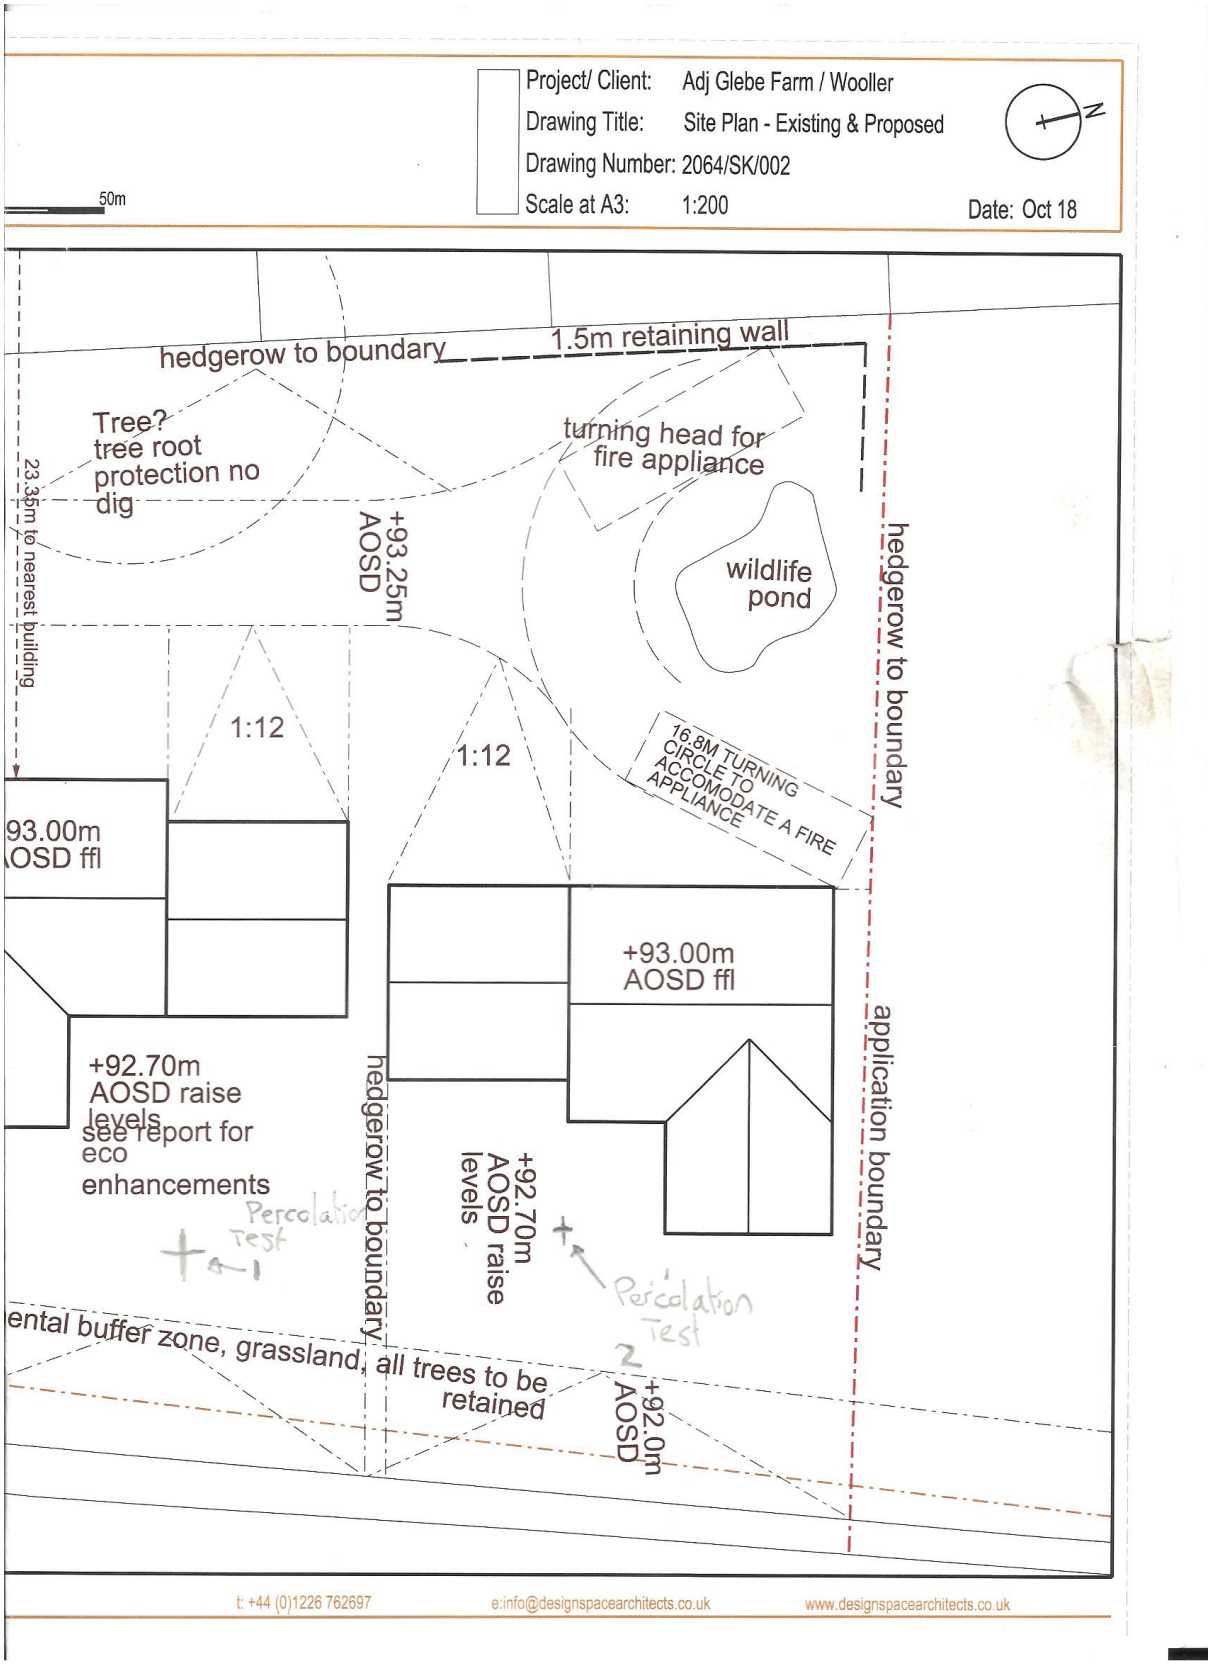

Hallroyd Homes

Barnsley Road, Silkstone
Percolation Tests

Percolation test 1

Dig hole 1.2m x 0.6m x 1.2m deep
Fill hole with approx 425 litre of water

Thursday 7th February 2019

10.15	water level	500 mm deep
10.45	water level	425 mm deep
11.15	water level	380 mm deep
11.45	water level	350 mm deep
12.48	water level	330 mm deep
13.42	water level	310 mm deep
15.47	water level	260 mm deep
16.40	water level	240 mm deep

Friday 8th February 2019

8.00 All Water drained away

Hallroyd Homes

Barnsley Road, Silkstone
Percolation Tests

Percolation test 2

Dig hole 1.2m x 0.6m x 1.2m deep
Fill hole with approx 425 litre of water

Monday 11th February 2019

8.10	water level	520 mm deep
8.55	water level	440 mm deep
10.15	water level	360 mm deep
11.20	water level	300 mm deep
12.30	water level	260 mm deep
13.50	water level	220 mm deep
15.55	water level	160 mm deep
16.45	water level	130 mm deep
