
Barnsley MBC 'Better Barnsley Town Centre Demolition Programme'

ID	Task Name	Duration	Start	Finish
1	Order Received	1 day	Mon 13/04/15	Mon 13/04/15
2	**Demolition Phasing Strategy by Phase# and SK00#**	**544 days**	**Tue 14/04/15**	**Fri 12/05/17**
3	**SK001 Demolition Phase 1. Site Establishment start May 2015. Numbered reference relates to Contract Sum Analysis**	**39 days**	**Tue 14/04/15**	**Fri 05/06/15**
4	Section 80 application	1 day	Tue 14/04/15	Tue 14/04/15
5	Network Rail approvals	0 days	Fri 22/05/15	Fri 22/05/15
6	Issue RAMS	1 day	Mon 20/04/15	Mon 20/04/15
7	Approve RAMS	1 day	Mon 27/04/15	Mon 27/04/15
8	4.09 to 4.16 Enabling works / temporary works / services	10 days	Mon 20/04/15	Fri 01/05/15
9	Erect Heras temporary fencing	4 days	Tue 05/05/15	Fri 08/05/15
10	4.01 Establish permanent hoarding	9 days	Tue 05/05/15	Fri 15/05/15
11	Establish welfare, drying room and site offices	3 days	Mon 11/05/15	Wed 13/05/15
12	4.02 Site clearance	5 days	Mon 11/05/15	Fri 15/05/15
13	4.03 Protect existing sub station at Western edge of compound	5 days	Mon 11/05/15	Fri 15/05/15
14	4.06 Break up existing Zero Ice ground slab DATE TO BE CONFIRMED	0 days	Tue 05/05/15	Tue 05/05/15
15	4.07 Requirement for vehicle containment along boundary with adjacent network rail land	3 days	Mon 11/05/15	Wed 13/05/15
16	Remove street furniture back to store	3 days	Mon 11/05/15	Wed 13/05/15
17	4.08 Construct temporary retaining wall on boundary of network rail land to allow the construction of temporary access road and ramp	10 days	Mon 18/05/15	Fri 29/05/15
18	4.04 Soft strip Zero Ice building	5 days	Mon 18/05/15	Fri 22/05/15
19	4.05 Demolish Zero Ice Building down to top of slab	10 days	Mon 25/05/15	Fri 05/06/15
20	**SK002a Demolition Phase 2a. Access Ramp - East start June 2015 - July 2015. Numbered reference relates to Contract Sum Analysis**	**50 days**	**Mon 11/05/15**	**Fri 17/07/15**
21	Issue RAMS	1 day	Mon 11/05/15	Mon 11/05/15
22	Approve RAMS	1 day	Mon 18/05/15	Mon 18/05/15
23	5.07 to 5.14 Enabling works / temporary works / services	10 days	Mon 25/05/15	Fri 05/06/15
24	5.01 Establish hoarding	5 days	Mon 08/06/15	Fri 12/06/15
25	5.02 Site clearance	1 day	Mon 15/06/15	Mon 15/06/15
26	5.04 Vehicle restraint system between compound and multi storey car park	10 days	Mon 15/06/15	Fri 26/06/15
27	5.05 Install permanent edge protection and vehicle restraint barrier system	10 days	Mon 15/06/15	Fri 26/06/15
28	5.07 Install structural restraint to Multi Storey car park elevation	10 days	Mon 15/06/15	Fri 26/06/15
29	Remove street furnitue back to store	3 days	Mon 15/06/15	Wed 17/06/15
30	5.03 Demolish ramp at two levels	15 days	Mon 29/06/15	Fri 17/07/15
31	**SK002b Demolition Phase 2b. Access Ramp - North start June 2015 - July 2015. Numbered reference relates to Contract Sum Analysis**	**70 days**	**Mon 11/05/15**	**Fri 14/08/15**
32	Issue RAMS	1 day	Mon 11/05/15	Mon 11/05/15
33	Approve RAMS	1 day	Mon 18/05/15	Mon 18/05/15
34	6.06 to 6.13 Enabling works / temporary works / services	10 days	Mon 29/06/15	Fri 10/07/15
35	6.01 Establish hoarding	5 days	Mon 13/07/15	Fri 17/07/15
36	6.02 Site clearance	1 day	Mon 20/07/15	Mon 20/07/15
37	6.04 Install permanent edge protection.	10 days	Mon 20/07/15	Fri 31/07/15
38	6.03 Demolish ramp.	10 days	Mon 03/08/15	Fri 14/08/15
39	6.05 Complete ramp into compound	10 days	Mon 20/07/15	Fri 31/07/15
40	**SK003 Demolition Phase 3. Kendray Street Bridge start July 2015. Numbered reference relates to Contract Sum Analysis**	**49 days**	**Mon 01/06/15**	**Thu 06/08/15**
41	Road closure application	0 days	Mon 01/06/15	Mon 01/06/15
42	Issue RAMS	1 day	Mon 22/06/15	Mon 22/06/15
43	Approve RAMS	1 day	Mon 29/06/15	Mon 29/06/15
44	7.07 to 7.14 Enabling works / temporary works / services	10 days	Mon 13/07/15	Fri 24/07/15
45	7.01 Establish hoarding	3 days	Mon 27/07/15	Wed 29/07/15
46	7.02 Install safety barriers at each end of link bridge	3 days	Thu 30/07/15	Mon 03/08/15
47	7.03 Prevent access TEC building at bottom of ramp Eldon Street	10 days	Fri 24/07/15	Thu 06/08/15
48	7.04 Prevent access to Central Offices via Market Parade footbrige	10 days	Fri 24/07/15	Thu 06/08/15
49	7.05 Site clearance	1 day	Mon 27/07/15	Mon 27/07/15
50	7.06 Demolish Kendray Street link bridge	3 days	Tue 04/08/15	Thu 06/08/15
51	**SK004 Demolition Phase 4. Market Parade Footbridge July 2015. Numbered reference relates to Contract Sum Analysis**	**50 days**	**Mon 15/06/15**	**Fri 21/08/15**
52	Issue RAMS	1 day	Mon 15/06/15	Mon 15/06/15
53	Approve RAMS	1 day	Mon 22/06/15	Mon 22/06/15
54	8.06 to 8.13 Enabling works / temporary works / services	10 days	Mon 13/07/15	Fri 24/07/15
55	8.01 Establish hoarding	15 days	Mon 27/07/15	Fri 14/08/15
56	Maintain Emergency vehicle access 'MAY DAY GREEN'	20 days	Mon 27/07/15	Fri 21/08/15
57	Maintain access fire escape	20 days	Mon 27/07/15	Fri 21/08/15
58	8.02 Install safety barriers at Market end of footbridge link	3 days	Mon 17/08/15	Wed 19/08/15
59	8.03 Allow acces for Semi open market customers including lighting	20 days	Mon 27/07/15	Fri 21/08/15
60	8.04 Clear site	1 day	Mon 17/08/15	Mon 17/08/15
61	8.05 Demolish footbridge	5 days	Mon 17/08/15	Fri 21/08/15
62	**SK005 Demolition Phase 5. Central offices - Main Block. August to November 2015. Numbered reference relates to Contract Sum Analysis**	**130 days**	**Mon 22/06/15**	**Fri 18/12/15**

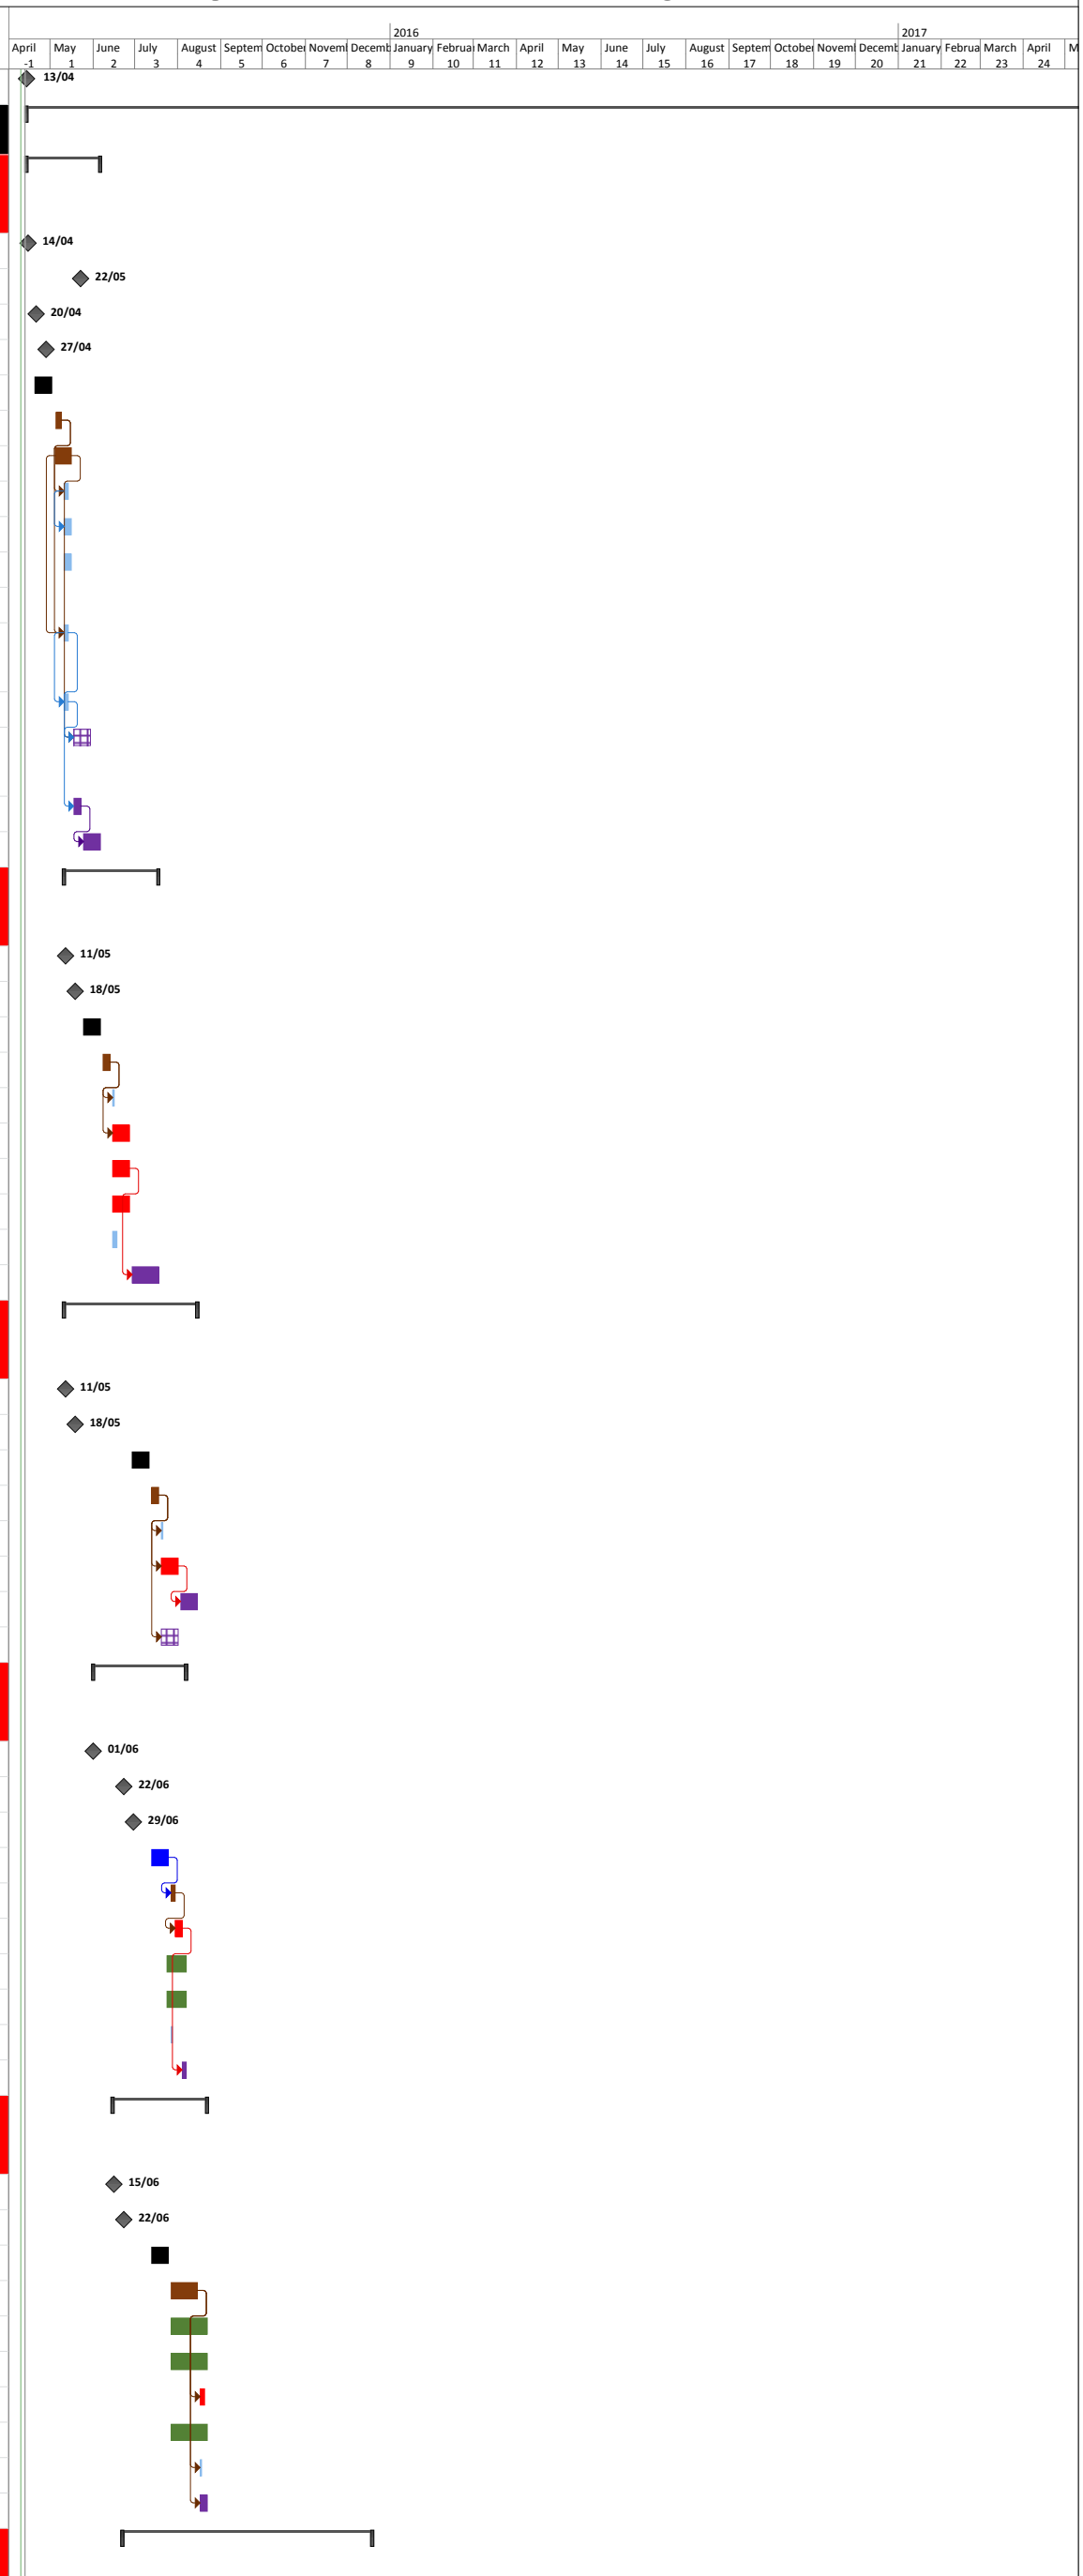


Project: mpro2017
Date: Fri 10/04/15

Task | Split | Milestone | Summary | Project Summary | External Tasks | External Milestone | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | Deadline | Progress | Manual Progress

Barnsley MBC 'Better Barnsley Town Centre Demolition Programme'

ID	Task Name	Duration	Start	Finish
63	Road closure application	0 days	Mon 22/06/15	Mon 22/06/15
64	Issue RAMS	1 day	Mon 13/07/15	Mon 13/07/15
65	Approve RAMS	5 days	Tue 14/07/15	Mon 20/07/15
66	9.06 to 9.13 Enabling works / temporary works / services	20 days	Mon 20/07/15	Fri 14/08/15
67	Maintain Emergency vehicle access 'MAY DAY GREEN'	89 days	Tue 18/08/15	Fri 18/12/15
68	Maintain access fire escape	89 days	Tue 18/08/15	Fri 18/12/15
69	9.02 Allow acces for Semi open market customers including lighting	89 days	Tue 18/08/15	Fri 18/12/15
70	9.03 Clear site	3 days	Mon 17/08/15	Wed 19/08/15
71	9.04 Soft strip including scaffolding	30 days	Mon 17/08/15	Fri 25/09/15
72	Install scaffold	30 days	Mon 17/08/15	Fri 25/09/15
73	9.05 Demolish central offices main block	59 days	Tue 29/09/15	Fri 18/12/15
74	Remove street furnitue back to store	3 days	Mon 17/08/15	Wed 19/08/15
75	Ensure access to the compound and the undercroft is closed throughout all phases	90 days	Mon 17/08/15	Fri 18/12/15
76	**SK006 Demolition Phase 6. Access Ramp - South - Start February 2016 - March 2016. Numbered reference relates to Contract Sum Analysis**	**60 days**	**Mon 14/12/15**	**Fri 04/03/16**
77	Issue RAMS	1 day	Mon 14/12/15	Mon 14/12/15
78	Approve RAMS	5 days	Tue 15/12/15	Mon 21/12/15
79	10.07 to 10.14 Enabling works / temporary works / services	10 days	Mon 18/01/16	Fri 29/01/16
80	10.01 Establish hoarding	15 days	Mon 01/02/16	Fri 19/02/16
81	10.02 Maintain access to Markets for customers	25 days	Mon 01/02/16	Fri 04/03/16
82	10.03 Prevent egress from undercroft service area	25 days	Mon 01/02/16	Fri 04/03/16
83	10.04 Prevent access from market hall	25 days	Mon 01/02/16	Fri 04/03/16
84	10.05 Site clearance	3 days	Mon 22/02/16	Wed 24/02/16
85	10.06 Demolish ramp first floor only	10 days	Mon 22/02/16	Fri 04/03/16
86	Remove street furniture back to store	3 days	Mon 22/02/16	Wed 24/02/16
87	Maintain access to the undercroft	25 days	Mon 01/02/16	Fri 04/03/16
88	Maintain access for fire escape	25 days	Mon 01/02/16	Fri 04/03/16
89	**SK007 Demolition Phase 7. Multi Storey Car Park. Start March 2016 - July 2016. Numbered reference relates to Contract Sum Analysis**	**135 days**	**Mon 18/01/16**	**Fri 22/07/16**
90	Issue RAMS	1 day	Mon 18/01/16	Mon 18/01/16
91	Approve RAMS	5 days	Tue 19/01/16	Mon 25/01/16
92	11.08 to 11.15 Enabling works / temporary works / services	15 days	Mon 07/03/16	Fri 25/03/16
93	11.02 Maintain access to Markets for customers	80 days	Mon 04/04/16	Fri 22/07/16
94	11.03 Prevent egress from undercroft service area	80 days	Mon 04/04/16	Fri 22/07/16
95	11.04 Prevent access from market hall	80 days	Mon 04/04/16	Fri 22/07/16
96	11.05 Site clearance	5 days	Mon 04/04/16	Fri 08/04/16
97	Prevent egress from undercroft service area	80 days	Mon 04/04/16	Fri 22/07/16
98	Prevent access from market hall	80 days	Mon 04/04/16	Fri 22/07/16
99	11.06 Demolish Multi Storey Car Park	60 days	Mon 04/04/16	Fri 24/06/16
100	11.07 Demolish concrete chimney and stair core	20 days	Mon 27/06/16	Fri 22/07/16
101	Maintain access to the undercroft	80 days	Mon 04/04/16	Fri 22/07/16
102	Maintain access for fire escape	80 days	Mon 04/04/16	Fri 22/07/16
103	**SK008 Demolition Phase 8. Market Offices. Start July 2016 to August 2016. Numbered reference relates to Contract Sum Analysis**	**105 days**	**Mon 16/05/16**	**Fri 07/10/16**
104	Application for road closure	1 day	Mon 16/05/16	Mon 16/05/16
105	Issue RAMS	1 day	Mon 16/05/16	Mon 16/05/16
106	Approve RAMS	5 days	Tue 17/05/16	Mon 23/05/16
107	12.07 to 12.14 Enabling works / temporary works / services	15 days	Mon 11/07/16	Fri 29/07/16
108	12.01 Establish hoarding	5 days	Mon 01/08/16	Fri 05/08/16
109	12.02 Provide temporary escape stairs and ramp	50 days	Mon 01/08/16	Fri 07/10/16
110	12.03 Prevent access from market hall	50 days	Mon 01/08/16	Fri 07/10/16
111	12.04 Site clearance	5 days	Mon 08/08/16	Fri 12/08/16
112	12.05 Decommission lift shafts	5 days	Mon 15/08/16	Fri 19/08/16
113	12.06 Demolish stair/lift core above first level only	10 days	Mon 22/08/16	Fri 02/09/16
114	12.06 Demolish Centre Offices down to street level	25 days	Mon 05/09/16	Fri 07/10/16
115	Prevent access to ALL levels during demolition	45 days	Mon 08/08/16	Fri 07/10/16
116	**SK009 Demolition Phase 9. TEC Building. February 2017. Numbered reference relates to Contract Sum Analysis**	**110 days**	**Mon 12/12/16**	**Fri 12/05/17**
117	Application for road closure	0 days	Mon 19/12/16	Mon 19/12/16
118	Issue RAMS	1 day	Mon 12/12/16	Mon 12/12/16
119	Approve RAMS	5 days	Tue 13/12/16	Mon 19/12/16
120	12.07 to 12.14 Enabling works / temporary works / services	15 days	Mon 09/01/17	Fri 27/01/17
121	13.01 Establish permanent hoarding	10 days	Mon 30/01/17	Fri 10/02/17
122	13.02 Maintain escape route from adjacent property	60 days	Mon 30/01/17	Fri 21/04/17
123	13.03 Site clearance	3 days	Wed 15/02/17	Fri 17/02/17
124	13.04 Protect existing sub station structure	5 days	Mon 13/02/17	Fri 17/02/17
125	13.07 Permanent edge protection required	10 days	Mon 13/02/17	Fri 24/02/17
126	13.05 Soft strip	15 days	Mon 27/02/17	Fri 17/03/17
127	13.06 Demolish TEC building	30 days	Mon 03/04/17	Fri 12/05/17

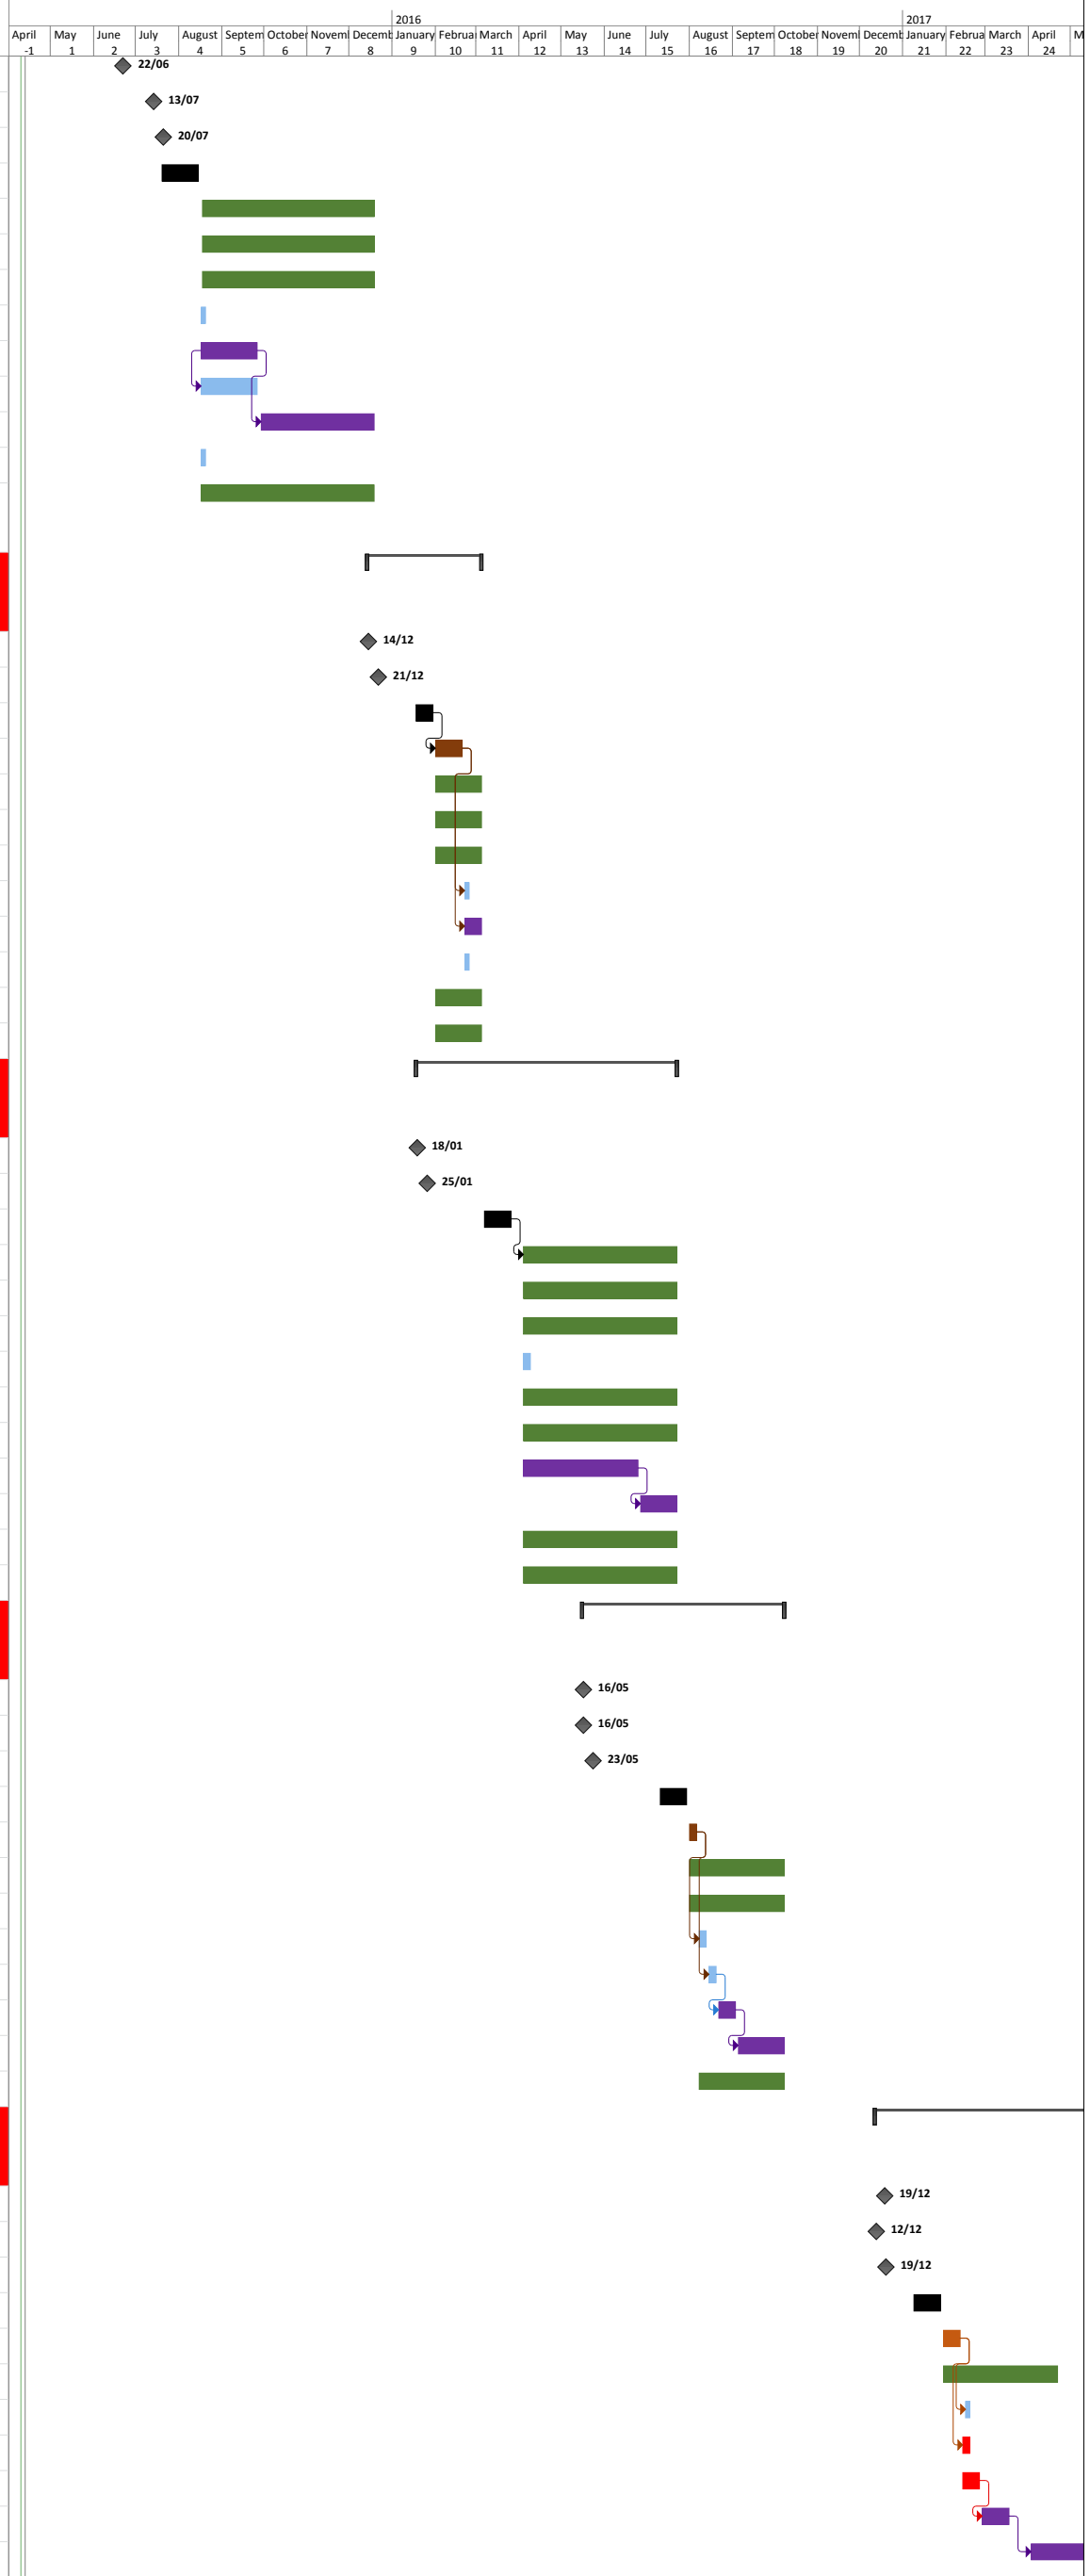

Project: mpr2014
Date: Fri 10/04/15

Task | Split | Milestone | Summary | Project Summary | External Tasks | External Milestone | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | Deadline | Progress | Manual Progress
