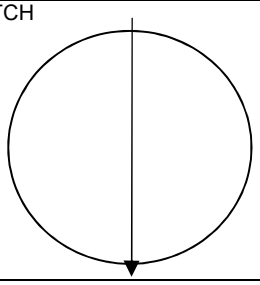
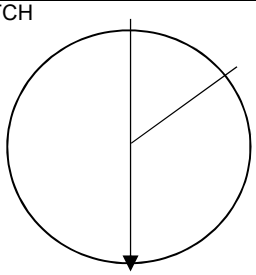
JET AIRE DRAIN CARE
GREAT NORTH ROAD
ABERFORD, LEEDS LS25 3AU
Tel: 0113 393 5500, Fax: 0113 281 4910

SITE: MILLFIELD PRIMARY SCHOOL	DATE: 06/09/2016
	JOB NO: 49151

MH NAME	FUNCTION		COVER		SKETCH
MH 1	SURFACE	√	SQUARE		
	FOUL		TRIANGLE		
PIPE MATERIAL VC	COMBINED		RECTANGLE	√	
	TRADE EFFLUENT		CIRCULAR		
COVER SIZE (mm):	690 x 540				
DEPTH (m):	0.775				
PIPE SIZE(mm):	INLET 100 Ø		OUTLET 100 Ø		
NO. OF STEPS:	0				
LANDINGS:	0				

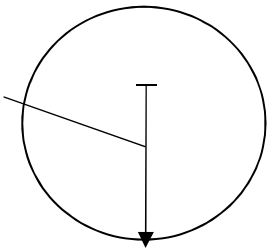
MANHOLE CHAMBER SIZE (mm):	600 x 450

MANHOLE CHAMBER SHAPE		MANHOLE CHAMBER CONSTRUCTION		COMMENTS
SQUARE		BRICK	√	
RECTANGLE	√	CONCRETE		
CIRCULAR		PLASTIC		
OTHER		OTHER		

MH NAME	FUNCTION		COVER		SKETCH
MH 2	SURFACE	√	SQUARE		
	FOUL		TRIANGLE		
PIPE MATERIAL VC	COMBINED		RECTANGLE	√	
	TRADE EFFLUENT		CIRCULAR		
COVER SIZE (mm):	680 x 520				
DEPTH (m):	1.275				
PIPE SIZE(mm):	INLET 100 Ø		OUTLET 100 Ø		
NO. OF STEPS:	0				
LANDINGS:	0				

MANHOLE CHAMBER SIZE (mm):	600 x 450

MANHOLE CHAMBER SHAPE		MANHOLE CHAMBER CONSTRUCTION		COMMENTS
SQUARE		BRICK	√	
RECTANGLE	√	CONCRETE		
CIRCULAR		PLASTIC		
OTHER		OTHER		

MH NAME	FUNCTION		COVER		SKETCH
MH 3	SURFACE		SQUARE		
	FOUL	√	TRIANGLE		
PIPE MATERIAL VC	COMBINED		RECTANGLE		
	TRADE EFFLUENT		CIRCULAR	√	
COVER SIZE (mm):	500				
DEPTH (m):	0.775				
PIPE SIZE(mm):	INLET 150 Ø		OUTLET 150 Ø		
NO. OF STEPS:	0				
LANDINGS:	0				

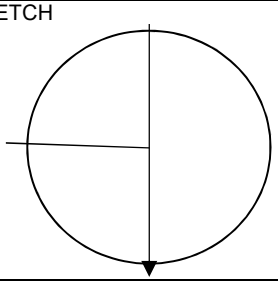
MANHOLE CHAMBER SIZE (mm):	500

MANHOLE CHAMBER SHAPE		MANHOLE CHAMBER CONSTRUCTION		COMMENTS
SQUARE		BRICK		
RECTANGLE		CONCRETE		
CIRCULAR	√	PLASTIC	√	
OTHER		OTHER		

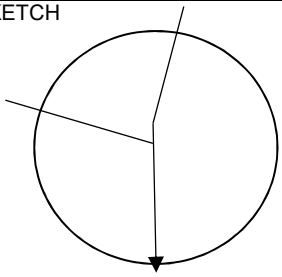
Our assessment of the drainage system is based upon our visual inspection and on information collated at the time of the survey. Where assumptions have been made these are based upon our experience and do not constitute any form of guarantee, nor do we guarantee that further deterioration will not occur following this survey. The CCTV CD/DVD will be forwarded with the report.

JET AIRE DRAIN CARE

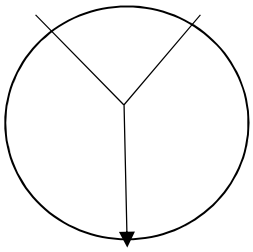
JET AIRE DRAIN CARE
GREAT NORTH ROAD
ABERFORD, LEEDS LS25 3AU
Tel: 0113 393 5500, Fax: 0113 281 4910

SITE: MILLFIELD PRIMARY SCHOOL						DATE: 06/09/2016 JOB NO: 49151
MH NAME	FUNCTION			COVER		SKETCH
MH 4	SURFACE			SQUARE		
	FOUL	√		TRIANGLE		
PIPE MATERIAL VC	COMBINED			RECTANGLE		
	TRADE EFFLUENT			CIRCULAR	√	
COVER SIZE (mm):	500					
DEPTH (m):	1.000					
PIPE SIZE(mm):	INLET 150 Ø		OUTLET 150 Ø			
NO. OF STEPS:	0					
LANDINGS:	0					
MANHOLE CHAMBER SIZE (mm):	500					

MANHOLE CHAMBER SHAPE		MANHOLE CHAMBER CONSTRUCTION		COMMENTS
SQUARE		BRICK		
RECTANGLE		CONCRETE		
CIRCULAR	√	PLASTIC	√	
OTHER		OTHER		

MH NAME	FUNCTION			COVER		SKETCH
MH 5	SURFACE			SQUARE		
	FOUL	√		TRIANGLE		
PIPE MATERIAL VC	COMBINED			RECTANGLE	√	
	TRADE EFFLUENT			CIRCULAR		
COVER SIZE (mm):	660 x 520					
DEPTH (m):	1.575					
PIPE SIZE(mm):	INLET 150 Ø		OUTLET 150 Ø			
NO. OF STEPS:	3					
LANDINGS:	0					
MANHOLE CHAMBER SIZE (mm):	1100 x 800					

MANHOLE CHAMBER SHAPE		MANHOLE CHAMBER CONSTRUCTION		COMMENTS
SQUARE		BRICK	√	
RECTANGLE	√	CONCRETE		
CIRCULAR		PLASTIC		
OTHER		OTHER		

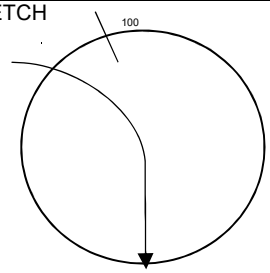
MH NAME	FUNCTION			COVER		SKETCH
MH 6	SURFACE			SQUARE	√	
	FOUL	√		TRIANGLE		
PIPE MATERIAL VC	COMBINED			RECTANGLE		
	TRADE EFFLUENT			CIRCULAR		
COVER SIZE (mm):	660 x 660					
DEPTH (m):	1.800					
PIPE SIZE(mm):	INLET 150 Ø		OUTLET 150 Ø			
NO. OF STEPS:	3					
LANDINGS:	0					
MANHOLE CHAMBER SIZE (mm):	1100 x 800					

MANHOLE CHAMBER SHAPE		MANHOLE CHAMBER CONSTRUCTION		COMMENTS
SQUARE		BRICK	√	
RECTANGLE	√	CONCRETE		
CIRCULAR		PLASTIC		
OTHER		OTHER		

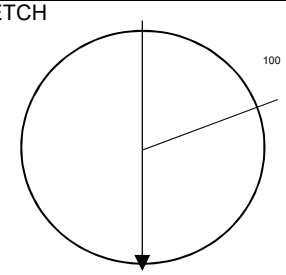
Our assessment of the drainage system is based upon our visual inspection and on information collated at the time of the survey. Where assumptions have been made these are based upon our experience and do not constitute any form of guarantee, nor do we guarantee that further deterioration will not occur following this survey. The CCTV CD/DVD will be forwarded with the report.

JET AIRE DRAIN CARE

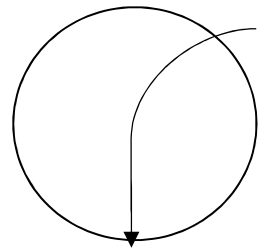
JET AIRE DRAIN CARE
GREAT NORTH ROAD
ABERFORD, LEEDS LS25 3AU
Tel: 0113 393 5500, Fax: 0113 281 4910

SITE: MILLFIELD PRIMARY SCHOOL						DATE: 06/09/2016 JOB NO: 49151
MH NAME	FUNCTION			COVER		SKETCH
MH 7	SURFACE			SQUARE		
	FOUL	√		TRIANGLE		
PIPE MATERIAL VC	COMBINED			RECTANGLE	√	
	TRADE EFFLUENT			CIRCULAR		
COVER SIZE (mm):	620 x 470					
DEPTH (m):	0.450					
PIPE SIZE(mm):	INLET 150 Ø		OUTLET 150 Ø			
NO. OF STEPS:	0					
LANDINGS:	0					

MANHOLE CHAMBER SIZE (mm):	900 x 550		
MANHOLE CHAMBER SHAPE		MANHOLE CHAMBER CONSTRUCTION		COMMENTS
SQUARE		BRICK		
RECTANGLE	√	CONCRETE	√	
CIRCULAR		PLASTIC		
OTHER		OTHER		

MH NAME	FUNCTION			COVER		SKETCH
MH 8	SURFACE			SQUARE	√	
	FOUL	√		TRIANGLE		
PIPE MATERIAL VC	COMBINED			RECTANGLE		
	TRADE EFFLUENT			CIRCULAR		
COVER SIZE (mm):	660 x 660					
DEPTH (m):	1.375					
PIPE SIZE(mm):	INLET 150 Ø		OUTLET 150 Ø			
NO. OF STEPS:	1					
LANDINGS:	0					

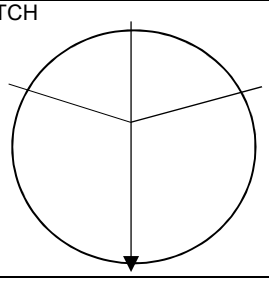
MANHOLE CHAMBER SIZE (mm):	1000 x 700		
MANHOLE CHAMBER SHAPE		MANHOLE CHAMBER CONSTRUCTION		COMMENTS
SQUARE		BRICK	√	
RECTANGLE	√	CONCRETE		
CIRCULAR		PLASTIC		
OTHER		OTHER		

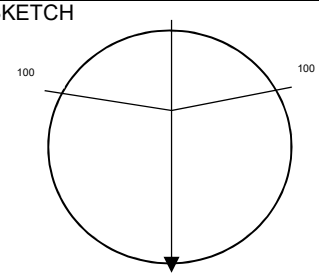
MH NAME	FUNCTION			COVER		SKETCH
MH 9	SURFACE			SQUARE		
	FOUL	√		TRIANGLE		
PIPE MATERIAL VC	COMBINED			RECTANGLE	√	
	TRADE EFFLUENT			CIRCULAR		
COVER SIZE (mm):	660 x 520					
DEPTH (m):	1.100					
PIPE SIZE(mm):	INLET 150 Ø		OUTLET 150 Ø			
NO. OF STEPS:	2					
LANDINGS:	0					

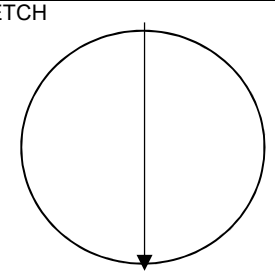
MANHOLE CHAMBER SIZE (mm):	1000 x 700		
MANHOLE CHAMBER SHAPE		MANHOLE CHAMBER CONSTRUCTION		COMMENTS
SQUARE		BRICK		
RECTANGLE		CONCRETE		
CIRCULAR	√	PLASTIC	√	
OTHER		OTHER		

Our assessment of the drainage system is based upon our visual inspection and on information collated at the time of the survey. Where assumptions have been made these are based upon our experience and do not constitute any form of guarantee, nor do we guarantee that further deterioration will not occur following this survey. The CCTV CD/DVD will be forwarded with the report.

JET AIRE DRAIN CARE
GREAT NORTH ROAD
ABERFORD, LEEDS LS25 3AU
Tel: 0113 393 5500, Fax: 0113 281 4910

SITE: MILLFIELD PRIMARY SCHOOL						DATE: 06/09/2016 JOB NO: 49151
MH NAME	FUNCTION			COVER		SKETCH
MH 10	SURFACE		√	SQUARE	√	
	FOUL			TRIANGLE		
PIPE MATERIAL VC	COMBINED			RECTANGLE		
	TRADE EFFLUENT			CIRCULAR		
COVER SIZE (mm):	490 x 490					
DEPTH (m):	1.375					
PIPE SIZE(mm):	INLET 100 Ø			OUTLET 100 Ø		
NO. OF STEPS:	0					
LANDINGS:	0					
MANHOLE CHAMBER SIZE (mm):	480					
MANHOLE CHAMBER SHAPE		MANHOLE CHAMBER CONSTRUCTION		COMMENTS		
SQUARE		BRICK				
RECTANGLE		CONCRETE				
CIRCULAR	√	PLASTIC	√			
OTHER		OTHER				

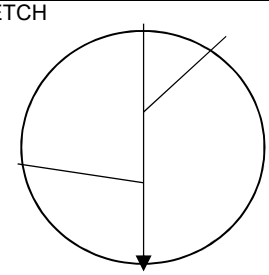
MH NAME	FUNCTION			COVER		SKETCH
MH 11	SURFACE		√	SQUARE		
	FOUL			TRIANGLE		
PIPE MATERIAL VC	COMBINED			RECTANGLE	√	
	TRADE EFFLUENT			CIRCULAR		
COVER SIZE (mm):	640 x 490					
DEPTH (m):	1.150					
PIPE SIZE(mm):	INLET 150 Ø			OUTLET 150 Ø		
NO. OF STEPS:	0					
LANDINGS:	0					
MANHOLE CHAMBER SIZE (mm):	480					
MANHOLE CHAMBER SHAPE		MANHOLE CHAMBER CONSTRUCTION		COMMENTS		
SQUARE		BRICK				
RECTANGLE		CONCRETE				
CIRCULAR	√	PLASTIC	√			
OTHER		OTHER				

MH NAME	FUNCTION			COVER		SKETCH
MH 12	SURFACE		√	SQUARE		
	FOUL			TRIANGLE		
PIPE MATERIAL VC	COMBINED			RECTANGLE	√	
	TRADE EFFLUENT			CIRCULAR		
COVER SIZE (mm):	740 x 590					
DEPTH (m):	0.700					
PIPE SIZE(mm):	INLET 150 Ø			OUTLET 150 Ø		
NO. OF STEPS:	0					
LANDINGS:	0					
MANHOLE CHAMBER SIZE (mm):						
MANHOLE CHAMBER SHAPE		MANHOLE CHAMBER CONSTRUCTION		COMMENTS		
SQUARE		BRICK				
RECTANGLE		CONCRETE				
CIRCULAR		PLASTIC				
OTHER		OTHER				

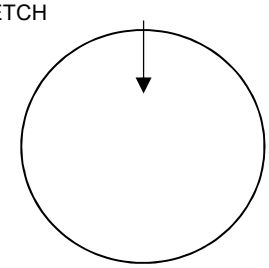
Our assessment of the drainage system is based upon our visual inspection and on information collated at the time of the survey. Where assumptions have been made these are based upon our experience and do not constitute any form of guarantee, nor do we guarantee that further deterioration will not occur following this survey. The CCTV CD/DVD will be forwarded with the report.

JET AIRE DRAIN CARE

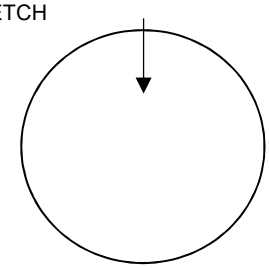
JET AIRE DRAIN CARE
GREAT NORTH ROAD
ABERFORD, LEEDS LS25 3AU
Tel: 0113 393 5500, Fax: 0113 281 4910

SITE: MILLFIELD PRIMARY SCHOOL						DATE: 06/09/2016 JOB NO: 49151
MH NAME	FUNCTION			COVER		SKETCH
MH 13	SURFACE	√		SQUARE	√	
	FOUL			TRIANGLE		
PIPE MATERIAL PVC	COMBINED			RECTANGLE		
	TRADE EFFLUENT			CIRCULAR		
COVER SIZE (mm):	510 x 510					
DEPTH (m):	0.550					
PIPE SIZE(mm):	INLET 100 Ø		OUTLET 100 Ø			
NO. OF STEPS:	0					
LANDINGS:	0					

MANHOLE CHAMBER SIZE (mm):	480			
MANHOLE CHAMBER SHAPE		MANHOLE CHAMBER CONSTRUCTION		COMMENTS
SQUARE		BRICK		
RECTANGLE		CONCRETE		
CIRCULAR	√	PLASTIC	√	
OTHER		OTHER		

MH NAME	FUNCTION			COVER		SKETCH
MH 14	SURFACE	√		SQUARE	√	
	FOUL			TRIANGLE		
PIPE MATERIAL VC	COMBINED			RECTANGLE		
	TRADE EFFLUENT			CIRCULAR		
COVER SIZE (mm):	650 x 650					
DEPTH (m):	1.500					
PIPE SIZE(mm):	INLET 100 Ø		OUTLET Ø			
NO. OF STEPS:	0					
LANDINGS:	0					

MANHOLE CHAMBER SIZE (mm):	1200 x 1200			
MANHOLE CHAMBER SHAPE		MANHOLE CHAMBER CONSTRUCTION		COMMENTS
SQUARE	√	BRICK	√	BRICKS MISSING IN CHAMBER. POSSIBLE SOAKAWAY
RECTANGLE		CONCRETE		
CIRCULAR		PLASTIC		
OTHER		OTHER		

MH NAME	FUNCTION			COVER		SKETCH
MH 15	SURFACE	√		SQUARE	√	
	FOUL			TRIANGLE		
PIPE MATERIAL	COMBINED			RECTANGLE		
	TRADE EFFLUENT			CIRCULAR		
COVER SIZE (mm):	650 x 650					
DEPTH (m):	1.300					
PIPE SIZE(mm):	INLET 100 Ø		OUTLET Ø			
NO. OF STEPS:	0					
LANDINGS:	0					

MANHOLE CHAMBER SIZE (mm):	1200 x 1200			
MANHOLE CHAMBER SHAPE		MANHOLE CHAMBER CONSTRUCTION		COMMENTS
SQUARE	√	BRICK	√	BRICKS MISSING IN CHAMBER POSSIBLE SOAKAWAY. LOTS OF ROOTS.
RECTANGLE		CONCRETE		
CIRCULAR		PLASTIC		

Our assessment of the drainage system is based upon our visual inspection and on information collated at the time of the survey. Where assumptions have been made these are based upon our experience and do not constitute any form of guarantee, nor do we guarantee that further deterioration will not occur following this survey. The CCTV CD/DVD will be forwarded with the report.

JET AIRE DRAIN CARE

JET AIRE DRAIN CARE
GREAT NORTH ROAD
ABERFORD, LEEDS LS25 3AU
Tel: 0113 393 5500, Fax: 0113 281 4910

OTHER		OTHER		

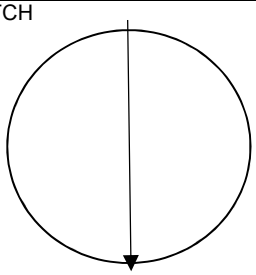
SITE:
MILLFIELD PRIMARY SCHOOL

DATE: 06/09/2016

JOB NO: 49151

MH NAME	FUNCTION		COVER	
MH 16	SURFACE		SQUARE	
	FOUL	√	TRIANGLE	
PIPE MATERIAL	COMBINED		RECTANGLE	√
VC	TRADE EFFLUENT		CIRCULAR	
COVER SIZE (mm):	620 x 470			
DEPTH (m):	0.650			
PIPE SIZE(mm):	INLET 100 Ø		OUTLET 100 Ø	
NO. OF STEPS:	0			
LANDINGS:	0			

SKETCH

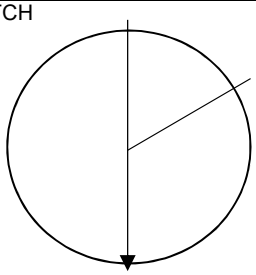


MANHOLE CHAMBER SIZE (mm): 800 x 600

MANHOLE CHAMBER SHAPE		MANHOLE CHAMBER CONSTRUCTION		COMMENTS
SQUARE		BRICK	√	
RECTANGLE	√	CONCRETE		
CIRCULAR		PLASTIC		
OTHER		OTHER		

MH NAME	FUNCTION		COVER	
MH 17	SURFACE		SQUARE	
	FOUL	√	TRIANGLE	
PIPE MATERIAL	COMBINED		RECTANGLE	√
VC	TRADE EFFLUENT		CIRCULAR	
COVER SIZE (mm):	640 x 490			
DEPTH (m):	0.950			
PIPE SIZE(mm):	INLET 100 Ø		OUTLET 100 Ø	
NO. OF STEPS:	0			
LANDINGS:	0			

SKETCH




MANHOLE CHAMBER SIZE (mm): 1100 x 700

MANHOLE CHAMBER SHAPE		MANHOLE CHAMBER CONSTRUCTION		COMMENTS
SQUARE		BRICK	√	ROOT INTRUSION IN MH
RECTANGLE	√	CONCRETE		
CIRCULAR		PLASTIC		
OTHER		OTHER		

MH NAME	FUNCTION		COVER	
	SURFACE		SQUARE	
	FOUL		TRIANGLE	
PIPE MATERIAL	COMBINED		RECTANGLE	
	TRADE EFFLUENT		CIRCULAR	
COVER SIZE (mm):				
DEPTH (m):				
PIPE SIZE(mm):	INLET Ø		OUTLET Ø	
NO. OF STEPS:				
LANDINGS:				

SKETCH



MANHOLE CHAMBER SIZE (mm):

MANHOLE CHAMBER SHAPE		MANHOLE CHAMBER CONSTRUCTION		COMMENTS
SQUARE		BRICK		
RECTANGLE		CONCRETE		

Our assessment of the drainage system is based upon our visual inspection and on information collated at the time of the survey. Where assumptions have been made these are based upon our experience and do not constitute any form of guarantee, nor do we guarantee that further deterioration will not occur following this survey. The CCTV CD/DVD will be forwarded with the report.

CIRCULAR		PLASTIC		
OTHER		OTHER		
